

ENVIRONMENTAL MANAGEMENT PROGRAMME (EMPr)

for the
management of activities relating to the protection of the natural environment during the construction- and
maintenance phases relating to the

PROPOSED DEVELOPMENT OF A 35M HIGH TELECOMMUNICATION MAST ON PORTION 22 OF FARM 22, ZOUTERIVIER, WESTERN CAPE



JUNE 2021

Compiled by: **EnviroAfrica cc**

INDEPENDENCE & CONDITIONS

EnviroAfrica is an independent consulting firm that has no interest in the proposed activity other than fair remuneration for services rendered. Remuneration for services is not linked to approval by decision-making authorities and EnviroAfrica has no interest in secondary or downstream development as a result of this project. There are no circumstances that compromise the objectivity of this EMP. The findings, results, observations, and recommendations given here are based on the author's best scientific and professional knowledge and available information. EnviroAfrica reserves the right to modify aspects of this report, including the recommendations if new information becomes available which may have a significant impact on the findings of this report.

RELEVANT QUALIFICATIONS & EXPERIENCE OF THE EAP

This EMP was compiled by Anthony Mader -

Qualifications:

Anthony Mader: BSc, BSc (Hons), Ph.D. (currently completing) at the University of the Witwatersrand, Johannesburg, South Africa.

Expertise:

Anthony has over three years of experience within environmental consulting and has worked on private and government projects throughout the country, including Western Cape, Northern Cape, KwaZulu-Natal, and the Eastern Cape. Anthony has facilitated Environmental (EA) and Water Use (WUA) applications whereas other duties included auditing of various types of construction types to ensure environmental compliance with the EA. The variety of projects Anthony has worked on include, but are not limited to;

- Housing developments;
- Civil engineering infrastructure projects such as water supply schemes, roads, culverts, bridges, warehouses, and a substation; and
- Auditing of water supply schemes, housing developments, warehouses, roads, bridges, and reservoirs

Anthony Mader joined EnviroAfrica CC in March 2020 and is employed as an Environmental Assessment Practitioner (EAP), working on various private and government projects throughout the Western Cape and Northern Cape.

Employment:

Previous employment as an Environmental : **EnviroPro Environmental Consultants**
Consultant (2017 – 2020)

Current employment as Environmental Assessment : **EnviroAfrica cc (2020 – present).**
Practitioner

The report was supervised by Bernard de Witt who has more than thirty (30) years of experience in environmental management and environmental impact assessments

Bernard: After qualifying with a B. Sc. in Forestry and a B. A. (Hons) in Public Administration at the University of Stellenbosch Bernard joined the Department of Forestry as an Indigenous Forest Planner in 1983, going on to become Manager of the Table Mountain Reserve with the Cape Town Council. He then joined Cape Nature Conservation (CNC) and headed its Conservation Planning Section before taking up the position of District Manager of the Boland area (inc. the Hottentots Holland and Kogelberg). As a Regional Ecologist, he coordinated

managerial and scientific inputs into Provincial Nature Reserves in the Boland, Overberg, and West Coast regions. For the last four years of his employment, he assessed and evaluated development applications, from an environmental perspective, on behalf of CNC (now DEA&DP). Since he left DEA&DP 10 years ago he has been involved in environmental consulting in the private sector as a member of EnviroAfrica.

TABLE OF CONTENTS

1. INTRODUCTION	1
1.1 TERMS OF REFERENCE	1
1.2 PURPOSE OF THE EMP	2
1.3 SCOPE.....	2
2. DEFINITIONS AND ABBREVIATIONS:	3
2.1 DEFINITIONS.....	3
2.2 ABBREVIATIONS	5
3. PROJECT LOCATION & DESCRIPTION	6
4. APPLICABLE LEGISLATION	10
5. SITE SPECIFIC ENVIRONMENTAL CONCERNS	11
5.1 BOTANICAL ASPECTS	11
5.2 RIVERS & WETLAND FEATURES	11
5.3 HERITAGE ASSESSMENT	11
6. RECOMMENDATIONS	12
6.1 RECOMMENDATIONS ON IMPACT MINIMISATION	12
6.1.1 Botanical	12
6.1.2 Freshwater	12
6.1.3 Heritage	<i>Error! Bookmark not defined.</i>
6.2 ENVIRONMENTAL AUTHORIZATION	13
7. CONSTRUCTION PHASE EMP	14
7.1 STRUCTURE AND RESPONSIBILITY	14
7.1.1 The client / applicant / owner	14
7.1.2 The Construction Supervisor	14
7.1.3 The contractor.....	14
7.1.4 The Environmental Control Officer (ECO).....	15
7.1.5 Health & safety officer:	16
7.2 COMMENCEMENT OF WORKS	17
7.3 ISSUES OF CONCERN	18
7.4 SITE SPECIFIC ARRANGEMENTS & CONSTRUCTION PROCEDURES	18
7.4.1 On-site start-up meeting.....	18
7.4.2 Start-up meeting participants.....	19
7.5 ENVIRONMENTAL AWARENESS TRAINING.....	19
7.5.1 Environmental awareness course	19
7.5.2 Specific training.....	19
7.6 METHOD STATEMENTS	19
7.6.1 Additional method statements	21
7.7 AUDITING PROGRAMME	21

7.8	NON-COMPLIANCE	21
7.8.1	Corrective action instruction	21
7.8.2	Written warning.....	22
7.8.3	Penalty fines.....	22
7.8.4	Stop works.....	22
7.9	CHANGES TO EMP.....	22
7.10	RECORD KEEPING	23
7.11	STANDARD MANAGEMENT PROCEDURES	23
7.11.1	Access & haul routes.....	23
7.11.2	Appropriate use of machinery	24
7.11.3	“No-Go” areas	24
7.11.4	Restriction of working areas.....	25
7.11.5	Protection of natural veld	26
7.11.6	Protection of flora.....	26
7.11.7	Protection of fauna and Avi-fauna	27
7.11.8	Clearing of vegetation, stripping & conservation of topsoil	27
7.11.9	Erosion & sedimentation control	28
7.11.10	Alien invasive management plan.....	29
7.11.11	Protection of archaeological & paleontological remains	30
7.11.12	Storage of construction material & stockpiling	31
7.11.13	Oil storage and management.....	32
7.11.14	Storing of petroleum products.....	32
7.11.15	Storing of hazardous substances	33
7.11.16	Use of cement or concrete.....	33
7.11.17	Blasting / drilling	34
7.11.18	Fire fighting	35
7.11.19	Emergency Procedures	35
7.11.20	Solid waste management	35
7.11.21	Toilets & Ablution Facilities	36
7.11.22	Discharge of construction water.....	36
7.11.23	Treating (flushing / testing) of pipelines.....	37
7.11.24	Eating facilities	37
7.11.25	Dust Control.....	37
7.11.26	Restoration and rehabilitation	38
7.11.27	Land Management	38
7.11.28	Socio-Cultural Issues	39
7.12	EMERGENCY PREPAREDNESS & RESPONCE.....	39
7.12.1	Accidental fires	39

7.12.2	Hydrocarbon spills	39
7.12.3	Concrete/cement spillages	39
8.	OPERATIONAL EMP (OEMP).....	40
8.1	TRAFFIC ACCESS ROUTES & HAUL ROADS	40
8.2	ENERGY MANAGEMENT	40
8.3	WATER MANAGEMENT	41
8.4	EROSION & SEDIMENT CONTROL	41
8.5	WASTEWATER MONITORING PROGRAM	41
8.6	WASTE & POLLUTION MANAGEMENT	42
8.6.1	Recycling	42
8.6.2	Pollution management	42
8.7	SEWERAGE MANAGEMENT	42
8.8	FIRE MANAGEMENT	42
8.9	MINIMISE DUST AND AIR EMISSIONS.....	43
8.10	MANAGEMENT OF NATURAL AREAS AND GARDENS.....	43
8.11	EMERGENCY PREPAREDNESS AND RESPONSE.....	43
8.11.1	Accidental fires	43
8.11.2	Hydrocarbon spills	43
9.	DECOMMISSIONING EMP (DEMP)	44

LIST OF APPENDIXES

- APPENDIX 1: DECLARATION OF UNDERSTANDING**
- APPENDIX 2: START-UP REPORT**
- APPENDIX 3: ENVIRONMENTAL EDUCATION**
- APPENDIX 4: BASIC RULES OF CONDUCT**
- APPENDIX 5: PENALTIES FOR NON-COMPLIANCE**
- APPENDIX 6: INFO ON METHOD STATEMENTS**
- APPENDIX 7: EXAMPLE OF METHOD STATEMENT**
- APPENDIX 8: CONTRACTOR ENVIRONMENTAL CHECKLIST**
- APPENDIX 9: ECO/ESO REPORT/CHECKLIST**
- APPENDIX 10: ENVIRONMENTAL INCIDENT REPORT FORMAT**
- APPENDIX 11: ENVIRONMENTAL COMPLAINTS REGISTER**
- APPENDIX 12: METHOD STATEMENT REGISTER**
- APPENDIX 13: MAPS & DRAWINGS**
- APPENDIX 14: SPECIALIST STUDIES**
- APPENDIX 15: PROOF OF COMPLIANCE**
- APPENDIX 16: EAP CV**

1. INTRODUCTION

The main purpose of this Environmental Management Plan or Programme (EMP) is to prevent avoidable damage and/or minimize or mitigate unavoidable environmental damage associated with any construction, maintenance, or demolition work where there is a risk of environmental damage and to enhance positive benefits of the project. The EMP forms part of the contractual obligations to which all contractors/employees involved in construction, maintenance, or demolition work must be committed. It serves as a guideline and baseline information document for the construction and operation of the proposed project and aims to comply with Section 24N of the National Environmental Management Act (Act no 107 of 1998) also known as NEMA, as well as the Environmental Impact Assessment Regulations Notice No R 982 and any additional specific information requested by any State Department, including the Department of Environmental Affairs and Development Planning (DEADP) for specific projects.

This EMP:

- identifies project activities that could cause environmental damage (risks) and provides a summary of actions required;
- identifies persons responsible for ensuring compliance with the EMP and provides their contact information;
- provides standard procedures to avoid and/or minimize the identified negative environmental impacts and to enhance the positive impact of the project on the environment;
- provides the site and project-specific rules and actions required, including a site plan/s showing:
 - areas where construction, maintenance, or demolition work may be carried out;
 - areas where any material or waste may be stored;
 - allowed access routes, parking, and turning areas for construction or construction-related vehicles;
- forms a written record of procedures, responsibilities, requirements, and rules for Contractor/s, their staff, and any other person who must comply with the EMP;
- provides a monitoring and auditing program to track and record compliance and identify and respond to any potential or actual negative environmental impacts; and
- provides a monitoring program to record any mitigation measures that are implemented;

The EMP is partly prescriptive (identifying specific people or organizations to undertake specific tasks, to ensure that impacts on the environment are minimized), but it is also an open-ended document in that information gained during the construction activities and/or monitoring of procedures on site could lead to changes in the EMP.

1.1 TERMS OF REFERENCE

EnviroAfrica (Pty) Ltd appointed by CTC Operations as the independent Environmental Assessment Practitioner (EAP) to draft the EMP. In terms of the special conditions of the contract (specifications) the EMP must include the following:

- Details of the EAP (Refer to Page ii of this document)
- Purpose of the EMP (Refer Par. 1.2)
- Legal requirements (Refer Par. 4 & 6.1)
- Management of possible impacts (Refer Par. 5-7)
- Institutional arrangements (Refer Par. 7.1)
- EMP operational & implementation procedures (Refer Par 5-9)
- Conclusion (Refer Par. 6)

- Annexures (Refer to Appendices)

1.2 PURPOSE OF THE EMP

The purpose of this Environmental Management Plan or Programme (EMP) is to give direction and guidance to all responsible parties and binds all contractors, sub-contractors, and other persons working on the site to adhere to the terms and conditions of the EMP during the construction and operational phase of the project. Any additional Site-Specific conditions decided and agreed upon during the “On-Site Start-Up Meeting” shall be included and will become a part of the EMP.

The overall aim of the EMP is to prevent avoidable damage and/or minimize or mitigate unavoidable environmental damage associated with the construction and to a lesser degree the operational, phases of the proposed project.

The EMP forms part of the contractual obligations to which all contractors/employees involved in construction, maintenance, or demolition work must be committed. It serves as a guideline and baseline information document for the construction, operational, and decommissioning phases of the proposed project and aims to comply with Section 24N of the National Environmental Management Act (Act no 107 of 1998) also known as NEMA, as well as the Environmental Impact Assessment (EIA) Regulations and any additional specific information requested by any State Department, including the Department of Environmental Affairs (DEA) for specific projects.

This EMP:

- identifies project activities that could cause environmental damage (risks) and provides a summary of actions required;
- identifies persons responsible for ensuring compliance with the EMP;
- provides standard procedures to avoid and/or minimize the identified negative environmental impacts and to enhance the positive impact of the project on the environment;
- provides the site and project-specific rules and actions required, through the start-up report;
- forms a written record of procedures, responsibilities, requirements, and rules for Contractor(s), their staff, and any other person who must comply with the EMP;
- provides for monitoring of compliance and record keeping.

The EMP is partly prescriptive (identifying specific people or organizations to undertake specific tasks, to ensure that impacts on the environment are minimized), but it is also an open-ended document in that information gained during the construction activities and/or monitoring of procedures on site could lead to changes in the EMP.

1.3 SCOPE

This EMP addresses the construction- and operational phases and all activities associated with this project. Compliance with the EMP shall be monitored by an independent Environmental Control Officer (ECO) who will visit the site regularly during the construction phase (at least twice monthly).

The Client or the Construction Engineer or Project Manager, on behalf of the Client, will be responsible to ensure the implementation of the requirements of this EMP by all contractors and sub-contractors.

2. DEFINITIONS AND ABBREVIATIONS:

2.1 DEFINITIONS

Applicant: the person or responsible person from an organization who applied for the proposed activity described in the ROD.

Audit (Site Completion): environmental evaluation (audit) of compliance of the construction phase to the conditions of the EMP.

Bund: enclosure under/around a storage facility to contain spillage.

Batch plant: a concrete or plaster mixing facility and associated equipment and materials.

Construction: means the construction period of the project during which the actual works are carried out, deemed to include site establishment, site preparation, the works, maintenance period, and decommissioning, and is defined as from the commencement of site establishment until site handover (practical completion).

Construction site: means the area influenced and affected by the construction activities or under the control of the Contractor often referred to as “the Site”.

Construction Supervisor: The person responsible (appointed by the owner) to ensure that the construction is carried out to completion on time, within budget and that the Contractor fulfills his obligations in terms of the EMP.

Contaminated water: means water contaminated by the Contractor's activities, *e.g.* concrete water and runoff from plant/ personnel wash areas.

Contractor: the principal persons/company and all other sub-contractors involved in the construction of the project.

Contractor's camp: means the designated and suitably demarcated areas on the Site within which all site offices and staff facilities are situated and within which equipment will be stored, for instance, borrow areas, batching plant, crusher plant, sand washing plant, workshop, offices, rest areas, ablution areas, etc., whichever is applicable.

Declaration of understanding: Form that is signed by all contractors involved in the construction works of their understanding and acceptance of the EMP and site-specific additions to the EMP.

Development site: boundary and extent of development works and infrastructure.

Environment: means the surroundings within which humans exist and that are made up of:

- the land, water, and atmosphere of the earth;
- micro-organisms, plant and animal life;
- any part of the combination of the above two bullets and the interrelationships between them;
- the physical, chemical, aesthetic and cultural properties and conditions of the foregoing that influence human health and well-being

Environmental Aspect: Any element of any construction activity, product, or services that can interact with the environment.

Environmental Audit Report: report done by the ECO and submitted by the Applicant to the satisfaction of the Chief Directorate Environmental Affairs, within six months after construction has been completed and also after the site(s) has been rehabilitated.

Environmental Control Officer: The ECO must be independent and suitably qualified (a diploma or degree in environmental management with at least 5 or more years of environmental site management experience) and must have a sound knowledge of the environment in which the activity will take place. The ECO should be registered as an Environmental Scientist (*in terms of section 20(3) of the Natural Scientific Professions Act, 2003 (Act 27 of 2003)*).

Environmental Completion Statement: A report by the ECO to the relevant authorities stating completion of the project and compliance with the EMP and its conditions.

Environmental Impact: Any change to the environment, whether adverse or beneficial, wholly or partially resulting from any construction activity, product, or services.

Method statement: A statement by the Contractor, describing the scope of intended construction works step-by-step, for the ECO and Construction Supervisor to understand the Contractor's intentions and be able to comment on so that they could assist with devising mitigating measures should it be necessary to avoid environmental impact.

No-Go Area(s): An area of such (environmental/aesthetical) importance that no person or activity is allowed within a designated boundary surrounding this area.

Owner: The owner, or dedicated person, responsible for the management of the property on which the proposed activity (in terms of the EA) will be performed.

Stop Works Order: An order which can be issued either by the ECO or Construction Supervisor to the Contractor (or any sub-contractor) if serious environmental damage is about to happen or is happening as a result of construction activities. On receiving such an order the Contractor must immediately stop all activities (or planned activities) relevant to the specific issue until an environmentally friendly resolution has been approved by the ECO.

Site meetings: Periodic (weekly or monthly) meetings between the ECO, Construction Supervisor, and Contractor to discuss construction activities that relate to the environment or any other environmental issues that might arise.

Works: The works to be executed in accordance with a contract.

On-site start-up meeting: a start-up meeting held on-site, before any construction has begun to discuss EMP and determine site-specific additions that will be included as the basis for the EMP.

Potentially hazardous substance: is a substance, which, in the reasonable opinion of the Engineer, can have a deleterious (detrimental) effect on the environment.

Precautionary principle: means the basic principle, that when in doubt or having insufficient or unreliable information on which to base a decision, to then undertake actions that will have minimal risk.

Reasonable: means unless the context indicates otherwise, reasonable in the opinion of the Engineer/Project Leader after he has consulted with a person, not an employee of the client, suitably experienced in "environmental implementation plans" and "environmental management plans", both as defined in the Environmental Management Act (Act No 107, 1998).

Solid waste: means all solid waste, including construction debris, chemical waste, excess cement/concrete, wrapping materials, timber, tins and cans, drums, wire, nails, food, and domestic waste (e.g. plastic packets and wrappers).

2.2 ABBREVIATIONS

CARA	Conservation of Agricultural Resources Act no. 43 of 1983
DEA	Department Environmental Affairs
EA	Environmental Authorization (Record Of Decision) issued by the relevant authority for the authorization to commence construction under certain environmental compliances
EAP	Environmental Assessment Practitioner
ECO	Environmental Control Officer - Must be a suitably qualified independent environmental consultant appointed to ensure compliance to the EMP
EIA	Environmental Impact Assessment
EMP	Environmental Management Plan or Programme
ER	Engineers representative or Main contractors representative
ESO	Environmental Site Officer -. Must be a person with adequate environmental knowledge to understand and implement the EMP by conducting onsite inspections determined by the ECO and the client.
MSDS	Material Safety Data Sheet(s)
NCNCA	Northern Cape Nature Conservation Act 9 of 2009.
NEMA	National Environmental Management Act no. 107 of 1998.
NEM: AQA	National Environmental Management: Air Quality Act 39 of 2004.
NEM: BA	National Environmental Management: Biodiversity Act 10 of 2004.
NEM: PAA	National Environmental Management: Protected Areas Act 57 of 2003
NEM: WA	National Environmental Management: Waste Act 59 of 2008.
NFA	National Forest Act 84 of 1998.
NHRA	National Heritage Resources Act 25 of 1999.
NVFFA	National Veld and Forest Fire Act 101 of 1998.
NWA	National Water Act 36 of 1998
OSSM	On-site Start-up Meeting
ROD	Record of Decision
SAHRA	South African Heritage Resources Agency

3. PROJECT LOCATION & DESCRIPTION

Project Location

The proposed project is for the development of a 35m high telecommunication mast and associated infrastructure on a disturbed site (Portion 22 of Farm 22, Zouterivier). The site is located within Ward 32 of the City of Cape Town Metropolitan, Western Cape, at the following coordinates: **33°36'22.90"S; 18°35'34.49"E**. Please refer to figure 1 below.

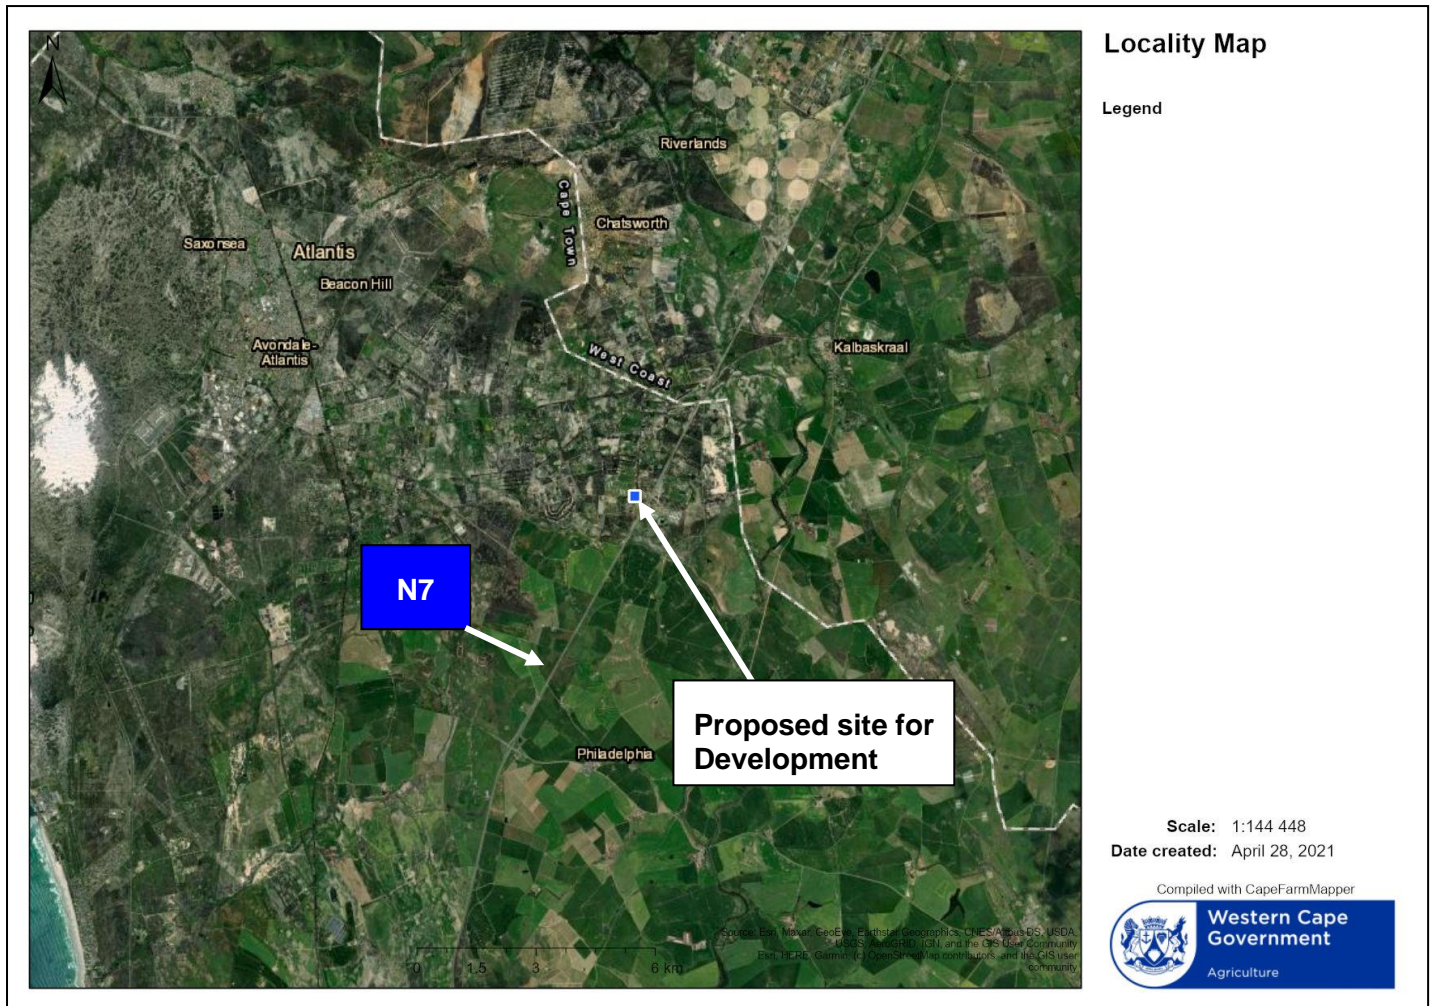


Figure 1: Location of the site for the proposed development of a 35m high telecommunication mast and associated infrastructure.

Project Description

The proposed project is for the development of a 35m high telecommunication mast and associated infrastructure on a disturbed site (Portion 22 of Farm 22, Zouterivier). The total footprint of the proposed development (35m high mast and associated infrastructure) will be approximately 90m². The site has been previously disturbed by grazing activities. The proposed development (Figure 2) will be comprised of:

- 35m High Telecommunication Mast, comprising of;
 - Standard platform;

- Proposed 1 x 300mm M/W Dish;
- Proposed antenna mounted on H-Boom;
- Navigation lights and earth lightning spike.
- Four (4) proposed equipment containers on concrete slab and plinths, including;
 - Three (3) x proposed 4.5kg DCP Fire Extinguishers per a container
- 2.4m high palisade fence;
- Low wall;
- 3m vehicle sliding gate (access); and;
- Proposed crusher stone (site surface).

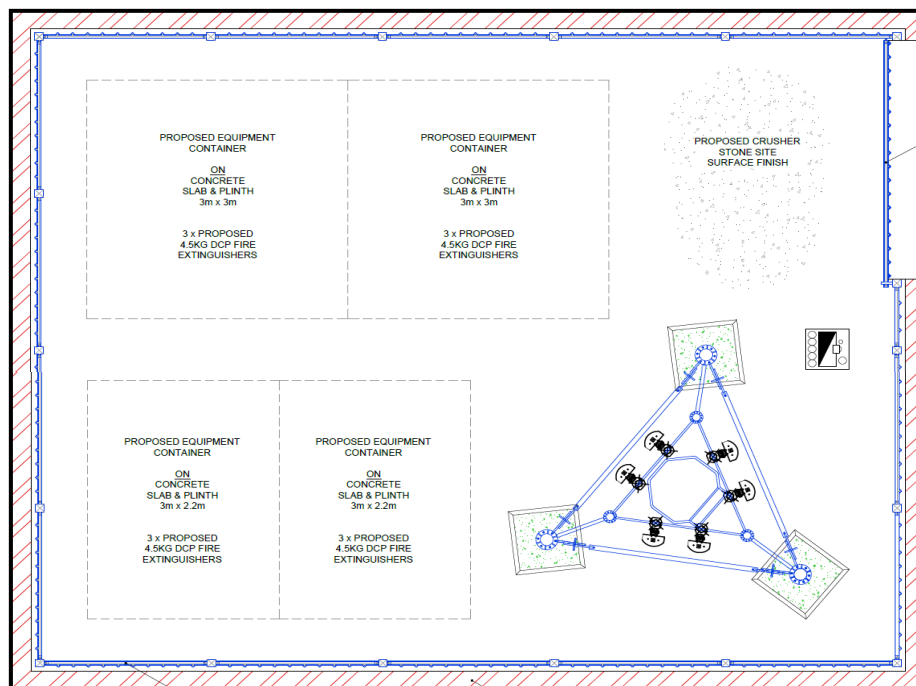


Figure 2. The layout of the proposed development of a 35m high telecommunication mast on Portion 22 of Farm 22, Zouterivier. Source: CTC Operations.

Site Description:

The proposed site for development is located on Portion 22 of Farm No. 22, Zouterivier.

The SG Digit code is: C0160000000002200022

The proposed dam centre coordinates are: 33°36'22.90"S; 18°35'34.49"E.

According to the 2018 (beta 2) update of the Vegetation map of SA (Mucina & Rutherford, 2006) the proposed site for development is located within the Atlantis Sandstone Fynbos vegetation type, classified as Endangered (EN) in terms of the “*List of ecosystems that are threatened and in need of protection*” (GN 1002, December 2011), promulgated in terms of the National Environmental Management Biodiversity Act, Act 10 of 2004. The proposed development footprint is approximately 90m² and will thus, not exceed 100m². mited plant species were observed within the proposed development footprint (Figures 2, 3, and 7). The construction and operation of the proposed development will have a negligible impact on the Plant Species Theme as no plant species of conservational value was observe within the proposed development footprint. Moreover, the (i) the high level of disturbance (due to previous grazing) associated with the site (Figure 8) and limited plant species which are disturbance indicators (namely common duwweltjie (*Tribulus terrestris*), Fynkweek (*Cynodon dactylon*), and potentially *Cephalophyllum* spp - possibly *Cephalophyllum loreum* - identified during the site visit) may characterize the sensitivity of the proposed site for development as “insignificant”. *Cynodon dactylon* is found in a wide range of edaphic and climatic conditions and has been demonstrated to rapidly grow and invade a range of soil types, enabling the species to be a tool for erosion prevention¹. This plant species is not threatened and invades disturbed areas². *Tribulus* spp have been identified as a noxious weed in many countries around the world, especially in disturbed habitats and transformed sites (e.g., sites used for agricultural practices) (Pacanoski *et al.*, 2014)³. This plant species has been reported to reduce plant biodiversity due to its high invasion / encroachment potential (Van Vleet, 2005⁴), and has been declared a weed in approximately 37 countries (Kir and Dogan, 2009)⁵. The plant’s root system (tap root with fine roots) enables this species to grow in semi- and arid-areas in loose sandy soils, outcompeting indigenous and / or desirable plant species – especially in disturbed habitats. *Cephalophyllum* spp (possibly *Cephalophyllum loreum*) is a plant species with a stable population within the Western Cape and is classified as Least Concern⁶. Therefore, no plant species of conservational value are located within the proposed site for development. Although the proposed site for development is located within the Atlantis Sandstone Fynbos vegetation type, classified as Endangered (EN) [in terms of the “*List of ecosystems that are threatened and in need of protection*” (GN 1002, December 2011), promulgated in terms of the National Environmental Management Biodiversity Act, Act 10 of 2004], the vegetation present within the proposed site for development is not characteristic of this vegetation type (as outlined in Mucina and Rutherford, 2006⁷). Furthermore, the proposed development footprint will be approximately 90m² and will thus, not exceed 100m². Furthermore, these observed plant species, indicators of disturbed sites, are established outside the proposed development footprint.

No animals were observed in, or around, the proposed site for development. The proposed site for development is disturbed due to previous grazing by livestock. Faunal diversity changes through space and time and are directly (change in land cover and disturbance of vegetation by previous grazing by livestock and edge effects) and indirectly (i.e., change in soil biogeochemistry) influenced by

¹ Shukla, S.K., Singh, K., Singh, B. and Gautam, N.N., 2011. Biomass productivity and nutrient availability of *Cynodon dactylon* (L.) Pers. growing on soils of different sodicity stress. *Biomass and Bioenergy*, 35(8), pp.3440-3447.

² Van Oudtshoorn, F. 1999. Guide to the grasses of southern Africa. Briza Publications, Pretoria.

³ Pacanoski, Z., Týr, Š. and Vereš, T., 2014. Puncturevine (*Tribulus terrestris* L.): noxious weed or powerful medical herb. *Journal of Central European Agriculture*.

⁴ Van Vleet, S.M. 2005. Invasive Weeds of Eastern Washington. Pullman: Washington State University Extension.

⁵ Kir, K., Dogan, M.N. 2009. Weed control in maize (*Zea mays* L.) with effective minimum rates of foramsulfuron. *Turk. J. for Agric.*, 33(6), 601–610.

⁶ Burgoyne, P.M. 2006. *Cephalophyllum loreum* (L.) Schwantes. National Assessment: Red List of South African Plants version 2020.1. Accessed on 2021/05/19

⁷ Mucina, L. and Rutherford, M.C., 2006. *The vegetation of South Africa, Lesotho and Swaziland*. South African National Biodiversity Institute.

anthropogenic activities (Tilman et al., 1997; Chapin et al., 2000; Didham *et al.*, 2015; McDonald *et al.*, 2020). Moreover, the previous erection of fences around the property would have physically restricted the movement of medium and larger animals in and out of the property – limiting the number and diversity of animals present within the property. Based on the site's level of disturbance, it is unlikely that the proposed site for development would adequately support vegetation characteristic of the Atlantis Sand Fynbos vegetation type, and consequently, fauna which may have naturally depended on the vegetation structure associated with this vegetation type. Furthermore, edge effects have diverse impacts on biodiversity and ecological functioning, further contributing to the disturbance of the site (Razafindratsima *et al.*, 2018). Such effects contribute to a disturbance factor, which is likely to have driven most wild animals away from the proposed site for development due to current land use activities. This in turn would have affected the food chain and ultimately the number and type of tertiary predators, particularly mammals and larger birds of prey, as well as animals on lower trophic levels. Although no animals were observed on-site during the site visit, conditions and measures will be incorporated in the EMP to mitigate any potential impact(s) of the proposed development on animal species. Due to long-term impacts associated with the disturbance of the proposed site for development, it is envisaged that the proposed development will have a negligible impact(s) on the Animal Species Theme. Based on factors highlighted above, it is envisaged that the proposed site for development has an insignificant sensitivity with regards to the Animal Species Theme.



Figure 3. Disturbed vegetation associated with the proposed site for development. Vegetation includes common duwweltjie (*Tribulus* sp.), Fynkweek (*Cynodon dactylon*), and potentially *Arctotis* sp.

Surface Water

A non-operational, artificial water attenuation feature is located within 32m of the proposed site for development, which forms part of the on-site stormwater management. The water attenuation feature is comprised of alien invasive plant species, namely *Acacia cyclops*. The proposed development will have no impact on any surface water resources.

4. APPLICABLE LEGISLATION

Constitution of the Republic of South Africa (1996): of special relevance in terms of environment is section 24

Conservation of Agricultural Resources Act 43 of 1983 (CARA): supports the conservation of natural agricultural resources (soil, water, plant biodiversity) by maintaining the production potential of the land and combating/preventing erosion; for example, by controlling or eradicating declared weeds and invader plants.

Hazardous Substances Act 15 of 1973: to control substances that may cause injury, ill-health, or death through their toxic, corrosive, irritant, strongly sensitizing, or flammable nature, or by the generation of pressure

National Environmental Management Act 107 of 1998 (as amended): replaces the Environmental Conservation Act (ECA) and establishes principles for decision-making on matters affecting the environment, and for matters connected therewith.

- **Environmental Impact Assessment Regulations:** identifying activities (listed activities) for which environmental authorization must be obtained.

National Environmental Management: Air Quality Act 39 of 2004 (NEMAQA): replaces the Atmospheric Pollution Prevention Act (No. 45 of 1965).

National Environmental Management: Biodiversity Act 10 of 2004 (NEMBA): supports the conservation of plant and animal biodiversity, including the soil and water upon which it depends.

- **National list of ecosystems that are threatened and in need of protection** (GN 1002 of 9 December 2011).

National Environmental Management: Protected Areas Act 57 of 2003 (as amended Act 31 of 2004) (NEMPAA): To provide for the protection and conservation of ecologically viable areas representative of South Africa's biological diversity and its natural landscapes and seascapes.

National Environmental Management: Waste Act 59 of 2008 (NEMWA): To reform the law regulating waste management to protect health and the environment by providing reasonable measures for the prevention of pollution and ecological degradation and for securing ecologically sustainable development.

- **List of Waste Management Activities that have, or are likely to have a detrimental effect on the environment:** Identifies activities in respect of which a waste management license is required.

National Forests Act 84 of 1998 (as amended): supports sustainable forest management and the restructuring of the forestry sector.

- **List of protected tree species** (GN 716 of 7 September 2012)

National Heritage Resources Act 25 of 1999: supports an integrated and interactive system for the management of national heritage resources, including supports soil, water, and animal and plant biodiversity.

National Veld and Forest Fire Act 101 of 1998 (NVFFA): protects soil, water, and plant life through the prevention and combating of the veld, forest, and mountain fires

National Water Act 36 of 1998 (NWA): promotes the protection, use, development, conservation, management, and control of water resources in a sustainable and equitable manner.

5. SITE-SPECIFIC ENVIRONMENTAL CONCERNS

The purpose of this section of the EMP is to discuss possible significant environmental impacts that may be encountered. In other words, this section aims to give site-specific guidance for impact minimization in the context of the proposed development.

5.1 BOTANICAL ASPECTS

According to the 2018 (beta 2) update of the Vegetation map of SA (Mucina & Rutherford, 2006) the proposed site for development is located within the Atlantis Sandstone Fynbos vegetation type, classified as Endangered (EN) in terms of the “*List of ecosystems that are threatened and in need of protection*” (GN 1002, December 2011), promulgated in terms of the National Environmental Management Biodiversity Act, Act 10 of 2004. The proposed development footprint is approximately 90m² and will thus, not exceed 100m². No plant species of conservational value are present within the proposed development footprint. Plant species present within the construction footprint is limited to disturbance indicators (namely common duwweltjie (*Tribulus* sp.), Fynkweek (*Cynadon dactylon*), and *Cephalophyllum* spp. (possibly *Cephalophyllum loreum*) (Figure 4). From the Biodiversity Overlay Maps from Cape Farm Mapper, the site does not fall within a Critical Biodiversity Area (CBA) or Ecological Support Area (ESA).



Figure 4. Plant species [A = Fynkweek (*Cynadon dactylon*); B = *Cephalophyllum* spp; C = common duwweltjie (*Tribulus* sp.)] present within the construction footprint. Note, these plant species are indicators of disturbed areas and are not of conservational significance.

5.2 RIVERS & WETLAND FEATURES

The Artificial water attenuation feature, located within 32m of the proposed site for development, is not operational and forms part of the on-site stormwater management. Moreover, the restriction of construction activities to the development footprint will not impact the functioning of the water attenuation feature. No watercourses are present within the proposed site for development.

5.3 HERITAGE

As per the NID, the anticipated impact on heritage resources will be very low. Furthermore, the heritage specialist recommended that a heritage impact assessment will not be required.

6. RECOMMENDATIONS

The following are site-specific recommendations for the proposed development of the 35m high telecommunication mast on Portion 22 of Farm No. 22, Zouterivier. Please note that if there is any contradiction between the conditions of the Environmental Authorisation, and the recommendations in Section 7 and 8 below, conditions stipulated in the Environmental Authorisation take precedent. Please also refer to the method statement attached as **Appendix 6 and 7 of this EMP** and which should be printed and used on-site with this EMP document.

6.1 RECOMMENDATIONS ON IMPACT MINIMISATION

- The construction and operational phase of the project must be done in accordance with this environmental management program, the aim of which is, to minimize environmental impact during the construction and operational phases.
- A suitable qualified ECO must be appointed to oversee the construction phase.

6.1.1 Botanical

The following mitigation measures should be implemented during the construction phase:

- A suitably qualified Environmental Control Officer must be appointed to monitor the construction phase;
- Before any work is done the site and access routes must be demarcated (with the aim at minimal width/smallest footprint);
- Lay-down areas or construction sites must be located within already disturbed areas or areas of low ecological value and must be pre-approved by the ECO (note, the proposed site for development comprises of disturbed vegetation where plant species within this footprint are not of conservational significance);
- Indiscriminate clearing of areas must be avoided;
- All areas impacted outside of the proposed construction footprint must be rehabilitated on completion of the project. Except to the extent necessary for the carrying out of the works, no flora may be removed, damaged, or disturbed;
- Alien invasive plant species encroachment must be monitored in and around the proposed development footprint. Alien invasive plants must be cleared and removed by hand (where applicable). Where the use of herbicides, pesticides, and other poisonous substances are to be used, the Contractor must submit a Method Statement;
- An integrated waste management approach (including recycling and reusing where possible) where must be implemented during construction.
- Trapping, poisoning, and/or shooting of animals is strictly forbidden.
- The Contractor may not deface, paint, damage or mark any natural features, if these should occur (e.g. trees, rock formations, buildings, etc.) situated in or around the Site for survey or other purposes unless agreed beforehand with the Engineer and the ECO. Any features affected by the Contractor in contravention of this clause must be restored/rehabilitated to the satisfaction of the Engineer and the ECO.

6.1.2 Freshwater

- The artificial water attenuation feature, located within 32m of the proposed site for development, is not operational. Due to the restriction of construction activities to the

development footprint is unlikely to impact any remaining functionality of the water attenuation feature. No watercourses are present within the proposed site for development.

- The proposed development is highly unlikely to impact the non-operational artificial, water attenuation feature.
- A suitably qualified ECO must be appointed;
- Environmental Awareness training to be conducted with all workers;
- Ensure construction activities are restricted to the demarcated footprint, strictly prohibit any vehicles or construction related activities outside of the demarcated footprint area
- No concrete/ cement will be mixed on site and surplus must be disposed of in the correct manner.
- Inspect all vehicles daily for the early detection of deterioration or leaks.
- During construction its footprint should be kept as small as possible; and
- All building rubble should be removed following the completion of the proposed development.

6.1.3 Heritage

- The heritage specialist recommended that no Heritage Impact Assessment will be required as the potential impact on any heritage resources is very low;
- Although unlikely, should any heritage resources be discovered/uncovered during the construction phase, construction activities must be immediately ceased. The ECO must be immediately notified and the relevant personnel at Heritage Western Cape (HWC) must be contacted to advise on the way forward;
- A suitably qualified ECO must be appointed;
- Environmental Awareness training to be conducted with all workers; and
- Ensure construction activities are restricted to the demarcated footprint, strictly prohibit any vehicles or construction related activities outside of the demarcated footprint area.

6.2 ENVIRONMENTAL AUTHORIZATION

Please ensure that DEADP confirms their approval of this project in writing.

7. CONSTRUCTION PHASE EMP

7.1 STRUCTURE AND RESPONSIBILITY

Implementation of the EMP and environmental control and management of the construction phase will be achieved through the responsibility structure set out below. The role players include the Owner, the Construction Supervisor, the Environmental Control Officer (ECO), and the Contractor. All role players must familiarize themselves with the prescriptions of the EMP.

7.1.1 The client / applicant / owner

The client (or the designated responsible person appointed by him) is responsible for:

- appointing a suitably experienced ECO, the Construction Supervisor and the Contractor for the duration of the construction contract, and
- ensuring that the Construction Supervisor and Contractor fulfill their obligations in terms of this EMP.

7.1.2 The Construction Supervisor

The Construction Supervisor is responsible to ensure that the construction is carried out to completion on time, within budget and that the Contractor fulfills his obligations in terms of the EMP. In addition, the Construction Supervisor and the ECO are expected to develop a close working relationship and to stay in contact with each other.

The responsibilities of the Construction Supervisor include:

- To issues site instructions to the Contractor.
- To serve as a conduit for all communication between the ECO and the Contractor [The only exception is where the ECO or the Construction Supervisor needs to issue a “**STOP WORKS**” order on the contractor if serious environmental harm is about to happen or is happening as a result of construction activity. The “**STOP WORKS**” order must be confirmed by the other party as soon as reasonably possible].
- Discussing any problems that might lead to environmental damage with the ECO.
- When the ECO is not on site the Construction Supervisor will be responsible for the implementation of the EMP.

7.1.3 The contractor

The Contractor shall be responsible to:

- ensure that all sub-contractors, employees, suppliers, agents, etc. are fully aware and adhere to the environmental conditions detailed in the EMP;
- liaise closely with the Construction Supervisor and the ECO;
- ensure that works on the site are conducted in an environmentally sensitive manner and full accordance with the EMP;
- carry out instructions issued in the site instruction book;
- assist with solutions to environmental problems that may arise during the construction phase; and
- ensure that all “**No-Go**” areas are adequately fenced off.

- will report any deviation from the requirements of this EMP to the Principal Agent, and any pollution or environmental contaminant spill events.
- agrees to work stoppage and/or payment of penalties as required by this EMP and directed by the ECO/Construction Supervisor.
- agrees to bear full costs for any work stoppage resulting from contravention of the requirements of this EMP, and/or the costs of remedying environmental damage resulting from their or their sub-contractors or employee's contravention of the requirements of this EMP.

NB: All contractors must sign the "Declaration of understanding" (page ii of this document) of this Environmental Management Plan before construction commences.

7.1.4 The Environmental Control Officer (ECO)

ECO will be responsible for overseeing the environmental aspects of the construction phase and will work in close coordination with the Construction Supervisor.

7.1.4.1 Frequency of site visits

An ECO must be appointed for the duration of the construction phase (as required by the EA). The ECO

The ECO must comply with the following:

- Conduct a start-up meeting before construction commences
- Conduct 2 site visits in the first month of construction and thereafter conduct 1 monthly site visit until construction is completed.
- Conduct a closing down visit as soon as possible after the completion of the Development (a total of 6 site visits).
- Conduct a Final Environmental Audit Report after project completion and submit the Audit Report to the Competent Authority (as specified in section 7.7 Auditing Programme, below).

7.1.4.2 ECO qualifications

The ECO must be independent and suitably qualified (a diploma or degree in environmental management with at least 5 or more years of environmental site management experience) and must have a sound knowledge of the environment in which the activity will take place.

7.1.4.3 ECO duties

An ECO must be appointed for the duration of the construction phase (as required by the EA). The ECO:

- will be primarily responsible for ensuring the implementation of the EMP and will perform regular site inspections/audits with the specific aim to ensure environmental conformance by the Contractor;
- to visit the site regularly while construction is in progress;
- will keep environmental records (including photographs) of the construction activities;
- must ensure that "No-Go" and "Open Space" areas are adequately protected and adhered to;

- must approve and be present during the demarcation of the necessary areas for storage of materials, ablutions, eating areas of contract workers, etc.;
- to conduct a start-up meeting before construction commences and will provide environmental training at the beginning of the project and will provide environmental awareness training throughout the life of the project;
- must be informed of the site and technical meetings to be able to comment and report on environmental issues;
- will call for, and approve, method statements for construction activities that might pose an environmental impact and must ensure that method statements are approved before commencement of the work;
- must implement immediate mitigating action in the case of critical environmental impacts
- must deal with public complaints/queries regarding environmental issues;
- will record his findings and all environmental non-conformances in an environmental completion report (which will be forwarded to the Client and the Construction Supervisor);
- will conduct a closing down visit ASAP after completion of the Development;
- will commission an independent Environmental Compliance Audit within 6 months after completion of the contract.

7.1.4.4 ECO Authority

The **ECO has the authority to stop works** if there is a serious threat to or impact on, the environment as a direct cause of construction. However, this authority is limited only to emergency situations where immediate consultation with the Construction Supervisor is not possible.

- The ECO is to inform the client/developer and site representative of the reasons for the stoppage as soon as possible. A relevant reason should be supplied as soon as possible after the stoppage of such works.
- Upon failure by the contractor or his employee to show adequate consideration to the environmental aspects of this contract i.e. willful destruction of the environment, the ECO may recommend to the client/developer or site representative to have the contractor's representative or any employee(s) removed from the site or work suspended until the matter is remedied.
- No extension of time will be considered in the case of such suspensions and all costs will be borne by the contractor

7.1.5 Health & safety officer:

A health & safety (H&S) officer for the project must be designated or appointed by the Contractor or Principal Agent, and his/her role is to support the successful implementation of the EMP through:

- Site evaluation regularly.
- Identifying issues relating to day-to-day construction activities and that can have a detrimental effect on the environment.
- Subcontractor audits to ensure compliance.
- Assist in the direct implementation of the EMP.
- Ensure that the requirements of the EMP are communicated understood by personnel on-site *via* induction sessions.
- Ensure that the contractors on site develop, implement and monitor the required H&S management functions.

- Evaluate the applicability and accuracy of the EMP and the method statements throughout the construction phase.
- Coordinate all statutory requirements including permit authorization and license requirements.
- Conduct or have conducted a hazard analysis and take the necessary corrective action.
- Where it is not possible to remove any remaining hazards to inform employees thereof and what precautionary action is to be taken.
- Detail mitigation measures are required to be taken, and the procedures for their implementation to the project manager.
- Representing H&S issues at the production meetings.
- Coordinate H&S training of personnel.
- Coordinating spill response personnel.
- The H&S Officer shall inspect the integrity of the hazardous waste containers/bins/skips on a weekly basis.

7.1.5.1 Health & Safety Officer qualifications

The Health and Safety Officer must be independent and suitably qualified, with a sound knowledge of the Occupational Health & Safety Act (Act no. 85 of 1993), and must have experience of the implementation of the act with regards to the construction and environmental environments in which the activity will take place.

7.2 COMMENCEMENT OF WORKS

The site project contractors must timeously receive a copy of the Construction Phase EMP (CEMP) and any other further additional information that pertains to site conditions/amendments or deviations from the original site plan.

- This EMP must be included to form part of the Contractors site specification documentation.
- A copy of the EMP must be on-site at all times and available for presentation to any authority requesting to see such a document.

NO WORK ON SITE MAY TAKE PLACE UNTIL

- The Declaration of Understanding/Environmental Contract is signed between the relevant parties.
- One week's written notice was given to the Department before the commencement of any construction activity (As per EA).
- On-Site Start-Up Meeting has been held
- Site and No-Go areas have been identified **and demarcated**.
- Contractors are in possession of the EMP and other relevant documentation
- Contractors/Subcontractors have signed the Declaration Of Understanding
- All mandatory site equipment is in place
- On-Site Environmental Education & Awareness training session has taken place with all relevant construction personnel present.

NB: Work refers to Camp Establishment, Earthmoving activities, and any pre-liminary construction activities.

7.3 ISSUES OF CONCERN

Issues of concern that were identified in the Environmental Impact Assessment process and included in the EA or detailed in the Basic Assessment Report must be addressed during the “On-Site Start-Up Meeting” and must be included in the On-Site Start-Up Report. Issues of Concern include but shall not be limited or restricted to the following:

- Waste management and disposal;
- Mandatory site equipment;
- Establishment of the construction site;
- Concrete works;
- Soil erosion & sediment control;
- Use and storing of hazardous substances; and
- Establishment of temporary laydown areas.

7.4 SITE-SPECIFIC ARRANGEMENTS & CONSTRUCTION PROCEDURES

7.4.1 On-site start-up meeting

The mandatory **On-Site Start-Up Meeting** must be conducted prior to commencement of any site/camp establishment, earthworks, and/or construction activities and will focus on site-specific conditions and requirements that may apply to the project and may require additional or special measures of control.

On-Site Start-Up Meeting points of discussion are:

- The Construction EMP & other relevant site documents
- Project to be discussed and all uncertainties are cleared
- Method statement/s to be discussed
- Power line installation access routes (if applicable)
- Road and construction area to be demarcated
- Materials stockpile and lay down areas to be demarcated
- Method of stockpiling to be discussed
- Firefighting procedures
- Mandatory firefighting equipment & fire preventative measures
- Solid waste removal intentions
- Placement, type, and service of toilets to be agreed on
- Placement and type of rubbish bins and removal of rubbish to be agreed on
- Labour camp to be demarcated and services agreed on
- Environmental Education and awareness training session to all contractors & onsite staff/labor.
- Location & establishment of concrete batching plant facility.
- Safety aspects for construction activities associated with the expansion of the dam. This must include safety aspects for on-site staff and/or contractors who will be employed to manage/oversee the dam expansion works.

7.4.2 Start-up meeting participants

Minutes of the onsite Start-Up Meeting will be condensed to a report format and circulated to all attendees of the above-named meeting for their perusal and comments. The On-site Start-up Meeting report will form part of this EMP. If any discrepancies between the start-up report and the EMP arise then the EMP will take precedence until clarification on the discrepancy is clarified. If any discrepancies between the EMP and the EA then the EA will take precedence until clarification on the discrepancy is clarified.

Participants to the start-up meeting can include:

- Applicants Representative.
- Main Contractor's Representative.
- Resident Engineer
- Site foreman.
- Environmental Consultant.
- Environmental Control Officer.

NB: It is the responsibility of the main contractors to ensure that all sub-contractors, that work on the site during and after the civil's contract, are informed of the environmental conditions pertaining to the site.

7.5 ENVIRONMENTAL AWARENESS TRAINING

7.5.1 Environmental awareness course

Environmental awareness training courses shall be run for all personnel on-site. The ECO will be responsible for the initial awareness course which shall include all relevant management, the Construction Supervisor, the Contractor, and all foremen. All attendees shall remain for the duration of the course.

The Contractor shall be responsible to ensure that all his personnel and subcontractors (if applicable) are informed and made aware of the environmental constraints and shall also supply the ECO with a monthly report indicating the number of employees used by him. If refresher courses are deemed necessary, for instance, where personnel disregard the requirements of the EMP, the time lost and the cost of the course would be for the account of the Contractor.

7.5.2 Specific training

All contractors and workers shall be informed about any special habitat, biodiversity feature, vegetation, and /or rare plant species that might be present on the specific construction site (if applicable).

7.6 METHOD STATEMENTS

Method statements from the contractor will be required for specific sensitive actions on request of the authorities, the Applicant, or ECO.

A method statement forms the baseline information on which sensitive area work takes place and is a “live document” in that modifications are negotiated between the Contractor and ECO/applicant, as circumstances unfold.

All method statements will form part of the EMP documentation and are subject to all terms and conditions contained within the EMP main document.

These documents must be available to the authorities for inspection or on request.

A method statement describes the scope of the intended work in a step-by-step description for the ECO and Applicant to understand the contractor’s intentions. This will enable them to assist in devising any mitigation measures, which would minimize environmental impact during these tasks.

The Contractor must submit the method statement before any particular construction activity is due to start. Work may not commence until the ECO and applicant have approved the method statement.

Method statements need to be compiled by the contractor for approval by Applicant and the ECO. The contractor must submit written method statements to Applicant for the purposes of the environmental specification, a “Method Statement” is defined as a written submission by the contractor to Applicant setting out the plant, materials, labor, and method the contractor proposes using to carry out an activity, in such detail that Applicant and the ECO can assess whether the contractor’s proposal is in accordance with the specifications and/ or will produce results in accordance with specifications.

The method statement must cover applicable details with regard to:

- Construction procedures
- Materials and equipment to be used
- Getting the equipment to and from site
- How the equipment/ material will be moved while on site
- How and where the material will be stored
- Location & establishment of concrete batching plant facility.
- The containment (or action to be taken if containment is not possible) of leaks or spills of any liquid or material (of any potentially hazardous material) that may occur
- Timing and location of activities
- Compliance/ non-compliance with the Specifications, and
- Any other information deemed necessary by the Applicant and the ECO

The Contractor must abide by these approved method statements, and any activity covered by a method statement must not commence until Applicant and the ECO has approved of such method Statement.

NB: No work may commence or take place before the Method Statement has been approved by all relevant parties. List of possible Method statements includes, but are not limited or restricted to:

- Demarcation
- Entrance and haul roads
- A traffic management plan for the site access roads.
- A transportation plan for the transport of larger components.
- An erosion management plan.
- Clearing of vegetation & topsoil removal
- Stockpiling
- Temporary storage facilities
- Construction camp & site offices

- Fuel storage
- Laborer's facilities (including chemical toilet(s))
- Mandatory site equipment
- Waste control
- Cement mixing & batching areas
- Construction vehicle maintenance
- Heavy earthmoving equipment
- Dust control
- Noise control
- Rehabilitation

7.6.1 Additional method statements

Any additional method statements (with regards to a specific aspect of construction) that may be required must be **submitted** and approved before commencement of the specific works and must be available at the site offices.

7.7 AUDITING PROGRAMME

In terms of Regulation 34 of the NEMA EIA Regulations, 2014 (as amended), the holder must conduct environmental audits to determine compliance with the conditions of the Environmental Authorisation, and/or other authorizations, the EMPr, and any other statutory requirements that may be applicable when undertaking the listed activities, and must submit Environmental Audits report to the Competent Authority. The Environmental Audit Report must be prepared by an independent person and must contain all the information required in Appendix 7 of the NEMA EIA Regulations (as amended).

A post-construction Environmental Audit, as defined above, must be conducted not less than one month after completion of construction, with the final construction audit report being submitted to the Competent Authority not more than 3 months after construction is completed, or as stated by the Competent Authority.

The holder of the license must within 7 days of the submission of the above-mentioned report to the Competent Authority, notify all potential and registered I&APs of the submission, and make the report available to anyone on request and a publicly accessible website.

7.8 NON-COMPLIANCE

Applicant (on recommendation by the ECO) reserves the right at all times for the duration of this agreement to impose restrictions and associate penalties on the contractor with respect to the specific nature, timing, and extent of construction activities on environmentally sensitive sites.

7.8.1 Corrective action instruction

The ECO may issue an onsite corrective action instruction to the site agent, or, by means of an entry into the Site Instruction Register for remedial work to be carried out to rectify any non-compliance that has been carried out within a reasonable agreeable time frame to carry out and complete the remedial work.

7.8.2 Written warning

In instances of non-compliance with the EMP by the contractor (or any of their employees) or sub-contractor/s (or any of their employees) that move on or off the site, the onsite ECO must issue a written warning indicating the non-conformance to the contractor.

If repeated instructions by the ECO to the site agent to respond to the corrective action instruction have not been carried out the ECO can issue a Written Warning notation instructing the site agent to timeously carry out the corrective measures as per the original non-compliance.

7.8.3 Penalty fines

In the event of the site agent's negligence to respond and correct the noted non-compliance, the ECO may in collaboration with the relevant parties recommend that a Penalty Fine be imposed on the contractor.

- The applicant, in consultation with the ECO, must determine the amount of the penalty applicable in accordance with the Penalties for Non-Compliance Schedule of Tariffs.
- Such penalty amount must be in writing and presented to the contractor within seven (7) days of the written warning.
- The applicant may recover penalties by deducting the fine from the offending contractor.
- The contractor will be responsible for all costs incurred where emergency procedures are implemented to deal with accidents impacting the environment as well as the rehabilitation of such damage in conjunction with the ECO and site engineer.
- In serious cases, at the discretion of the Applicant and the Environmental Consultant/ECO, any multiple offenses can be added together.

7.8.4 Stop works

The ECO (after consultation with Environmental Consultant/Applicant/Engineer) may also stop the works or part thereof until the situation is resolved; no extension of time is claimable by the contractor.

These penalties do not preclude any prosecution under any law or regulation.

7.9 CHANGES TO EMP

Although care has been taken to address all known relevant environmental issues for the construction phase, it may become necessary to add or amend certain procedures or instructions to improve the efficiency of the Environmental Management Plan (EMP).

- Only those additions or amendments of this EMP that will either improve environmental protection or can be proved not to have any negative effect on the immediate and surrounding environment will be considered.
- Changes or deviations have to be motivated in writing by means of a Method Statement and the same procedures for a standard Method Statement have to be followed.
- Any additions or amendments must be submitted by the ECO to DEADP (if so requested) after the ECO has consulted with the Environmental Consultant and Applicant.
- No deviation from the contents of the EMP will be allowed without following the above procedures.

7.10 RECORD KEEPING

All records relating to the implementation of this Environmental Management Plan must be kept together, be readily retrievable, and available for scrutiny by any relevant authority. Records include the following:

- Declarations of understanding;
- ECO Checklist, audits, and /or diary;
- Method statements
- Photographs (must be taken before, during, and immediately after construction as a visual reference);
- The Environmental completion statement.

These records must be available for scrutiny by any relevant authorities.

7.11 STANDARD MANAGEMENT PROCEDURES

7.11.1 Access & haul routes

The Contractor must control all access (vehicles and plant) to and from the construction site, including that of his suppliers so that they remain on the pre-approved designated routes. In addition, such vehicles and plant must be so routed and operated as to minimize disruption to regular users of the routes.

- Where heavy-duty vehicles and construction plant are required, both the type of vehicles/machinery and the area/s these are to access shall be specified in a Method Statement.
- Access routes/haul roads will utilize only existing roads or tracks unless such routes are not available or new routes are to be constructed as part of the project, in which case a Method Statement must be submitted for the construction of any new access/ haul roads (including temporary routes).
- No new roads or tracks may be created except where such routes are specifically approved by the ECO, in the EA, or this EMP.
- Any new access roads/haul roads must be designed to minimize erosion and must run across slopes and not directly uphill.
- All vehicles and access to the site must remain within demarcated access routes and working areas on site.
- All reasonable measures must be implemented to minimize impacts on local commuters e.g. limiting construction vehicles traveling on public roadways during the morning and late afternoon commute time and avoid using roads through densely populated built-up areas so as not to disturb existing retail and commercial operations.
- On gravel or earth roads on site, the vehicles of the Contractor and his suppliers may not exceed a speed of 25 km/h.
- On public roads adjacent to the site vehicles will adhere to municipal and provincial traffic regulations.
- All temporary access routes must be rehabilitated at the end of the contract to the satisfaction of the ECO.

If so required by the owner of the land the following may also apply concerning access and vehicular movement on site:

- All Contractors, subcontractors, and staff shall be identified by clothing with company logos and be in possession of valid SA identity documents.

- Deliveries, removals, etc. to be completed during normal working hours (unless otherwise agreed upon by the Construction Supervisor.
- No personnel shall stay permanently on-site unless permission to stay on-site is provided as part of the construction contract.
- Access routes must be demarcated by orange twine/danger tape on steel posts or temporary fencing.
- The Contractor shall at his cost document the existing condition of all access roads prior to commencement.
- Should any damage occur to the access road as a result of the upgrade activities, the road will be rehabilitated to its original state with all costs borne by the contractor.

7.11.2 Appropriate use of machinery

The contractor must at all times carefully consider what machinery is appropriate to the task while minimizing the extent of environmental damage.

- The contractor may not operate any machinery outside the demarcated area.
- All vehicles and equipment must be routinely inspected for fuel and oil leaks and kept in good working order and serviced regularly. Leaking equipment must be repaired immediately or removed from the Site. When servicing equipment, drip trays must be used to collect the waste oil and other lubricants. Drip trays must also be provided in construction areas for stationary plant (such as compressors) and for "parked" plant (such as scrapers, loaders, vehicles). Drip trays will be kept free of water that will float the oil to the overspill. All drip trays/bungs to attain a 120% capacity of the plant fuel/oil capacity.
- Where practical, all maintenance of plant and machinery on Site must be performed in workshops. If it is necessary to do maintenance outside of a workshop area, the Contractor must obtain the approval of the Engineer and the ECO prior to commencing activities.
- Appropriate 2.5 kg (minimum requirement) dry powder SABS approved and service certified firefighting extinguisher must be a mandatory item on all vehicles working and moving on or off the construction site.
- The servicing, repairs, and maintenance of all construction machinery must take place at the designated service and maintenance yard and not along the proposed new road construction route.

7.11.3 "No-Go" areas

Specifications of the Environmental Authorisation (EA), the Environmental Management Plan (EMP), or the On-Site Start-Up Meeting (OSSM) can require that certain areas are to be considered as "No go" areas as a result of their environmental significance or proximity to environmental significant features.

- No-Go areas will be demarcated and indicated on a site plan.
- A Method Statement is to be submitted to the ECO by the Contractor, detailing the method of fencing for the protection of such conservation areas.
- No-Go areas are out of bounds to the Contractor and his staff, sub-contractors and their staff or suppliers and their staff or any other person involved in the project, without the written permission specified by the ECO.
- The Contractor must ensure that, insofar as he has the authority, no person, machinery, equipment or material enters the designated "No Go" areas at any time.

- All contractors must be made aware of the importance of these features and the consequences of non-compliance.

7.11.4 Restriction of working areas

The approved layout plans will be used to establish the site demarcation (footprint). All relevant parties responsible for the day-to-day activities on the site will be present and made aware of the implication of the site demarcation. They include the:

- Environmental Consultant: EnviroAfrica
- Principle Agent
- Main Contractor: Project Site Manager
- Sub-contractor: The project contractor
- ECO: Environmental Control Officer

The proposed site will be demarcated prior to the commencement of any construction whatsoever, this includes site establishment, the moving of construction material, or any other items onto the site, etc.

- The site will be demarcated with appropriate dropper poles. A single strand of orange baler twine is to be attached to the dropper poles to indicate boundaries and no-go areas for site personnel and vehicular movement. (Alternative fencing may be decided upon dependent on site requirements).
- The construction area i.e. road, stockpile areas and development footprint, etc., must be demarcated and fenced off with dropper poles and orange baler twine approximately 1m high is considered adequate. **The demarcation will be agreed on during the start-up meeting.**
- All fencing and fence placement/positioning must be approved by the ECO on site.
- Work areas and access routes must be demarcated to minimize environmental impact.
- In the event that sensitive features are threatened by construction activities, temporary fencing off of these areas (for individual areas such as trees or rocks) or the construction area (when working in a mainly natural environment) is recommended.
- NB: Also note the requirements discussed under the following paragraphs: 7.11.6; 7.11.7; 7.11.2; 7.11.10; 7.11.8; 7.11.9.
- The Contractor must maintain in good order all demarcation, fencing, and barriers for the duration of construction activities, or as otherwise instructed.
- The demarcation may not be moved, re-located or altered, or changed without the approval of the ECO.
- Any temporary fencing removed for the execution of any portion of the works is to be reinstated by the Contractor as soon as practicable.
- The Contractor at the end of the contract must remove all demarcation, fencing, or barriers not forming part of the final works on Site.

7.11.5 Safety aspects during the expansion of dam (construction phase)

Working in the vicinity of the existing dam may present risks with regards to injury where staff may slip and fall into the existing dam (even if emptied) during construction. Therefore, work conducted in/around the dam must be carried out safely and cautiously. The following measures can be implemented:

- Appropriate platforms;

- Safety nets and safety harnesses;
- Dam signage (including warning signs);
- First aid equipment;
- Rescue equipment (e.g. buoyancy equipment) and adequate procedures to be followed in case of an emergency;
- suitable means of access to and out of the construction area;
- Daily consideration for weather conditions; and
- No-go areas must be adequately demarcated.

7.11.6 Protection of natural veld

Habitat fragmentation is usually defined as a landscape-scale process involving both habitat loss and the breaking apart of habitat. Habitat loss has large, consistently negative effects on biodiversity. Habitat fragmentation per se has much weaker effects on biodiversity but could be just as negative. As such the construction activities must endeavor to minimize its impact on any remaining natural features and natural corridors.

- All remaining natural corridors identified as significant biodiversity features during the environmental assessment stage, must be mapped and identified as “No-Go” areas on the site plans and protected measures must be installed (demarcated);
- Except to the extent necessary for the carrying out of the works, no flora may be removed, damaged, or disturbed;
- Trapping, poisoning, and/or shooting of animals is strictly forbidden. No domestic pets or livestock are permitted on Site;
- Where the use of herbicides, pesticides, and other poisonous substances are to be used, the Contractor must submit a Method Statement;
- The Contractor may not deface, paint, damage or mark any natural features, if these should occur (e.g. trees, rock formations, buildings, etc.) situated in or around the Site for survey or other purposes unless agreed beforehand with the Engineer and the ECO. Any features affected by the Contractor in contravention of this clause must be restored/rehabilitated to the satisfaction of the Engineer and the ECO.
- All incidents of harm to any animal or natural vegetation (apart from the agreed-upon areas) must be reported to the ECO.

7.11.7 Protection of flora

It must be noted that the vegetation associated with the proposed site for development is characteristic of disturbed areas. Moreover, plant species within the construction footprint are not of conservation value. A plant rescue and protection plan (if applicable) which allows for the maximum transplant of conservation important species from areas to be transformed should be implemented, if possible. Please also refer to the specific recommendations in Section 6.2 above.

- The areas of vegetation that are to be protected during construction must be demarcated and indicated as “No-Go” areas on a site plan. Include the area under the canopy of trees so that tree roots will not be damaged by soil compaction.
- All flora identified to be rescued must be removed and placed in an area specifically allocated for these plants to ensure that the necessary care thereof will take place until being relocated and planted in designated areas.
- The specialist must also advise and oversee a re-vegetation and habitat rehabilitation plan during the construction and operation of the facility (if applicable). Restoration must be

undertaken as soon as possible after the completion of construction activities to reduce the amount of habitat converted at any one time and to speed up the recovery of natural habitats.

- Also, refer to the requirements of the rehabilitation and restoration guidelines (Refer to paragraph 7.11.27).

7.11.8 Protection of fauna and Avi-fauna

The trapping, poisoning, and/or killing of animals is strictly forbidden. No domestic pets or livestock are permitted on Site. Many slow-moving animals, local amphibians, and other species follow instinctive movements along roadside corridors where they travel from place to place.

- Every effort must be implemented on a daily ongoing basis by the contractor to ensure that the construction areas have been checked for any animals and to ensure their removal and protection from direct and in-direct impacts during the construction activities.
- The removal of fauna from the site must be done in accordance with the requirements of the Nature Conservation Ordinance regulating these activities.
- Environmental corridors and “No-Go” areas must be demarcated and protected.

7.11.9 Clearing of vegetation, stripping & conservation of topsoil

The contractor shall take all reasonable steps to minimize the impact of his activities on the environment. If natural vegetation has to be removed for construction purposes, the natural vegetation shall be rescued, re-used (e.g. stabilizing the area after construction or re-vegetating other impacted areas) in such a way that it enhances the remaining natural veld. By the same principle topsoil (which contains the remaining natural seed store as well as possibly many bulb species) must be carefully removed and stored or re-used for rehabilitation or impacted areas in the immediate vicinity.

Vegetation clearing:

- A Method Statement must be submitted detailing the methods to be used for vegetation clearing.
- All cleared areas must be stabilized as soon as possible.
- Burning of cleared vegetation on site is prohibited.
- The burying of cleared vegetation or use as part of backfill or landscape shaping is prohibited unless written approval is obtained from the ECO.
- Cleared vegetation may be used for mulch or slope stabilization of the Site.
- Should bulk vegetation be removed from the designated working areas (footprint area) then tall vegetation shall first be removed through brush cutting and chipping of larger shrub material; this may be added to the topsoil material stockpiles as mulch.
- Unless otherwise agreed upon, only indigenous plant material shall be used for this purpose.

Topsoil removal

- Prior to any activities within the demarcated work areas, topsoil material shall be removed to a depth of 300 mm or deeper if specified by the engineer in consultation with the ECO, and stockpiled in a designated area for use in the rehabilitation of the site post-construction.
- Any area where the topsoil will be impacted by construction activities, including the construction offices and storage areas, must have the topsoil stripped and removed and covered with herbaceous vegetation (other than alien species), overlying grass, and other fine organic matter and stockpiled for subsequent use in rehabilitation.

- Topsoil storage areas must be convex and should not exceed 2m in height. The Contractor must ensure that the material does not blow or wash away.
- Topsoil must be treated with care, must not be buried, or in any other way be rendered unsuitable for further use (e.g. by mixing with spoil) and precautions must be taken to prevent unnecessary handling and compaction.
- In particular, topsoil must not be subject to compaction greater than 1 500 kg/m² and must not be pushed by a bulldozer for more than 50 m. Trucks may not be driven over the stockpiles.
- Topsoil from different soil types must be stockpiled separately and replaced in the same areas from which they were taken if this proves to be the case. Specific attention should be given to the areas that may house rare and threatened species.
- Topsoil areas must be demarcated to ensure the safekeeping of topsoil and to separate different stockpile types.
- Remove and stockpile topsoil and subsoil separately
- Stockpile topsoil within an area where no stormwater runoff is expected

Reestablishment of topsoil

- Replace the soil in the correct order e.g. subsoil below and topsoil above, as soon as possible after construction activities have been completed
- Compact subsoil while in a moist state and spread topsoil as evenly as possible over the subsoil. The areas where the soil has been replaced should be at the same level as the immediate surroundings.
- Rip compacted areas, manually, within the immediate vicinity of the construction footprint to a depth of approximately 300mm and cover with topsoil and seed with *Cynodon dactylon*. The use of fertilizers and other chemical soil enhancers should be avoided.

7.11.10 Erosion & sedimentation control

The Contractor must take appropriate ongoing and active measures to prevent erosion resulting from their construction activities and operations as well as stormwater control measures to the satisfaction of the ECO. During construction, the Contractor must protect areas susceptible to erosion by installing all the necessary temporary and permanent drainage works as soon as possible.

To achieve erosion and sediment control, the following apply to all sites:

- No new development, without written authority approval, will be allowed on slopes greater than 12% (CARA, regulation 3). If applicable terraces will be made in accordance with agricultural regulations.
- Install erosion and sediment controls before work starts and maintain these features throughout the construction and operational phases (as applicable).
- Leave as much vegetation as possible.
- Install temporary fences to define “No Go” areas in those areas that are not to be disturbed.
- Divert run-off from upslope away from the site, but ensure that it does not cause downstream erosion. For example, dig drainage channels (catch drains sized to accommodate the upslope catchment).
- Install sediment controls downslope of the site to catch sediment (if applicable).
- Inspect and maintain erosion and sediment controls regularly.
- Limit vehicle movement to the site and control access points. Clearly mark such access points and inform all suppliers.
- Save and re-use topsoil during re-vegetation. Never store topsoil around trees as this may kill them. Spread the topsoil back when the work is finished and re-vegetate the site as soon as

possible to control erosion. Remove the sediment and erosion controls only after re-vegetation was successfully implemented.

- Store all stockpiles and building materials behind sediment fences. Cover them with plastic to prevent erosion by wind.
- It is illegal to discharge water into a public stream if the quality does not conform to the required health or water standards. Other measures as may be necessary must be taken to prevent the surface water from being concentrated in streams and from scouring the slopes, banks, or other areas. All potential hazardous fluids/materials must be protected from the rain to prevent them from being washed into stormwater channels. All such measures must be discussed with and approved by the ECO.

Please also refer to the method statements of the river maintenance and management plan. Please note that these Method statements only serve as guidelines and any changes to the method statements should be communicated to the Department of Environment and Development Planning.

7.11.11 Alien invasive management plan

In accordance with Regulation 15 and 16 of the Conservation of Agricultural Resources Act, 1983 (Act no. 43 of 1983) (CARA) as amended, all listed alien invasive plant species must management on any land in SA. As such an alien invasive management plan may be required to be implemented during the construction and operation phase of the project. If such a plan is required, it must include mitigation measures to reduce the invasion of alien species and ensure that the removal of alien species is undertaken. Wetlands and rivers are especially susceptible to many species.

- In accordance with CARA all identified alien invasive plants encountered on the property and its immediate surroundings must be controlled.
- All alien invasive species must be identified and removed from each site and its immediate surroundings.
- No vegetation may be buried or burned on site.
- Where the use of herbicides and other poisonous substances are to be used, the Contractor must submit a Method Statement.

Please also refer to the method statements of the river maintenance and management plan. Please note that these Method statements only serve as guidelines and any changes to the method statements should be communicated to the Department of Environment and Development Planning.

The invader status of the various invasive alien species in South Africa is described according to Regulation 15 and 16 of the Conservation of Agricultural Resources Act, 1983 (Act no. 43 of 1983) (CARA) as amended (the 3 categories and their control are summarised underneath).

Category 1 (Declared Weed)

- Prohibited on any land or water surface in South Africa
- Must be controlled or eradicated (except in biological control reserves).

Category 2 (Declared Invader – commercial value)

- Allowed only in demarcated areas under controlled conditions
- Outside of controlled areas, invaders must be controlled or eradicated where possible
- Prohibited within 30 m off the 1:50 year flood line of watercourses or wetlands unless authorization has been obtained

Category 3 (Plant Invaders – ornamental value)

- Allowed only in areas where they were already in existence with the promulgation of the regulations.

- Prohibited within 30 m of the 1:50 year flood line of watercourses or wetlands unless authorization has been obtained.
- All reasonable steps must be taken to ensure that they do not spread.
- Propagative materials of these plants (e.g. seeds or cuttings) may no longer be planted, propagated, imported, bought, sold, or traded in any way.

7.11.12 Protection of archaeological & paleontological remains

Archaeological remains are ancient man-made objects, structures, or ancient burials that have been preserved on the earth's surface, underground, or underwater and serve as the historical sources that make it possible to reconstruct the history of human society, including mankind's prehistory. Paleontology, on the other hand, is the study of prehistoric life. It includes the study of fossils to determine organisms evolution and interactions with each other and their environments (their paleoecology). Paleontology lays on the border between biology and geology and shares with archaeology a border that is difficult to define. Please refer to the specific recommendations in Section 6.2.

- Basic archaeological remains include work tools, weapons, domestic utensils, clothing, and ornaments; settlements including campsites, fortified and unfortified settlements, and separate dwellings; ancient fortifications; the remains of ancient hydraulic structures; ancient agricultural fields; roads; mining pits and workshops; ancient burial grounds and various burial and religious structures (stelae, stone figurines, stonefish monoliths (vishaps), menhirs, cromlechs, dolmens, sanctuaries); drawings and inscriptions carved into individual stones and cliffs; and architectural monuments. Archaeological remains also include ancient ships and their cargoes that sank in rivers and seas and settlements that came to be underwater as a result of shifts in the earth's crust
- Should any unmarked human burials/remains or ostrich eggshell water flask caches be uncovered, or exposed during construction activities, these must immediately be reported to the ECO and South African Heritage Resources Agency (SAHRA) (At Ms. Mariagrazia Galimberti 021 462 4502) for information on the appropriate course of action to be taken. Burials, etc. must not be removed or disturbed until inspected by an archaeologist or without written approval from SAHRA.
- Should any substantial fossil remains (e.g. vertebrate bones and teeth, shells, petrified wood) be encountered during excavation, however, these should be reported to SAHRA for possible mitigation by a professional paleontologist.
- Note that the Contractor may not, without a permit issued by the responsible heritage resource authority; destroy, damage, excavate, alter, deface or otherwise disturb any archaeological site or archaeological material. The latter is a criminal offense under the Heritage Resources Act.

SAHRA contact details:

PO Box 4637, CAPE TOWN, 8000
 111 Harrington Street, Cape Town
 Tel: (021) 462 4502
 Fax: (021) 462 4509
 Website: www.sahra.org.za

7.11.13 Storage of construction material & stockpiling

New construction material will be stored in demarcated areas on the affected properties prior to commencement construction. The Contractor must provide a method statement (for approval by the ECO) of the construction activities which will indicate:

- the type and quantity of material to be stored;
- whether any oil contaminated/containing equipment will be stored;
- how (including what type of vehicles will be required) it will be delivered the material on-site at the necessary storage area; and
- whether there is any risk of spill or runoff of any building materials or chemicals and how this is to be mitigated.

In addition:

- The Contractor must ensure that any delivery drivers are informed of all procedures and restrictions (including "no go" areas) required to comply with the Specifications. The Contractor must ensure that these delivery drivers are supervised during off-loading, by someone with an adequate understanding of the requirements of the Specifications.
- All manufactured and/or imported material must be stored within the demarcated area, and, if so required, out of the rain. All lay-down areas outside of the construction camp must be subject to the Engineer and the ECO's approval in such a way as not to cause a nuisance or environmental damage.
- All building materials are to be prepared at the batching plant, to enable the effects of cement and other substances, and the resulting effluent to be more easily managed.
- It is essential that any imported material i.e. base material for road works, building sand, bedding base sand for pipe/cable lines, etc. must be screened and of which the origins must be identified prior to arriving at the receiving environment, this must be approved by the Engineer / ECO.
- Special care must be taken to prevent bringing in materials contaminated with seeds of Invasive Alien Plants. Contractors shall not import construction materials such as sand, gravel, or fill contaminated with seeds of Invasive Alien Plants, or quarried from areas surrounded by Invasive Alien plant species such as Port Jackson or Rooikrans.
- The Contractor must negotiate appropriate space for this purpose on an area away from natural vegetation and any wetland habitat with the ECO.
- The Contractor must ensure that all staff, contractors, and subcontractors are aware of and keep material within these designated storage areas. The Construction Supervisor shall ensure that the consultant team is familiar with the same.
- Contractors will not be allowed to store new construction material on the sides of the access road, or within natural vegetation, or next to the existing access road.
- Stockpiling of gravel, cut, fill or any other material including spoil should only be allowed in degraded areas or areas below the future cover of buildings and tar or paved parking surface.
- Any area used for stockpiling and not covered by building development must be returned to at least the state they were in before stockpiling and it must be ensured that the erosion potential of these areas is not increased.
- The Contractor must ensure that the material does not blow or wash away or mix. If the stockpiled material is in danger of being washed or blown away, the Contractor must cover it with a suitable material, such as hessian, netting, or plastic.
- Also, refer to the traffic- and transportation management plans and their requirements.

7.11.14 Oil storage and management

An important potential environmental impact is oil spills from any oil-filled equipment and machinery that may occur during transportation or storage of decommissioned and new construction material/equipment. The following conditions shall apply:

- Vehicles must be checked for oil leaks prior to going on site
- Care should be taken to prevent any potential oil spillage during upgrading activities.
- Sufficient measures should be put in place to ensure that any potential oil spills are mitigated.
- An oil spill kit should be available on-site at all times during the construction activities;
- Oil containment facilities should be provided for any oil-filled equipment onsite;
- All oil spills must be reported to the ECO within 24 hours, indicating the containment and rehabilitation measures implemented

Oil spill kits are available from:

- **Drizit** (021) 531 5335
- **Enretech** (021) 683 1858
- **Pinelands Environmental Technology** (021) 531 3749

7.11.15 Storing of petroleum products

Although no petroleum products will be stored on-site, it is important to know that petroleum fuels contain harmful substances known to cause health problems and can easily have adverse effects on water quality, and the environment. Petroleum spills can move rapidly into the soil and quickly contaminate drinking water. To prevent pollution it is important to, use proper methods when handling, using, and storing diesel fuel, gasoline, kerosene, or other petroleum products.

The South African National Standards pertaining to the installation of a storage tank include:

- Sans 310, which requires that an aboveground storage tank be of sufficient structural strength, based on sound engineering practices, to withstand normal operations and use;
- Sans 1668, for fiber-reinforced plastic tanks for the underground storage of petroleum products;
- Sans 10089-1, which deals with the storage and distribution of petroleum products in aboveground bulk installations; and
- Sans 1535, for glass-reinforced polyester-coated steel tanks, for the underground storage of hydrocarbons and oxygenated solvents, which are intended to be buried horizontally.

Storing of smaller quantities of fuel or oil

Any fuel storage proposals must be cleared by the ECO before any storage or stockpiling takes place. If the contractor proposes to use only small fuel storage facilities (< 200 liters) the following basic requirements must be adhered to:

- Fuels and oils must be safely located out of harm's way from the elements and safety and fire prevention must be strictly adhered to.
- All fuel oil containers must be placed within suitable drip trays to prevent accidental spillage of oils and fuels.
- A suitable leak-proof container for the storage of oiled equipment (filters, drip tray contents, and oil changes, etc.) must be established.
- All spills are to be recorded in the ECO diary.

7.11.16 Storing of hazardous substances

Although no potentially hazardous substances will be stored on-site it is important to understand how potentially hazardous substances are to be stored on-site, the Contractor must submit a Method Statement detailing the substances and/or materials to be used, together with the storage, handling, and disposal procedures of the materials to the ECO.

- Hazardous materials must be stored under lock and key in designated areas with properly displayed and visible warning signs.
- No works related to the submitted Method Statement may commence until the Method Statement has been studied and approved in writing.
- An effective monitoring system to detect any leakage or spillage of all hazardous substances during their transportation, handling, use, and storage must be implemented. This must include precautionary measures to limit the possibility of oil and other toxic liquids from entering the soil or stormwater systems.
- Measures to protect hydrological features such as streams, rivers, pans, wetlands, dams and their catchments, and other environmentally sensitive areas from construction impacts including the direct or indirect spillage of pollutants must be implemented.
- **Paints:** - No paint products may be disposed of on Site and brush/roller wash facilities must be established to the satisfaction of the Engineer and the ECO. Oil-based paints and chemical additives and cleaners such as thinners and turpentine must be strictly controlled. A Method Statement detailing the paint management procedures is required.
- **Hazardous building materials:** -Hazardous building materials (e.g. asbestos, fiber claddings, refrigerants, coolants, sub-station cooling oils, etc.) must be identified and dealt with in accordance with the relevant safety and health legislation. All such material must be separated on-site and disposed of at appropriately licensed disposal sites. The Contractor must supply the ECO with a certificate of disposal.

7.11.17 Use of cement or concrete

All concrete will be imported from a local supplier and will not be mixed on-site.

The Contractor is advised that cement and concrete are highly hazardous to the natural environment because of the high pH levels of the material, and the chemicals contained therein. Wash-out water with high pH is the number one environmental issue for the ready mix concrete industry. The alkalinity levels of wash water can be as high as pH 12, which is toxic to fish and other aquatic life.

No cement will be mixed on-site for this project. The site agent must indicate on the Method Statement the proposed total volume of concrete that is needed for the completion of the entire project.

Concrete/cement mixing (if applicable):

- Concrete and cement may only be mixed on existing hard-surfaced areas, edged mortarboards, or a suitable container. Concrete may not be mixed or stored directly on the ground under any circumstances;
- The visible remains of the batch and concrete, either solid, or from washings, must be physically removed immediately and disposed of as hazardous waste.
- Washing of equipment shall be done in a container to prevent any runoff of contaminated washing water.

- Extreme care must be taken to limit the amount of water contaminated by washing equipment. Water from concrete washing can be re-used in concrete mixes or must be stored in drums, then removed from the site and disposed of at a licensed municipal dumpsite.

Concrete batching plants (not applicable)

The following procedures must be implemented to control wastewater run-off from concrete batching plant locations:

- The location of concrete batching areas must be approved by the ECO (if possible/appropriate, the use of ready-mix concrete is preferred).
- Concrete batching facilities must have suitable bunding methods in place to ensure minimal wastewater run-off occurs during batching operations.
- Contaminated water may not enter a natural or man-made (e.g. trench / sloop or dam) water system. Preventative measures include establishing sumps from where contaminated water can be either treated in situ or removed to an appropriate waste site.
- Dry mixing batching areas to be carefully placed in consultation with the ECO.
- Cement bags are to be stored securely out of harm's way from the elements (wind and rain). Bags have to be covered and placed on plastic sheeting. Used cement bags must be disposed of regularly via the solid waste management system, and must not be used for any other purpose.
- Sand and stone used for cement or concrete batching must be stored on plastic layers (or on ECO-approved disturbed areas) to prevent contamination of the natural environment.
- Cleaning of equipment and flushing of mixers must not result in pollution of the surrounding environment. All wastewater resulting from batching of concrete must be disposed of *via* the contaminated water management procedure.
- Excess or spilled concrete must be confined within the works area and all visible remains of excess concrete must be physically removed and disposed of on completion of cement work. Washing the remains into the ground is not acceptable. All excess aggregate must also be removed.
- Wash-down areas must be confined to within the concrete batching areas only.

7.11.18 Blasting/drilling (not applicable)

In the event where blasting or rock drilling is required, the following must be implemented:

- A Method statement must be provided for each case separately **before** commencement of blasting works.
- The contractor must take all necessary precautions to prevent damage to special features and the general environment, which includes the removal of fly rock.
- The contractor must ensure that no pollution results from drilling operations, either as a result of oil and fuel drips or from drilling fluid. The contractor must take all reasonable measures to limit dust generation as a result of drilling operations.
- The ECO must be given a 24-hour notice before blasting events.

7.11.19 Fire fighting

Adequate firefighting equipment according to the fire hazard during the construction period must be available on-site and in good working order (at least one type ABC (all-purpose) 2.5 kg extinguisher and 3 fire beaters per working area). The persons on site must be trained in the use of such equipment.

- The main contractor must provide a list of all authorities involved in firefighting in the region. This list must include emergency contact numbers and must be visible at the site office.
- Welding, gas cutting, or cutting of metal will only be permitted inside the working areas.
- The Contractor must pay the costs incurred to organizations called to put out any fires started by him. The Contractor must also pay any costs incurred to reinstate burnt areas as deemed necessary by the landowner.
- It is required that contractors have available [if there is cell phone reception] the emergency telephone numbers of the nearest local Fire Fighting Station and that an emergency firefighting re-action plan has been drawn up with onsite workers and the resident land-owner / farmer.

7.11.20 Emergency Procedures

It is the responsibility of the contractor to assess the potential risks to the environment as a result of the project. As such, the contractor must have the necessary standard emergency operating procedures in place to deal with any potential emergency such as oil spills or fire.

- All staff should be made aware of the necessary basic emergency procedures in the event of an emergency including injuries to staff. The appropriate equipment and identified personnel to deal with such basic emergencies should be available on site.
- **Fire:** The Contractor must advise the relevant authority of a fire as soon as one starts and must not wait until he can no longer control it. The Contractor must ensure that his employees are aware of the procedure to be followed in the event of a fire.
- **Hazardous Material Spills:** The Contractor must ensure that his employees are aware of the procedure to be followed for dealing with spills and leaks, which must include notifying the Engineer, the ECO, and the relevant authorities. Treatment and remediation of the spill areas must be undertaken to the reasonable satisfaction of the ECO and Local Authority.

7.11.21 Solid waste management

Waste refers to all solid waste, including domestic waste, hazardous waste, and construction debris. The Contractor is responsible for the establishment of a refuse control system (which must consider recycling wherever possible) that is acceptable to the ECO. Disposal arrangements must be made in advance and cleared with the ECO before construction starts.

- No littering or on-site burying or dumping of any waste materials, vegetation, litter, or refuse may occur.
- All solid waste must be disposed of offsite at an approved landfill site in terms of section 20 of the Environment Conservation Act (Act No. 73 of 1989). The Contractor must supply the ECO with a certificate of disposal.
- The Contractor must provide problem animal- and weatherproof bins with lids of sufficient number and capacity to store the solid waste produced daily. The lids must be kept firmly in the bins at all times. Bins must not be allowed to become overfull and must be emptied regularly.

- Waste from bins may be temporarily stored on Site in a central waste area that is weatherproof and scavenger-proof and which the Engineer and the ECO have approved.
- All hazardous waste must be disposed of at a registered hazardous waste disposal site and certificates of safe disposal must be obtained.
- All waste generated during the decommissioning and reconstruction activities must be removed by the Contractor as soon as possible, and within the period specified in the EMP and disposed of at a registered landfill site.
- The Contractor must make provision for workers to clean up the Contractor's camp and working areas daily so that no litter is left lying around and so that the site is in a neat and tidy state. The Contractor must remove from the site the refuse collected at least once a week.

7.11.22 Toilets & Ablution Facilities

The Contractor must provide suitable sanitary arrangements at designated points of the construction site for all site employees. A minimum of one toilet must be provided per 15 persons at each working area (station) or as stipulated in the Management plan.

- Toilets must be at least 32m away from any watercourse
- The toilet must be within easy reach (max 300m) of the working area and be in good working condition and cleaned daily. Toilet paper must be provided. The toilets must be emptied weekly or when full or when instructed by the ECO on site.
- Disposal arrangements must be made in advance and cleared with the ECO before construction starts. Sanitation provision and servicing must be to the satisfaction of the ECO.
- The Contractor must ensure that toilets are emptied prior to any builders' holidays, and/or weekends.
- Toilets must be of neat construction and must be provided with doors and locks and must be secured to prevent them from blowing over.
- NB: No burying of any waste material on or near the construction site nor anywhere on the surrounding property is permitted.
- Eating areas that are allocated for workers must be established in an environmentally acceptable manner and line with all OH & Safety Act regulations. All on-site and on route workers' temporary eating areas must have acceptable toilet and refuse management systems in place and these areas must have suitable refuse receptacles available for the containment and disposal of general litter and refuse.

7.11.23 Discharge of construction water

Potential pollutants of any kind and in any form must be kept, stored, and used in such a manner that any escape can be contained and the water table not endangered. This particularly applies to water emanating from runoff from fuel depots/workshops/truck washing areas.

- The contractor is responsible for the construction and effective containment and maintenance of settlement ponds must ensure that the surrounding environment is not adversely affected as a result of construction activities.
- Wash-down areas must be placed and constructed in such a manner to ensure that the surrounding areas are not polluted. Contaminated water includes water that is carrying excess sediment due to construction activities.
- Contaminated water storage facilities must not be allowed to overflow and appropriate protection from rain and flooding must be implemented.

- Contaminated water that is removed from site must be disposed of at a facility approved by the ECO and Local Authority.
- No contaminated water that does not meet the water quality standards and criteria under the National Water Act may be released into a natural system, whether it is to surface or groundwater.
- All cement effluent from mixer washings, and run-off from batching areas and other work areas must be contained in suitable sedimentation ponds.
- Sedimentation ponds must be allowed to dry out regularly to allow for solid material to be removed.
- This material must be disposed of suitably, depending on the nature of the material, and to the discretion of the ECO

7.11.24 Treating (flushing/testing) of pipelines (not applicable)

Cleaning/sterilization/flushing of pipelines shall not impair surrounding environmental quality.

- Any contaminated water from such activities shall be contained until it complies with the standards contained in the National Water Act or other relevant Acts, as well as those laid down by the Local Authority.
- Alternatively, it shall be removed from the site and disposed of at an approved waste disposal site.

7.11.25 Eating facilities

The Contractor must designate eating areas for the approval of the ECO, which must be demarcated. No eating of meals must take place outside these designated areas without the approval of the Contractor/ESO.

- The feeding or leaving of food for animals is strictly prohibited.
- Sufficient waste bins must be present in this area and emptied regularly.
- The contractor must supply cooking facilities that are suitable for the environment and are not liable to cause the outbreak of fires.
- No overnight camping/stay on site allowed. If overnighting is necessary for security purposes then it must be cleared with the ECO on site.
- No washing in dams or streams is allowed.

7.11.26 Dust Control

The Contractor must take all reasonable measures to minimize the generation of dust as a result of construction activities resulting from along-construction-route activities (but must also take into account possible water constrictions of the area).

- The onsite construction site agent must take into account prevailing wind strength and wind direction and must have preventative measures on standby to minimize dust pollution that may cause damage to people and property.

7.11.27 Restoration and rehabilitation

The Contractor must ensure that all structures, equipment, materials, and facilities used or created on-site for or during construction activities are removed once the project has been completed. On completion of the project or phase, all areas impacted by the construction activities must be reinstated and/or rehabilitated to the satisfaction of the ECO with emphasis on the following:

- Immediately after the demolition of the campsite, the contractor shall restore the site to its original state, paying particular attention to its appearance relative to the general landscape.
- The contractor's procedure for rehabilitation shall be approved by the ECO and Engineer.
- Site offices must be removed and the areas rehabilitated or reinstated to the satisfaction of the ECO.
- Laborer's facilities (if applicable) must be removed and the areas rehabilitated or reinstated to the satisfaction of the ECO.
- All construction site areas must be rehabilitated or reinstated to the satisfaction of the ECO.
- All temporary fencing and demarcation must be removed and the areas reinstated to the satisfaction of the ECO.
- Temporary storage areas must be rehabilitated or reinstated to the satisfaction of the ECO.
- All remaining construction material must be removed and the areas rehabilitated or reinstated to the satisfaction of the ECO.

Any additional **disturbed** areas must be rehabilitated or reinstated to the satisfaction of the ECO. This shall include but not be limited to:

- Earthworks to reinstate the physical characteristics of the site. Here attention to the natural vertical and lateral heterogeneity in landform shall guide the reinstatement of natural areas.
- Replacement of topsoil material – care shall be taken to ensure that the same material that was removed from each area is replaced there since this will carry the seed complement appropriate for re-establishment of each plant community type.
- Final landscaping by machine, but landscaping by hand may be required in many areas under rehabilitation.
- Re-seeding and/or replanting of rehabilitated areas.
- The Contractor shall not be permitted to use fertilizers or pesticides.
- Any potential erosion problems must be addressed. This may require subsequent site visits to monitor the efficacy of erosion control measures.

7.11.28 Land Management

- Vehicles accessing the construction site must be made aware of driving in hazardous road conditions, sharp bends, narrow roads, bad weather, on or near children, or domestic animals along the road.
- Vehicle movements should be kept to a minimum during rain to avoid damage to access roads.
- No fences or gates on the relevant construction property must be damaged. All access gates to the property (construction site) to be kept closed at all times to prevent domestic and or wild animals from getting out. Access by unauthorized personnel should be controlled. The access gates to the construction areas must always be closed.
- Soil erosion must be prevented at all times along the access roads and around construction areas.

7.11.29 Socio-Cultural Issues

- Property owners or property occupiers must be treated with respect and courtesy at all times.
- The cultural lifestyles of the communities living in close proximity to the construction areas must be respected.

7.12 EMERGENCY PREPAREDNESS & RESPONSE

The following potential emergency situations have been identified and include the procedure for responding to, and for preventing and mitigating the environmental impacts that may be associated with them (also refer to Penalties and Fines).

7.12.1 Accidental fires

Fire safety in Fynbos Area is a very real risk and must be stringently controlled. No fires will be permitted on site for any reason. If required, a designated smoking area will be provided, and demarcated, and signposted, with a facility for safe containment and disposal of cigarette butts.

The following measures must be implemented:

- Adequate firefighting equipment must be available on-site and in good working order (including at least one type ABC (all-purpose) 9 kg fire extinguisher and 3 fire beaters per working area). The persons on site must be trained in the use of such equipment.
- The main contractor must provide a list of all authorities involved in firefighting in the region. This list must include emergency contact numbers and must be visible at the site office.
- The contractors must establish an emergency procedure (with contact numbers) to the satisfaction of ECO (whenever work is done in any fire-prone areas).

7.12.2 Hydrocarbon spills

Since the project is in proportion relatively small, no fuel storage or distribution facilities will be established. As a result, the significance of any spill is much reduced. The following must be observed:

- Vehicles will arrive on site already fuelled for the project.
- If additional fuel is needed, it will be brought in as needed (minimal volumes) and refueling will be done using a pump and not a funnel (to minimize the risk of spills).
- Spill trays shall be used during re-fuelling.
- In the case of accidental spillages or leakage, the contractor will be responsible for immediate containment and corrective action (e.g. stopping the leakage), and to inform the Construction Supervisor and ECO.
- The ECO will recommend the best possible environmental solution.
- The Contractor will be liable for any costs incurred.

7.12.3 Concrete/cement spillages

The Contractor/supplier will be liable for the safe and correct deliverance of substantial loads of concrete or cement.

- Should a spill occur the Contractor/supplier will be liable for all costs of the rehabilitation needed.

8. OPERATIONAL EMP (OEMP)

The most important part of the operational phase will be to ensure that the site is meticulously maintained and that the operations are carefully monitored. The applicant will remain overall responsible for the environmental performance of the site and must be aware of the legal requirements and obligations. The applicant must also be aware of the legal action that can be taken against him as a person with regards to negligence leading to environmental pollution.

The owner or delegated responsible person must implement an operational and maintenance management plan which must include:

- Access management and control;
- Energy management and monitoring;
- Erosion management;
- Fire Management;
- Minimize dust and air emissions;
- Protection of indigenous natural vegetation and fauna;
- Specific monitoring and operational instructions;
- Emergency plans will cover all reasonable aspects of the operations which might lead to environmental pollution or degradation.

8.1 TRAFFIC ACCESS ROUTES & HAUL ROADS

The Operator of the site must control the movement of all vehicles and plant including that of his suppliers so that they remain on designated routes. In addition, such vehicles and plant must be so routed and operated as to minimize disruption to regular users of the routes not on the Site.

- On gravel or earth roads on Site, the vehicles of the Contractor and his suppliers must not exceed a speed of 25 km/h.
- On public roads adjacent to the Site vehicles will adhere to municipal and provincial traffic regulations.
- Only approved access roads may be used.
- All measures must be implemented to minimize impacts on local commuters e.g. limiting construction vehicles traveling on public roadways during the morning and late afternoon commute time and avoid using roads through densely populated built-up areas so as not to disturb existing retail and commercial operations.

8.2 ENERGY MANAGEMENT

All reasonable steps must be taken to ensure the efficient management of energy. Energy management and conservation measures must be propagated and encouraged. The objective of energy management will be to encourage the conservation of energy, for example:

- Ensure that the cooling unit is located and operated to conserve energy. If the refrigerant is to be used, please note that R22 as a refrigerant is being phased out (due to negative impact on the ozone) and that the following gasses are more environmentally friendly options: ammonia, R134a, R143a, R404A, R407C, R410A, and R507A.
- Install energy-efficient appliances (e.g. a grade one refrigerator is at least 35% more energy-efficient than a grade three one).

- Install energy efficient lightning (which uses less energy to give the same amount of illumination and last longer than conventional incandescent bulbs).
- Monitor different energy uses (e.g. electricity, fuels, and gas).

8.3 WATER MANAGEMENT (NOT APPLICABLE)

- Ensure that all additional water uses are correctly registered with the Department of Water Affairs (e.g. Agri-industrial use).
- Water conservation measures such as low flow taps, high-pressure hoses, dual flush toilets, water-wise gardens, rainwater tanks, etc. must be encouraged and implemented.
- Every reasonable effort must be made to reduce the long-term water demand.
- Environmental training of personnel must include water conservation awareness.
- A monthly water monitor program to ever reduce the water usage must be implemented (records must be kept).

8.4 EROSION & SEDIMENT CONTROL

Soil erosion (through wind & water) removes valuable topsoil which is the most productive part of the soil profile (containing plant nutrients, seeds, and bulbs). Development disturbs and loosens soils which can easily lead to erosion. The plants and animals that depended on that soil can no longer survive, and the plants that once grew cannot re-establish themselves because the seed store is gone. Soil may then have to be brought back from elsewhere, increasing the cost of the project and the risk of importing weeds and other waste or toxic material. In accordance with the Conservation of Agricultural Resources Act, 1983 (Act No. 43 of 1983) (CARA), erosion management aims to prevent any form of soil erosion through proactive thinking and prevention as well as immediate rehabilitation.

To achieve erosion and sediment control, the following apply to all properties:

- Inspect and maintain erosion and sediment controls regularly and ensure that they can accommodate the upslope catchment.
- Leave as much vegetation as possible.
- Install permanent fences to define 'no go' areas in those areas that are not to be disturbed.
- Install sediment catchment controls down-slope of the site to catch sediment (if applicable).
- Limit vehicle movement to the site and control access points. Mark such access points and inform all suppliers.

8.5 WASTEWATER MONITORING PROGRAM (NOT APPLICABLE)

In terms of the National Water Act, 1998 (Act 36 of 1998), the Discharge of waste or water containing waste is a controlled activity for which a Licence or General Authorization must be obtained. The applicant/legal operator must ensure that wastewater (if applicable) is legally disposed of by applying for a General Authorization, a License, or exemption in terms of the Water Act.

- Wash water used for cleaning of instruments or equipment must not contain any chemicals or hazardous materials that will increase the risk of soil and water contamination.
- Wash water used to clean panels must be recycled as far as possible.
- Measures to prevent erosion must be implemented.
- A wastewater monitoring program may be required, which must include monitoring of quantities disposed of (monthly) and compliance of treated wastewater quality after treatment but before disposal.

8.6 WASTE & POLLUTION MANAGEMENT

An integrated waste management approach based on waste minimization (e.g. reduction, recycling, re-use, and disposal) must be encouraged. Poor waste management can lead to adverse environmental impacts (e.g. odors, pollution, and visual impact) as well as health risks. Sound waste management is thus non-negotiable.

- No on-site burying or dumping of any waste materials, vegetation, litter, or refuse may be allowed.
- Domestic waste must be stored in approved containers (e.g. bins with removable lids).
- All solid waste will be disposed of at a landfill licensed in terms of section 20 of the Environment Conservation Act (Act No. 73 of 1989).

8.6.1 Recycling

Whenever possible, a suitable recycle arrangement must be negotiated with a local recycle agent to ensure the re-use of recyclable material. Recycling should aim at sorting as much of the following materials as practical:

- Paper and cardboard
- Aluminum
- Copper
- Metals (other than aluminum and copper)
- Glass
- Organic waste
- Batteries
- Electronic equipment

8.6.2 Pollution management

All possible pollution sources must be identified and all reasonable steps are taken to prevent pollution or accidental spillages.

- Ensure that all concentrated potential sources of pollution are protected (bunded) to minimize the risk of accidental spillage or pollution. Storage tanks should be bunded in such a way as to contain at least 120% of the storage tank's capacity.

8.7 SEWERAGE MANAGEMENT (NOT APPLICABLE)

If applicable sewerage must be installed in accordance with the Municipal regulations and Department of Water Affairs (DWA) requirements.

- Sewerage management must aim at the prevention of pollution and must be maintained regularly.
- Maintenance records must be kept.

8.8 FIRE MANAGEMENT

Refer to emergency preparedness and response paragraph 8.11.

8.9 MINIMISE DUST AND AIR EMISSIONS

Refer to erosion and sedimentation control paragraph 8.4.

8.10 MANAGEMENT OF NATURAL AREAS AND GARDENS

The objective regarding the management of natural areas and gardens are to identify critical or conservation-worthy features and to manage such areas and gardens in such a manner as to promote biodiversity and ecological processes.

- Natural areas must be managed as close to natural as possible (no interference wherever possible).
- No garden areas will be allowed.
- All listed invasive alien vegetation must be removed in accordance with CARA legislation (The Conservation of Agricultural Resources Act, 1983 (Act No. 43 of 1983)) as revised.

8.11 EMERGENCY PREPAREDNESS AND RESPONSE

The following potential emergency situations have been identified and include the procedure for responding to, and for preventing and mitigating the environmental impacts that may be associated with them.

8.11.1 Accidental fires

Fire safety in Fynbos Area is a very real risk and must be stringently controlled. No fires will be permitted on site for any reason. If required, a designated smoking area will be provided, and demarcated, and signposted, with a facility for safe containment and disposal of cigarette butts.

The following measures must be implemented:

- Adequate firefighting equipment must be available on-site and in good working order (including at least one type ABC (all purpose) 9 kg fire extinguisher and 3 fire beaters per working area). The persons on site must be trained in the use of such equipment.
- The main contractor must provide a list of all authorities involved in firefighting in the region. This list must include emergency contact numbers and must be visible at the site office.
- The contractors must establish an emergency procedure (with contact numbers) to the satisfaction of the ECO.

8.11.2 Hydrocarbon spills

Since the project is in proportion relatively small, no fuel storage or distribution facilities will be established. As a result, the significance of any spill is much reduced. The following must be observed:

- Vehicles will arrive on site already fuelled for the project. If additional fuel is needed, it will be brought in as needed (minimal volumes) and refueling will be done using a pump and not a funnel (to minimize the risk of spills). Spill trays shall be used during re-fuelling.
- In the case of accidental spillages or leakage, the client will be responsible for immediate containment and corrective action (e.g. stopping the leakage) and will be liable for any costs incurred.

9. DECOMMISSIONING EMP (DEMP)

The facility is expected to have a lifespan of 20+ years (i.e. with routine maintenance). The facility infrastructure would only be decommissioned and rehabilitated if it becomes outdated or inadequate, in which case the facility will normally be upgraded and not decommissioned.

It is thus considered unlikely that the facility will be decommissioned. However, it is likely that the facility will be upgraded or enlarged as part of maintenance and the replacement of individual components with more appropriate technology/infrastructure available at that time.

- **The relevant mitigation measures contained under the construction section should be applied during decommissioning and therefore are not repeated in this section.**
- Site preparation activities will include confirming the integrity of the access to the site to accommodate required equipment, preparation of the site (e.g. lay down areas, construction platform), and the mobilization of construction equipment.
- Disassembled components will be reused, recycled, or disposed of in accordance
- Specific consideration must be given to ways to minimize waste and wastage in maintenance and the decommissioning phase of the proposed development.
- Equipment used in the plant must be recycled and reused where possible to avoid the filling of already limited landfill space.
- Batteries must be re-used or recycled.

APPENDIX 1: DECLARATION OF UNDERSTANDING

DECLARATION OF UNDERSTANDING

I _____

Representing: _____

Declare that the conditions of the EMP were brought to my attention and that I have read and understood the contents of this Environmental Management Plan and that a copy of this EMP has been made available to me.

Site: _____

Date: _____

I also declare that I understand my responsibility in terms of enforcing and implementing the Environmental Specifications as set out in this Environmental Management Plan.

I also undertake to inform all persons under my supervision of these specifications and the contents of the Environmental Management Plan.

Signed: _____

Place: _____

Date: _____

Witness 1: _____

APPENDIX 2: START-UP REPORT

To be included after the start-up meeting.

APPENDIX 3: ENVIRONMENTAL EDUCATION

ENVIRONMENTAL TRAINING FOR CONSTRUCTION.

The why what and how...

BUT WHY...

... should we care about the environment?

The environment provides us with everything we need to survive – food, water, fuel, air, etc. The human activity uses resources and has an impact on those resources. Managing our resource use and ensuring that our impact is minimized will ensure that these resources are not depleted.

The Constitution says that all people in South Africa have the right to a healthy environment. If you damage the environment, you are taking away that basic right of others as well as future generations – your children and grandchildren!

...environmental management if there is already conservation?

Historically, development and environmental conservation have been in conflict, because conservation was understood as the protection of resources, and development as the use, or exploitation of resources. The two competed for the same resources, but both are needed! Enter: *SUSTAINABLE DEVELOPMENT*.

Sustainable development is development that meets the needs of the present without compromising the ability of future generations to meet their own needs.

Sustainable development thus aims to improve the quality of human life while living within our ecological means = the wise use of resources!

...environmental management of construction?

South Africa's effort to attain sustainable development is based on the concept of Integrated Environmental Management (IEM). The purpose of IEM is to resolve or lessen any negative environmental impacts and to enhance positive aspects of development.

IEM is designed to ensure that the environmental consequences of development proposals are understood and adequately considered in the planning, implementation and management of all developments.

It is intended to guide, rather than impede the development process by providing a method of gathering, analysing and utilising information about the environmental impacts of development. IEM and other principles of Environmental Management are set out in the National Environmental Management Act (No. 107 of 1998) & National Environmental Management Amendment Act (No. 62 of 2008)

BUT WHAT...

...exactly is the 'environment'? What if we're not working near rivers or fynbos or leopard toad habitat?

The environment is not only the 'conservation-worthy' such as rare plants and endangered animals. The environment is everything around you!

It is made up of living things (e.g. people, plants & animals) and non-living things (e.g. soil, water, buildings & cars). People and man-made things are also important parts of the environment.

Protection of the environment means that all living and non-living things are protected. During construction, Environmental Management Programmes (EMP's) are implemented not only to protect fynbos or leopard toads but also to protect people (both on site and off), property (houses, cars, etc.) as well as natural resources such as water, air and soil.

...do Environmental Management Programmes (EMP's) do? What does this mean for my contract?

EMPs are tools to facilitate environmental management during the construction phase of development projects and thereby avoid *unnecessary* impacts to the environment.

In the past, the functionality and efficiency of EMPs was hampered by resistance from contractors and engineers, the difficulties of costing for compliance and the lack of legal enforceability.

Now Environmental Management Programmes (EMP's) are stipulated in the Environmental Authorisations (ROD) as a condition of the approval to go ahead with the development, in other words it is legally binding.

When you sign a contract do work on a project with an EMP, you are legally bound to comply with that EMP!

Methods of implementing EMPs are becoming more and more stringent and issues of enforceability are being addressed. Those individuals and companies that are familiar with compliance with EMPs will be at a competitive advantage!

...do EMPs consist of?

EMPs usually contain an environmental policy statement, organisational structure detailing the responsibilities and authorities involved in the project, procedures for communication and record-keeping and environmental specifications.

EMPs are adapted to the scale and sensitivity of the construction project. They can be thick documents detailing specifications for every eventuality specifically adapted to the project, or they can be short and brief documents setting out standard environmental procedures and controls. Sometimes EMPs include extensive penalty and incentive schemes.

A WORD ON METHOD STATEMENTS:

A method statement can be requested or proposed when an activity is either not included in the EMP at all, if the EMP specifications for an activity are not deemed adequate, if an activity is required that is not allowed by the EMP, etc. In other words, when the EMP does not give enough information to manage the environmental impact of a specific activity.

A method statement is defined as a written submission by the Contractor setting out the plant, materials, labour and method proposed to carry out an activity. Method statements must provide enough detail that the environmental impact of the activity can be assessed. Method statements must therefore be submitted well in advance of the activity (usually at least 5 days but sometimes more).

Method statements are therefore an extension of the EMP, are also legally binding and are intended to ensure that the environmental implications of an activity outside of the EMP can be addressed.

Method statements usually require the approval by the engineer, the ECO/ESO/DEO, etc. before the activity can take place. If such an activity takes place without approval and results in environmental damage, the contractor is responsible for the cost of rehabilitation/clean-up/etc.

...is an ECO, ESO, DEO, etc.?

EMPs usually require the appointment of an ECO, ESO, DEO, etc. to oversee the implementation of and compliance with the EMP on behalf of the engineer or the contractor(s). Ultimate responsibility for compliance with the EMP lies with the contractor(s) and the engineer.

ESO = Environmental Site Officer – usually on site permanently or often. Can be independent consultant or from contractor/engineer.

ECO = Environmental Control Officer – usually visits site on a regular basis and audits compliance with the EMP. Usually independent consultant.

DEO = Designated Environmental Officer – usually on site permanently, usually member of contractor or engineer site staff.

Organisational structures and responsibilities differ from project to project and depend on environmental sensitivity of the project, scale of the project, etc. Increasingly nowadays, each party is required to appoint their own person responsible for environmental management on site, e.g. the engineer would have an ESO/ECO and the main contractor(s) would have an ESO/DEO etc.

It is therefore important to familiarise yourself with that part of the EMP that deals with organisation and responsibilities for each contract that you are involved in.

BUT HOW...

...do EMPs promote sustainable development?

They don't!

It is the people on site that protect the environment. The EMP, like any other plan or policy, is not worth anything if there isn't a commitment from those working on the project to compliance with the EMP.

...can I ensure my work comply with the EMP?

Environmental specifications in different EMPs can vary from vague to very detailed.

- Firstly, it is obviously important to know what those specifications are, vague or not, so **READ THE DOCUMENT!** Ignorance does not absolve you from your responsibility. A copy of the EMP must be kept at the site office at all times.
- It also helps to understand **WHY** those specifications are there – some things are obvious but others may not be. Some EMPs may have specifications that are not relevant. Don't be afraid to question the EMP; it can only increase its efficiency!
- Know where the sensitive areas on site are – watercourses, wetland areas, residential areas, etc. – and be extra vigilant when working in these areas.

Mostly environmental management of construction activities and compliance with EMPs require only common sense and with good housekeeping the battle is half won!

The enclosed environmental hand-out sets out the standard environmental specifications

DO'S AND DON'TS (1)

**Workers & equipment must stay inside the site boundaries at all times.
Nobody may enter areas marked as No-go areas.**

Why? Construction activities, equipment and people cause damage and disturbance to the area surrounding the site. As small an area as possible will be affected if all workers and equipment stay within the site boundaries. This is especially important if there are people who live around the site or natural areas around the site which should not be disturbed.



**Do not swim in or drink from streams.
Do not throw oil, petrol, diesel, concrete or rubbish in streams.
Do not work in the stream without direct instruction.
Do not damage the banks or plants of streams.**

Why? River water may be polluted which could make you sick.
Oil, petrol, diesel, concrete or rubbish will kill plants and animals living in the water. They may also make people who may drink the water downstream sick. Rubbish in the stream also makes it look ugly.
People and machinery working in the stream will damage it and kill plants and animals living in the stream. It may also cause erosion, which is expensive to repair.
The plants on the edge of the stream bind the soil together and prevent soil from getting washed away. Soil washed into a stream may affect people using the water downstream (e.g. for irrigation).



**Protect animals on the site.
Ask your supervisor to remove animals found on site.**

Why? Animals are an important part of the environment. All animals have a purpose, even snakes which catch mice and rats. Other important animals are owls, chameleons and frogs.



**Do not damage or cut down any trees or plants without permission.
Do not pick flowers.**

Why? Some plants are rare and may take a long time to grow back, if at all. Plants in the “no go” areas should not be damaged.
Some plants will die if their flowers are picked. Rare plants may be lost.



**Put cigarette butts in a rubbish bin.
Do not smoke near gas, paints or petrol.
Do not light any fires without permission.
Know the positions of firefighting equipment.
Report all fires.
Do not burn rubbish/ vegetation without permission.**

Why? Leaving a burning cigarette butt on the ground may lead to runaway fires which are dangerous to construction workers, people living around the site, equipment, houses, plants and animals.
Smoking near flammable material is dangerous and may cause an explosion.
Lighting a fire without permission may cause a runaway fire (see above).
Reacting quickly to fires that break out will prevent them from spreading and causing damage.

DO'S AND DON'TS (2)



Work with petrol, oil & diesel only in designated areas.
Report any petrol, oil & diesel leaks or spills.
Use a drip tray under vehicles & machinery.
Empty drip trays after rain & throw away were instructed.

Why? Designated areas should have measures to protect against petrol, oil & diesel spills. Oil, petrol and diesel can drip onto the soil and soak into it. Plants will not grow and animals will not live in dirty soil. It also looks ugly to people living around the area.

Drip trays will prevent oil, petrol or diesel from soaking into the soil and killing plants and animals.

If drip trays are not emptied they may overflow and pollute the surrounding soil. If oil, petrol or diesel is put into a stream, plants and animals living in the stream will be killed. They may also make people who may drink the water downstream sick. Ask your supervisor where drip tray water may be disposed of on site.



Try to avoid producing dust – wet dry ground and stockpiles.

Why? Dust can be irritating to people and can reduce production on site. It can cause problems such as eye irritations and coughs. It also reduces visibility on and around the site, which can be dangerous to drivers and pedestrians, and can cause damage to the surrounding environment.

Soil should not be made too wet because that will cause safety problems and soil may be washed away.



Do not make loud noises around the site, especially near schools and homes.
Report or repair noisy vehicles.

Why? Loud noises are irritating to workers and people living around the site. Loud noise can also be harmful to people (especially children) and affect their hearing.

By keeping vehicles in good condition, loud noise can be prevented.



Use the toilets provided.
Report full or leaking toilets.

Why? Sewage attracts flies and other irritating pests. If the site is near a river or stream, sewage makes the water smell and people who swim in it or use it to wash their clothes will get sick. It also causes plants to grow too much which blocks the river, which may cause flooding of houses and property.

Regular emptying of toilets is hygienic and will also prevent overflows.



Make sure that you eat where there is a rubbish bin nearby.
Never eat near a river or stream.
Put packaging & leftover food into rubbish bins.

Why? Eating areas generate a lot of rubbish and litter (e.g. bottles and packets) which will pollute the site and surrounding areas. Therefore, eating must be done near bins which are placed in the eating.

Rubbish in a stream looks ugly and can be harmful to people's health. It may also kill the plants and animals living in the stream. Rubbish and food left lying around will attract pests (such as rats) which are

dangerous to people and cause a health hazard. Also, rubbish left lying around is ugly and unpleasant to look at.



Do not litter—put all rubbish (especially cement bags) into the bins provided.
Ask your supervisor for a bin if there is none. Bins must be provided.
Report full bins to your supervisor.
The responsible person should empty bins regularly.

Why? Litter is ugly. It is also dangerous and unhealthy to adults, children and animals walking around the area.
Not putting the lid back on the bin will cause rubbish to be blown away.
Regularly emptying bins will prevent litter and rubbish flying around the site.



Always keep to the speed limit.
Drivers - check & report leaks.
Ensure loads are secure & do not spill.

Why? Speeding is dangerous to people who live in the area, especially children. Speed kills!
Faulty vehicles are dangerous to the driver, pedestrians and other motorists. Leaks can also pollute the ground and water and smoke from vehicles can cause health problems.
This is a potential danger to other motorists. Also, do not overload vehicles.



Know all the emergency phone numbers.

Why? Prompt reaction to an accident, fire or spill will reduce the risk of serious damage to the environment and to workers.



If rules are broken:
- Spot fines
- Removal from site.
- Construction may be stopped.

Why? Failure to adhere to the EMP may result in spot fines being issued to the company. It is then the Site Agent's responsibility to collect these fines from guilty individuals and he may even deduct fines off your wages.

The fines are meant to act as an incentive for workers to take the EMP seriously.

A person may be removed from site if they continually disregard the specifications in the EMP.

If the EMP is not adhered to, the local Environmental Authority may stop construction.



Report any breaks, floods, fires, leaks and injuries to your supervisor.

Ask questions!

Thank you for your attention.

APPENDIX 4: BASIC RULES OF CONDUCT

BASIC RULES OF CONDUCT

The following list represents the basic Do's and Don'ts towards environmental awareness, which all participants in this project must consider whilst carrying out their tasks. These are not exhaustive and serve as a quick reference aid.

NOTE: ALL new site personnel must attend an environmental awareness presentation. Please inform your foreman or manager if you have not attended such a presentation or contact the ESO.

DO:

- Use the toilet facilities provided – report dirty or full facilities
- Clear your work areas of litter and building rubbish at the end of each day – use the waste bins provided and ensure that litter will not blow away.
- Report all fuel or oil spills immediately & stop the spill continuing.
- Dispose of cigarettes and matches carefully. (Littering is an offence.)
- Confine work and storage of equipment to within the immediate work area.
- Use all safety equipment and comply with all safety procedures.
- Prevent contamination or pollution of streams and water channels.
- Ensure a working fire extinguisher is immediately at hand if any “hot work” is undertaken e.g. welding, grinding, gas cutting etc.
- Report any injury of an animal.
- Drive on designated routes only.
- Prevent excessive dust and noise.

Do not:

- Remove or damage vegetation without direct instruction.
- Make any fires.
- Injure, trap, feed or harm any animals – this includes birds, frogs, snakes, lizards etc.
- Enter any fenced off or marked area.
- Allow cement or cement bags to blow around.
- Speed or drive recklessly
- Allow waste, litter, oils or foreign materials into the stream
- Swim in the dam.
- Litter or leave food laying around

Notes:

If any animals such as tortoises, chameleons or snakes be encountered then do not harm them. The ECO or Site Supervisor must be contacted to remove these safely. The harming of any animal will result in disciplinary action.

Construction and heavy machine operators must be particularly sensitive to staying within access routes and prevention of unnecessary damage. Dust and noise is also of particular concern. Ensure that vehicles and machinery do not leak fuel or oils. Refuelling or maintenance must be done within the maintenance camp area only.

Alien plant clearing and control work teams must be closely supervised.

BASIESE GEDRAGSKODES

Die volgende lys verteenwoordig die moets en moenies vir omgewingsbewustheid wat alle deelnemers aan hierdie projek in ag moet neem tydens die uitvoer van hul take. Hierdie lys is nie volledig nie en dien slegs as 'n vinnige verwysing.

Nota: alle nuwe terreinpersoneel moet 'n aanbieding ten opsigte van omgewingsbewustheid bywoon. Indien u nog nie so 'n aanbieding bygewoon het nie, lig asseblief u voorman of bestuurder in of kontak die omgewings terreinbeampste.

Moets:

- Gebruik die beskikbare toilet-geriewe – rapporteer vuil of vol geriewe.
- Maak u werkplek skoon van rommel of bourommel aan die einde van elke dag – gebruik beskikbare vullisdromme en verseker dat rommel nie rondwaai nie.
- Rapporteer alle brandstof- en olie stortings onmiddellik – stop verdere storting.
- Wees versigtig met die wegdoen van sigarette en vuurhoutjies. (rommelstrooi is 'n oortreding.)
- Beperk werkaktiwiteite en die stoor van toerusting tot die onmiddellike werkarea.
- Gebruik veiligheidstoerusting en voldoen aan alle veiligheids-maatreëls.
- Voorkom besoedeling van strome en waterbane
- Verseker dat 'n brandblusser in werkende toestand byderhand is wanneer “warm” werk verrig word bv. Sweis, wegslyp, gasny, ens.
- Rapporteer beseerde diere.
- Ry slegs op aangewese roetes.
- Voorkom oormatige stof en geraas.

Moenie:

- Plantegroei verwyder of beskadig sonder direkte instruksie nie.
- Enige vure maak nie.
- Enige diere dood, beseer, vang of voer nie, insluitende voëls, paddas, slange, akkedisse, ens.
- Enige omheinde of afgesperde areas binnetree nie.
- Sement of sementsakke laat rondwaai nie.
- Vinnig of roekeloos bestuur nie.
- Enige rommel, afval, olie of enige vreemde materiaal in strome laat beland nie.
- In die dam swem nie.
- Rommelstrooi of kos laat rondlê nie.

Notas:

Indien enige diere soos skilpaaie, verkleurmannetjies of slange teëgekom word, moet hulle nie beseer of dood nie. Kontak die otb of ri om hulle veilig te verwyder. Die besering van diere sal lei tot dissiplinêre optrede.

Operateurs van konstruksie- en swaar masjiene moet veral versigtig wees om binne toegangsroetes te bly en om enige onnodige skade te voorkom. Verseker dat voertuie en masjiene nie olie of brandstof lek nie. Brandstofaanvulling en voertuigonderhoud mag slegs binne die onderhoudsarea gedoen word.

Streng toesig moet gehou word oor indringerplantbeheerspanne.

EZIPPHAMBILI EKUNYANZELEKILEYO UKUBA ZENZIWE

Zonke ezi zinto zilandelayo zizinto ekufuneka zenziwe nekufuneka zingenziwanga.

Wonke umntu ofikayo kufuneka afundiswe ngemigaqo kupala. Needa yazisa iforman yakho ikuba awukhange uye kufundiswa.

Izinto emazenziwe

- Sebenzisa izindlu zangasese, yazisa xa kukho umonakalo.
- Zama ukucoca apho ubusebenza khona.
- Sebenzisa imigqomo yenkukuma ungayeki iphaphtieke.
- Yazisa xa ubona ioil echithskalayo okanye ipetrol.
- Cima lozoli cigarette xa ugqibibile ukutshaya
- Zonke izixhobo usebenza zibuyisele apho zihlaka khona xa ucgibile apho zihlala khona xa ugqibile ukuzisebenzisa.
- Zisebenzise izikhuselixa uzinkiwe.
- Sukugalela izinto emlanjeni.
- Masibekho isicima mlilo xausebenza ngomlilo.
- Yazisa msinyane xa ubone isilwanyana ezonzakeleyo.
- Xauqhuba isithuthi hamba endleleni qha ungafathulinje.
- Naphina zamaungenzi thuli okanye ingxolo xa usebenza.

Emazingenziwa

- Sukususa nesiphina isityalo ungakhange uxelelwe
- Sukwenza mlilo nokuba sekubanda
- Amagqara ukubulala izilwanyana nokuzifida akuvumelekanga
- Sukungena xa kuvaliwe ngaphandle kwe mvume
- Ingxowa zesamente mazincedwe zingahlwa nje
- Sukuqhuba ngesantya esiphakamileyo
- Sukugalele nayiphi into phaya emlanjeni
- Sukuqubha edameni q oqosha yonk inkukuma

APPENDIX 5: PENALTIES FOR NON-COMPLIANCE

PENALTIES FOR NON-COMPLIANCE

The contractors / sub-contractors must contact the ECO at any stage if unsure about any matter, or if a pollution incident occurs, or vegetation or animals are damaged.

ECO = Environmental Control Officer ESO= Environmental Site Officer

PHASE	Penalty for Non-compliance	
	Bottom range	Top Range*
PRE-CONSTRUCTION PHASE		
Construction area to be marked off before construction starts.		5000
The demarcated area must be maintained throughout the construction phase	500	1000
Site area for stock piling of building material must be demarcated	500	5000
Site area for storing of waste material must be demarcated	500	5000
Fencing off the construction site with mesh fencing of 1.8m, where necessary or other suitable material as agreed on by ECO	500	1000
Sitting of access road/s to be approved by ECO & demarcated with stakes before any construction starts (if applicable)		5000
Temporary route used for construction must be determined on site with ECO (if applicable)	1000	5000
Telecommunications & AC power routes must be determined with the ECO (if applicable)	1000	5000
Sensitive features that may be harmed must be clearly marked or demarcated.	500	2000
Vegetation that may not be removed must be clearly marked or demarcated.	500	5000
Contractor must make the Construction team and all sub-contractors aware of all environmental aspects that could lead to imposition of penalties	100	5000
Contractor to sign Declaration of understanding (DOU) before construction starts		5000
Contractor to assure that all subcontractors be informed and signed DOU	1000	5000
Method statements must be provided on request by the ECO. No work may commence until the Method Statement is accepted by the ECO and Engineer	1000	5000
CONSTRUCTION PHASE		
Information		
A copy of the EMP & Record of Decision with all the conditions of approval, and the relevant Method Statements must be at site at all times.	200	5000
Construction crew behaviour		

Construction crews may not overnight on site.	200	5000
No amplified music allowed on site	100	200
Construction crew must stay within the demarcated construction area. (Applicable in sensitive sites)	50	500
Eating of meals only allowed in demarcated area	50	500
No pets permitted on site		100
Driving, Parking & Storing of machinery and vehicles are only allowed inside demarcated areas and existing roads	1000	5000
Machinery may only be used on the road and may not disturb the vegetation on the sides of the road except if cleared by ECO. Machinery used must be carefully considered to limit environmental damage	500	5000
No vegetation other than that agreed on may be damaged - i.e. no access to areas outside construction area.	500	2000
No individual may cause unnecessary damage to flora and fauna on, around or near the site	20	2000
No littering allowed (incl. cigarette butts)	50	500
Excavations		
No topsoil may be removed or altered outside the demarcated area and/or which was not specified.		2000
Commercial sources of sand, rock and gravel to be cleared with ECO	200	5000
All surplus material to be taken off-site and be disposed of at approved site	500	5000
Toilets		
Sufficient ablution facilities must be provided		3000
Toilets to be secured to prevent them from falling or blowing over.	100	1000
They must be serviced regularly, (according to the manufacturer's instructions) and kept clean.	100	1000
Everybody on site must make use of ablution facilities	50	1000
Fire Prevention		
All mandatory firefighting equipment (as specified at start-up) must be on site at all times	500	4000
Firefighting equipment to be in good working order and serviced.	500	2000
No fires, including cooking fires, allowed on site	1000	5000
Cement		

Concrete may only be mixed within the boundaries of the demarcated area and/or where was agreed on by the ECO.	500	5000
All excess cement & concrete mixes to be contained on construction site prior to disposal off site	200	5000
Any cement / concrete spillage to be cleaned up immediately.	500	5000
Ready-mix delivery trucks must not carry out the wash down of their trucks on or around the site unless arranged with ECO.	1000	3000
Dust pollution control		
Ensure that loose building material is covered to prevent dust pollution	100	1000
Water run-off		
Contamination of water bodies, rivers, dams or wetlands must be prevented at all cost	500	5000
Rainwater from construction & building site/s must be channelled, contained & allowed to dry out, so as not to transport any pollutants into the surrounding area. Temporary trenches, straw stabilising, brush cutting can be used	500	5000
Waste control		
Sufficient refuse bins must be placed on site	500	2000
Refuse bins must be cleaned on a regular basis	100	1000
General litter / building refuse must be cleaned up on a regular basis from the site	500	3000
Cement-contaminated water; paint; oil; cement slurries etc. must be stored in watertight containers or as agreed with ECO	500	5000
Store all refuse & waste material in wind & animal proof containers	100	1000
Waste must be disposed of at an official waste deposit site on a regular basis.	500	5000
The absence of or inadequate drip trays or bunding facilities	500	5000
Failure to address oil/fuel leaks from on-site machinery	200	5000
Herbicides		
No herbicides or pesticides whatsoever may be used.	200	2000
Construction road		
Road must be upgraded to prevent degradation and erosion of the road and surrounds.	500	5000
Power and Telecommunications supply		
Demarcate power supply route	500	5000

No vehicles to drive through vegetation unless authorised by ECO	500	5000
Storage of equipment may only take place at an area demarcated by the ECO.	500	5000
Working must be done in phases to prevent trampling of vegetation	N/A	
Use of generators and fuel powered equipment		
A watertight cover must be place under the power generator equipment to prevent accidental spillage of fuel & oil seeping into the soil.	500	5000
Drip tray must be able to take 120% of fuel on site	500	5000
All waste material generated from the use of this equipment must be contained and removed from the site	500	5000
Mobile fuel powered equipment must be well maintained and must not have any fuel or oil leaks.	200	5000
Soil Stabilisation		
Ensure that soil material for filling and stabilisation comes from a source that does not contain seeds alien to the area. The source must be cleared with the ECO.	100	2000
Rehabilitation		
Remove rocks and stones and stock pile in area recommended by ECO	500	5000
Remove all plants that can be used for rehabilitation and store on- or off-site in appropriate manner as agreed with ECO	200	5000
Removal of all old concrete and alien materials from site	500	5000
Site must be cleared of all waste and building material	500	5000

*(Large scale / repeated offence)

APPENDIX 6: INFO ON METHOD STATEMENTS

INFORMATION ON METHOD STATEMENT

Method Statements are to be completed by the person undertaking the work (i.e. the Contractor). The Method Statement will enable the potential negative environmental impacts associated with the proposed activity to be assessed.

The Method Statement can only be implemented once approved by the ECO

The Contractor (and, where relevant, any sub-contractors) must also sign the Method Statement, thereby indicating that the works will be carried out according to the methodology contained in the approved Method Statement.

The ECO will use the Method Statement to audit compliance by the Contractor with the requirements of the approved Method Statement.

Changes to the way the works are to be carried out must be reflected by amendments to the original approved Method Statement; amendments require the signature of the ECO denoting that the changed methodology or works are necessary for the successful completion of the works, and are environmentally acceptable. The Contractor will also be required to sign the amended Method Statement thereby committing him/herself to the amended Method Statement.

This Method Statement **MUST** contain sufficient information and detail to enable the ECO to apply their minds to the potential impacts of the works on the environment. The Contractor will also need to thoroughly understand what is required of him/her to undertake the works.

THE TIME TAKEN TO PROVIDE A THOROUGH, DETAILED METHOD STATEMENT IS TIME WELL SPENT. INSUFFICIENT DETAIL WILL RESULT IN DELAYS TO THE WORKS WHILE THE METHOD STATEMENT IS REWRITTEN TO THE ER'S AND ESO'S SATISFACTION.

The page overleaf provides a *pro forma* method statement sheet, which needs to be completed for each activity requiring a method statement in terms of the EMP.

APPENDIX 7: EXAMPLE OF METHOD STATEMENT

PRO-FORMA METHOD STATEMENT

CONTRACT:..... **DATE:**.....

PROPOSED ACTIVITY (give title of method statement and reference number):

--

WHAT WORK IS TO BE UNDERTAKEN (give a brief description of the works):

--

WHERE ARE THE WORKS TO BE UNDERTAKEN (where possible, provide an annotated plan and a full description of the extent of the works):

--

START AND END DATE OF THE WORKS FOR WHICH THE METHOD STATEMENT IS REQUIRED:

Start Date:

End Date:

HOW ARE THE WORKS TO BE UNDERTAKEN (provide as much detail as possible, including annotated maps and plans where possible):

Note: please attach extra pages if more space is required

--

DECLARATIONS

1) ENVIRONMENTAL CONSULTANT AND/OR ENVIRONMENTAL CONTROL OFFICER

The work described in this Method Statement, if carried out according to the methodology described, is satisfactorily mitigated to prevent avoidable environmental harm:

(Signed) (Print name)

(Signed) (Print name)

Dated: _____

2) PERSON UNDERTAKING THE WORKS

I understand the contents of this Method Statement and the scope of the works required of me. I further understand that this Method Statement may be amended on application to other signatories and that the ESO will audit my compliance with the contents of this Method Statement

(Signed) (Print name)

Dated: _____

3) THE APPLICANT

The works described in this Method Statement are approved.

(Signed) (Print name) (Designation)

Dated: _____

APPENDIX 8: CONTRACTOR ENVIRONMENTAL CHECKLIST

CONTRACTOR/S REPRESENTATIVE: ENVIRONMENTAL WEEKLY CHECKLIST

SITE: _____

PHASE OF WORK AND % OF COMPLETION: _____

ENVIRONMENTAL ASPECT	YES/ NO (✓ or X)	COMMENTS
How many workers are on site		
All new personnel on site are aware of the contents of the EMP and have been through the environmental awareness course.		
Contractor's camp is neat and tidy and the labourers' facilities are of an acceptable standard.		
Sufficient and appropriate firefighting equipment is visible and readily available.		
Waste control and removal system is being maintained.		
Refuse bins in place and maintained		
Toilets are in place and clean		
Demarcation and other fences are being maintained.		
What machinery are on site		
Drip trays are being utilised where there is a risk of incidental spillage		
Bunds/ drip trays are being emptied on a regular basis (especially after rain).		
No leakages (oil & fuel) are visible from construction vehicles		
No go areas, remaining natural features and trees have not been damaged.		
Dust control measures (if necessary) are in place and are effectively controlling dust.		
Noise Control measures (if necessary) is in place and is working effectively.		
Erosion control measures (if necessary) are in place and are effective in controlling erosion. (Access road, site areas etc.)		
Stockpiles are located within the boundary of the site, do not exceed 2 m in height and are protected from erosion.		

Completed by:..... Sign:..... Date:.....

To be submitted at the end of each week to the Environmental Site Officer (ESO)

Received by:

Environmental Site Officer: :..... Sign:

Date:.....

APPENDIX 9: ECO/ESO REPORT/CHECKLIST

ECO CONSTRUCTION SITE ENVIRONMENTAL INSPECTION REPORT

Project Name: _____

Report no _____

Main Contractor: _____

Date _____

ECO: _____

EnviroAfrica Ref. no. _____

ENVIRONMENTAL ASPECT	RATING	FINDINGS & RECOMMENDATIONS
RATING: 1 = EXTREMELY POOR 2 = POOR 3 = AVERAGE 4 = GOOD 5 = EXCELLENT		
1. DEMARCATION Boundaries of “no go” areas, construction sites, -offices, temporary storage areas as well as labourer’s facilities must be demarcated (EMP and ECO requirements) and maintained for the length of the construction period.		
2. NO-GO AREAS Identified “No-Go Areas”, must be demarcated for protection from construction damage (including secondary impact). <ul style="list-style-type: none"> • All areas outside of the demarcated construction site(s) and access road(s) to be regarded as NO-GO areas, including remaining natural veld identified trees. • Special attention to identified areas with significant vegetation. 		
3. SEARCH & RESCUE All flora identified for search & rescue must be removed before any construction take place and re-used in pre-approved way.		
4. VEGETATION & TOPSOIL REMOVAL Before any construction or earthworks, topsoil must be stripped (>150mm) and stockpiled for rehabilitation/ landscaping. Stockpiles: <ul style="list-style-type: none"> • must be protected (erosion) and stored separately. • may not be moved further than 50m or mixed with any other soil. • must be convex and should not exceed 2m in height. In addition: <ul style="list-style-type: none"> • Cleared areas must be stabilized. • Burning or burying of cleared vegetation is prohibited (may be used for mulch or slope stabilisation on site). 		
5. CONSTRUCTION CAMP & SITE OFFICES Must be demarcated, organised and free of day-to-day litter (good housekeeping standards).		

ENVIRONMENTAL ASPECT	RATING	FINDINGS & RECOMMENDATIONS
RATING: 1 = EXTREMELY POOR 2 = POOR 3 = AVERAGE 4 = GOOD 5 = EXCELLENT		
6. LABOURER'S FACILITIES Facilities must be of acceptable standards suitably demarcated, well maintained, neat and tidy and with adequate ablution facilities.		
7. ENTRANCE AND HAUL ROADS Only approved entrance and haul roads may be used. No new roads or parking areas may be developed without written approval from the ECO.		
8. MANDATORY SITE EQUIPMENT Mandatory site equipment must be in place, well maintained and in accordance with EMP and ECO requirements. <ul style="list-style-type: none"> • Sufficient refuse bins, well placed and cleaned regularly. • Sufficient fire extinguishers, readily available, maintained and functional. • Drip trays must be used at all fuel and oil storage and refuelling sites. • Toilets and sanitation facilities must be kept clean neat and hygienic. 		
9. FUEL STORAGE Fuel storage areas must be situated within the demarcated construction camp site (or an area approved by the ECO). <ul style="list-style-type: none"> • Larger containers must be bunded (containment of accidental spillages). • Drip trays must be used during refuelling or under stationary refuelling vehicles. • Fuel and oil storage and refuelling sites must be maintained. 		
10. STOCKPILING & TEMPORARY STORAGE May only be placed on pre-approved sites, demarcated, stabilised or organised and neat.		
11. WASTE CONTROL The contractor is expected to control all construction related waste material and general litter on actual construction sites and its immediate surroundings. <ul style="list-style-type: none"> • Waste management must be in accordance with the EMP, of acceptable standards, with regular removal of general waste, hazardous waste as well as construction waste (e.g. concrete waste and spoil). 		
12. CEMENT MIXING & BATCHING AREAS Mixing areas must be approved by the ECO, suitably demarcated and may not result in pollution. <ul style="list-style-type: none"> • Polluted cement water may only be released into sedimentation ponds. 		

ENVIRONMENTAL ASPECT	RATING	FINDINGS & RECOMMENDATIONS
RATING: 1 = EXTREMELY POOR 2 = POOR 3 = AVERAGE 4 = GOOD 5 = EXCELLENT		
<ul style="list-style-type: none"> Sedimentation ponds must be maintained and cleaned regularly (and reinstated after use). 		
13. CONSTRUCTION VEHICLE MAINTENANCE Construction vehicles must be in good working order and well maintained to prevent oil and fuel leakages and to reduce noise levels.		
14. HEAVY EARTHMOVING EQUIPMENT Construction vehicles and equipment may only operate <u>within</u> the demarcated site boundaries (and approved access roads), especially heavy earthmoving vehicles.		
15. DUST CONTROL Adequate control measures must be in place to prevent dust nuisance or pollution (entrance-, haul roads and exposed surfaces). <ul style="list-style-type: none"> Areas of concern must be watered regularly during construction AND periods of strong winds, BUT must take water saving into account. 		
16. EROSION CONTROL Erosion resulting from works must be controlled. <ul style="list-style-type: none"> Temporary and permanent drainage areas must be maintained. Erosion damage and damage in drainage courses must be reinstated. 		
17. NOISE CONTROL Effective noise control measures must be in place and acceptable working hours must be kept (deviations must be approval by the ECO).		
18. ARCHAEOLOGICAL & HERITAGE FINDS Should any archaeological or heritage remains be exposed during excavations or any activity on site, these must immediately reported to The site agent/engineer, the ECO HWC or SAHRA.		
19. METHOD STATEMENTS Method statements must be submitted and approved before commencement of the works. Possibly Required: <ol style="list-style-type: none"> Demarcation & No-Go Areas (Map) Clearing of vegetation & topsoil conservation Stockpiling & temporary storage Construction camp & site offices Labourer's facilities Mandatory site equipment 		

ENVIRONMENTAL ASPECT		RATING	FINDINGS & RECOMMENDATIONS
RATING: 1 = EXTREMELY POOR 2 = POOR		3 = AVERAGE	4 = GOOD 5 = EXCELLENT
7. Fuel storage 8. Entrance & haul roads 9. Waste management 10. Cement/Concrete mixing 11. Dust control 12. Erosion control 13. Noise control 14. Rehabilitation Additional Method Statements			
20. ENVIRONMENTAL CONDUCT Environmental conduct of construction personnel must be acceptable (e.g. no burning or burying of refuse; no littering and no cement bags or other construction waste material lying around).			
21. ENVIRONMENTAL CHECKLIST The contractor must ensure that the weekly environmental checklist is completed at the end of each week and it must be available at the site offices.			
22. REHABILITATION On completion of the project or phase, all areas impacted by the construction activities must be reinstated and/or rehabilitated to the satisfaction of the ECO with emphasis on the following: <ul style="list-style-type: none"> • Site offices must be removed and the areas rehabilitated or reinstated to the satisfaction of the ECO. • Labourer's facilities must be removed and the areas rehabilitated or reinstated to the satisfaction of the ECO. • All construction site areas must be rehabilitated or reinstated to the satisfaction of the ECO. • All temporary fencing and demarcation must be removed and the areas reinstated to the satisfaction of the ECO. • Temporary storage areas must be rehabilitated or reinstated to the satisfaction of the ECO. • All remaining construction material must be removed and the areas rehabilitated or reinstated to the satisfaction of the ECO. • Any additional disturbed areas must be rehabilitated or reinstated to the satisfaction of the ECO. 			
23. SPOT FINES & PENALTIES			

ENVIRONMENTAL ASPECT	RATING	FINDINGS & RECOMMENDATIONS
RATING: 1 = EXTREMELY POOR 2 = POOR 3 = AVERAGE 4 = GOOD 5 = EXCELLENT		
Spot fines and penalties must be recorded and documented by the ECO (in accordance with the EMP).		
24. FIXED POINT PHOTOS Photographs must be taken by the ECO, Site Engineer and or Site Manager, prior to, during and immediately after construction as visual reference. These photographs must be stored with other records relating to the EMP.		

ECO COMMENTS

[illegible]

End of report

ECO Signature

APPENDIX 10: Environmental incident report format
--

ENVIRONMENTAL INCIDENT REPORT

No. _____

PROJECT NAME			
PROJECT LOCATION			
SITE AGENT			
DATE OF INCIDENT		TIME	
BRIEF DESCRIPTION AND CAUSE OF INCIDENT:			
WHAT IMMEDIATE ACTIONS / CONTROL MEASURES WERE TAKEN:			
WHAT CORRECTIVE ACTIONS WERE TAKEN TO ENSURE NO REPEATS OF THE INCIDENT:			
ECO/ESO RESPONSE TO INCIDENT AND RECOMMENDATIONS:			
IS THIS INCIDENT A: <input type="checkbox"/> FIRST OFFENCE <input type="checkbox"/> SECOND OFFENCE <input type="checkbox"/> THIRD OFFENCE			
SIGNATURE OF SITE AGENT: _____		DATE _____	
SIGNATURE OF ECO/ESO _____		DATE _____	
REMEMBER TO BE FACTUAL WHEN DESCRIBING THE INCIDENT			

APPENDIX 11: Environmental complaints register

COMPLAINTS REGISTER FORM

(To be completed by Site Agent/Supervisor)

[illegible]

APPENDIX 12: Method statement register

METHOD STATEMENT REGISTER		SITE AGENT:				PROJECT NAME:			
		CONTRACTOR:				PROJECT LOCATION:			
No.	METHOD STATEMENT ACTIVITY REFERENCE	DATE CREATED	DATE RECEIVED	CREATED BY		ACCEPTED / REJECTED		DATE APPROVED	APPROVED BY
1	Demarcation								
2	Clearing of vegetation and topsoil removal								
3	Stockpiling								
4	Temporary storage facilities								
5	Construction camp and site offices								
6	Fuel storage								
7	Labourer's facilities								
8	Entrance and haul roads								
9	Mandatory site equipment								
10	Waste management/control								
11	Cement mixing and batching areas								
12	Construction vehicle maintenance								
13	Dust control								
14	Erosion control								
15	Noise control								
16	Archaeological and heritage finds								
17	Rehabilitation								
18									

19	<u>Additional MS (Waste Licence requirements)</u>						
20							
21							
22							
23							
24							
25							
26							
27							
28							
29							
30							

APPENDIX 13: Maps & Drawings

APPENDIX 14: Specialist studies

APPENDIX 15: Proof of compliance

APPENDIX 16: EAP CVs
