

ENVIRONMENTAL MANAGEMENT PROGRAMME (EMPr)

for the management of activities relating to the protection of the natural environment during the construction, operation and decommissioning phases of the

ELECTRIC VEHICLE CHARGING STATION AND SOLAR PV FACILITY



DECEMBER 2024

Compiled by:

EnviroAfrica cc

TABLE OF CONTENTS

1. INTRODUCTION	5
1.1.1 PURPOSE	6
1.1.2 SCOPE.....	6
1.2 SITE LOCATION.....	6
1.2.1 PROJECT DESCRIPTION.....	8
1.2.2 ACCESS.....	8
1.2.3 THE RECEIVING ENVIRONMENT.....	8
1.2.4 VEGETATION TYPES EXPECTED	8
1.2.5 SURFACE WATER.....	9
1.2.6 ARCHAEOLOGICAL, HERITAGE AND PALAEOLOGICAL RESOURCES.....	10
1.3 RECOMMENDATIONS ON IMPACT MITIGATION/MINIMISATION	10
1.4 ENVIRONMENTAL AUTHORISATION	12
2. DEFINITIONS AND ABBREVIATIONS:.....	13
2.1 DEFINITIONS.....	13
2.2 ABBREVIATIONS	16
3. CONSTRUCTION PHASE EMP	17
3.1 STRUCTURE AND RESPONSIBILITY	17
3.1.1 The client / applicant / owner.....	17
3.1.2 The Construction Supervisor	17
3.1.3 The contractor.....	17
3.1.4 The Environmental Control Officer (ECO).....	18
3.1.5 ECO qualifications	18
3.1.6 ECO duties	18
3.1.7 ECO Authority.....	18
3.1.8 Health and safety officer.....	19
3.1.9 Health and Safety Officer qualifications	19
3.2 COMMENCEMENT OF WORKS	19
3.3 ISSUES OF CONCERN.....	20
3.4 SITE SPECIFIC ARRANGEMENTS & CONSTRUCTION PROCEDURES	20
3.4.1 On-site start-up meeting.....	20
3.4.2 Start-up meeting participants.....	21
3.5 ENVIRONMENTAL- & AWARENESS TRAINING	21
3.5.1 Environmental awareness course	21
3.5.2 Specific training.....	21
3.6 METHOD STATEMENTS	21
3.6.1 Additional method statements	23
3.7 NON-COMPLIANCE.....	23

3.7.1	Corrective action instruction	23
3.7.2	Written warning	23
3.7.3	Penalty fines.....	23
3.7.4	Stop works.....	23
3.8	CHANGES TO EMP	24
3.9	RECORD KEEPING	24
3.10	STANDARD MANAGEMENT PROCEDURES	24
3.10.1	Access and haul routes	24
3.10.2	Appropriate use of machinery	25
3.10.3	“No-Go” areas	25
3.10.4	Restriction of working areas.....	26
3.10.5	Protection of natural vegetation	27
3.10.6	Protection of fauna and Avi-fauna	27
3.10.7	Clearing of vegetation, stripping and conservation of topsoil.....	27
3.10.8	Erosion and sedimentation control.....	28
3.10.9	Alien invasive management plan.....	29
3.10.10	Protection of archaeological & paleontological remains	30
3.10.11	Storage of construction material and stockpiling.....	31
3.10.12	Oil storage and management.....	31
3.10.13	Storing of petroleum products.....	32
3.10.14	Storing of hazardous substances	33
3.10.15	Use of cement or concrete.....	33
3.10.16	Firefighting	34
3.10.17	Emergency Procedures	34
3.10.18	Solid waste management	35
3.10.19	Toilets and Ablution Facilities	35
3.10.20	Discharge of construction water.....	36
3.10.21	Eating facilities	36
3.10.22	Dust Control.....	36
3.10.23	Restoration and rehabilitation	37
3.10.24	Land Management	37
3.10.25	Socio-Cultural Issues	38
3.11	EMERGENCY PREPAREDNESS & RESPONSE	38
3.11.1	Accidental fires	38
3.11.2	Hydrocarbon spills	38
3.11.3	Concrete/cement spillages	38
4.	OPERATIONAL EMP (OEMP)	39
4.1	TRAFFIC ACCESS ROUTES AND HAUL ROADS	39
4.2	ENERGY MANAGEMENT	39

4.3	WATER MANAGEMENT	40
4.4	EROSION AND SEDIMENT CONTROL	40
4.5	WASTE & POLLUTION MANAGEMENT	40
4.6	MINIMISE DUST AND EMISSIONS	41
4.7	MANAGEMENT OF NATURAL AREAS.....	41
4.8	EMERGENCY PREPAREDNESS AND RESPONSE.....	41
4.8.1	Accidental fires.....	41
4.9	CHEMICAL MANAGEMENT	41
4.10	BATTERY ENERGY STORAGE SYSTEM (BESS) MANAGEMENT.....	42
4.11	SOLAR PANEL ARRAY AND ASSOCIATED INFRASTRUCTURE MANAGEMENT.....	42
5.	ENVIRONMENTAL AUDIT PROGRAMME	44
6.	DECOMMISSIONING PHASE	45
7.	IMPACT MANAGEMENT OUTCOMES	46

LIST OF APPENDIXES

APPENDIX 1: DECLARATION OF UNDERSTANDING

APPENDIX 2: ENVIRONMENTAL AUTHORISATION

APPENDIX 3: MAPS & DRAWINGS

APPENDIX 4: START-UP REPORT

APPENDIX 5: PENALTIES FOR NON-COMPLIANCE

APPENDIX 6: INFO ON METHOD STATEMENTS

APPENDIX 7: EXAMPLE OF METHOD STATEMENT

APPENDIX 8: CONTACTOR ENVIRONMENTAL CHECKLIST

APPENDIX 9: BASIC RULES OF CONDUCT

APPENDIX 10: ECO/ESO REPORT/CHECKLIST

APPENDIX 11: METHOD STATEMENT REGISTER

APPENDIX 12: ENVIROMENTAL INCIDENT REPORT FORM

APPENDIX 13: COMPLAINTS REGISTER FORM

1. INTRODUCTION

The main purpose of this Environmental Management Programme (EMP) is to prevent avoidable damage and/or minimise or mitigate unavoidable environmental damage associated with any construction, operational, maintenance, or decommissioning/ demolition work where there is a risk of environmental damage and to enhance positive benefits of the project.

The EMP forms part of the contractual obligations to which all contractors/employees involved in construction, maintenance, or demolition work must be committed. It serves as a guideline and baseline information document for the construction and operational of the proposed project and aims to comply with Section 24N of the National Environmental Management Act (Act no 107 of 1998) also known as NEMA, as well as the Environmental Impact Assessment Regulations, 2014 (Government Notice No R 326) and any additional specific information requested by any State Department, including the Department of Forestry, Fisheries and the Environment (DFFE) for specific projects.

In furtherance of the above, Section 28(1) of National Environmental Management Act (Act no 107 of 1998) (NEMA) places an absolute Duty of Care and provides that every person who causes, has caused or may cause significant pollution or degradation of the environment must take reasonable measures to prevent the pollution or degradation from occurring, or, if the harm to the environment is authorised by law or cannot be avoided or stopped, to reduce and rectify the pollution or degradation

This EMP:

- Identifies project activities that could cause environmental damage (risks) and provides a summary of actions required
- Identifies persons responsible for ensuring compliance with the EMP and provides their contact information
- Provides standard procedures to avoid and/or minimise the identified negative environmental impacts and to enhance the positive impact of the project on the environment
- Provides site and project specific rules and actions required, including a site plan/s showing:
 - Areas where construction, maintenance, or demolition work may be carried out
 - Areas where any material or waste may be stored
 - Allowed access routes, parking and turning areas for construction or construction related vehicles
- Forms a written record of procedures, responsibilities, requirements and rules for Contractor/s, their staff and any other person who must comply with the EMP
- Provides a monitoring and auditing programme to track and record compliance and identify and respond to any potential or actual negative environmental impacts
- Provides a monitoring programme to record any mitigation measures that are implemented

The EMP is partly prescriptive (identifying specific people or organisations to undertake specific tasks, in order to ensure that impacts on the environment are minimised), but it is also an open-ended document in that information gained during the construction activities and/or monitoring of procedures on site could lead to changes in the EMP.

This EMP was compiled by Zandria Jordaan who is a junior Environmental Consultant with EnviroAfrica cc. She holds a MSc in Geology from Stellenbosch University and BSc (Hons) in Environmental Sciences with Environmental Geology from the North-West University. Zandria has accumulated experience in the fields of environmental compliance auditing, environmental management, renewable energy and public participation processes. Zandria is a Candidate EAP (#2023/7974) registered with the Environmental Assessment Practitioners Association of South Africa (EAPASA).

This EMP was reviewed by Clinton Geyser who is an Environmental Consultant at EnviroAfrica cc. Clinton has a MSc. Degree in Geography and Environmental Management and BSc (Hons) in Geography and Environmental Management from the University of Johannesburg. Clinton has over twelve years' experience in the environmental management field as an Environmental Assessment Practitioner and as an Environmental Control Officer, having worked on a variety of projects in the Western, Eastern and Northern Cape, and Free State Provinces. He is a registered EAP with Environmental Assessment Practitioners Association of South Africa (EAPASA), registration number: 2021/3287.

1.1.1 PURPOSE

The purpose of the EMP is to give direction and guidance to all responsible parties, which are in turn expected to cooperate closely to minimise or avoid unnecessary environmental impacts or delays. The ECO will ensure compliance with the EMP (and other Environmental issues) and will visit the site on a regular basis during the construction phase, with additional visits at the professional, project-linked, discretion of the ECO or relevant authority.

This EMP binds all contractors, sub-contractors and other persons working on the site to adhere to the terms and conditions of the EMP throughout the construction activities of the project and any other construction activities associated with the upgrade of the site.

Any other site-specific additional activities decided and agreed upon at the "On Site Start-Up Meeting" must be included to form part of this EMP.

1.1.2 SCOPE

This EMP addresses the construction phase (CEMP) and operational phase (OEMP) and all activities associated with the project. In addition, it will deal with all the requirements of regulation 19 (4) of the EIA regulations (R. 982, 04 December 2014) as well as any additional specific information requested by the Department of Environmental Affairs and Development Planning (DEA&DP) pertaining to some developments.

Compliance to this EMP (which serves as a basis for all the phases of the project) will be monitored by the Environmental Control Officer (ECO). The Construction Engineer/Project Managers, the Contracting Agent(s) and the Client will be responsible for the implementation of this Environmental Management Plan.

This EMP constitutes a generic EMP relevant to all Zero Carbon Charge car charging stations and associated solar PV plant and infrastructure. Each approved vehicle charging station within the Zero Carbon Charge network may require its own site-specific EMP and mitigation measures if required.

1.2 SITE LOCATION

Zero Carbon Charge electric vehicle charging stations are proposed at regular intervals along major routes across the country. Each site will have its own unique environmental characteristics, which will need to be taken into consideration for inclusion in any site-specific EMP and mitigation measures.

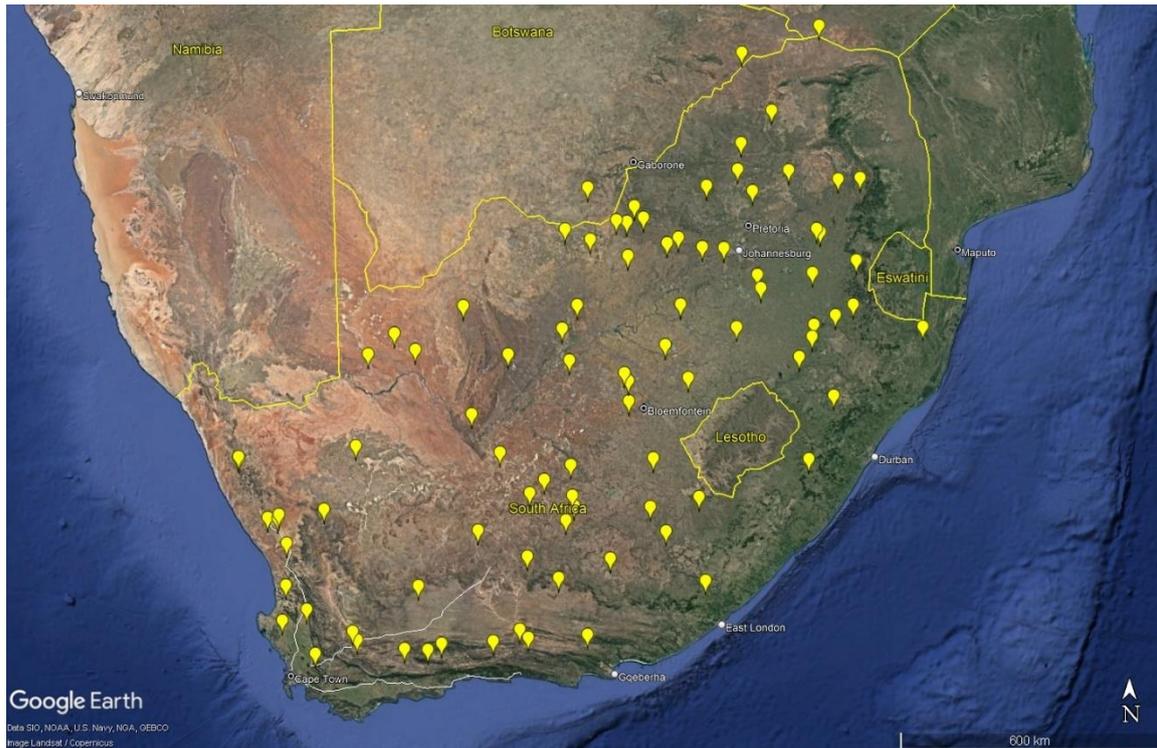


Figure 1. Google Earth Image Showing the Current Proposed Electric Vehicle Charging Station Network (As of July 2023).

This EMPr speaks to one of the sites along the N14, between Kakamas and Keimoes (Figure 2). The proposed development is located on Portions 19 and 47 of Farm No. 466, within the Kai! Garib local Municipality and within the Dawid Kruiper District Municipality.

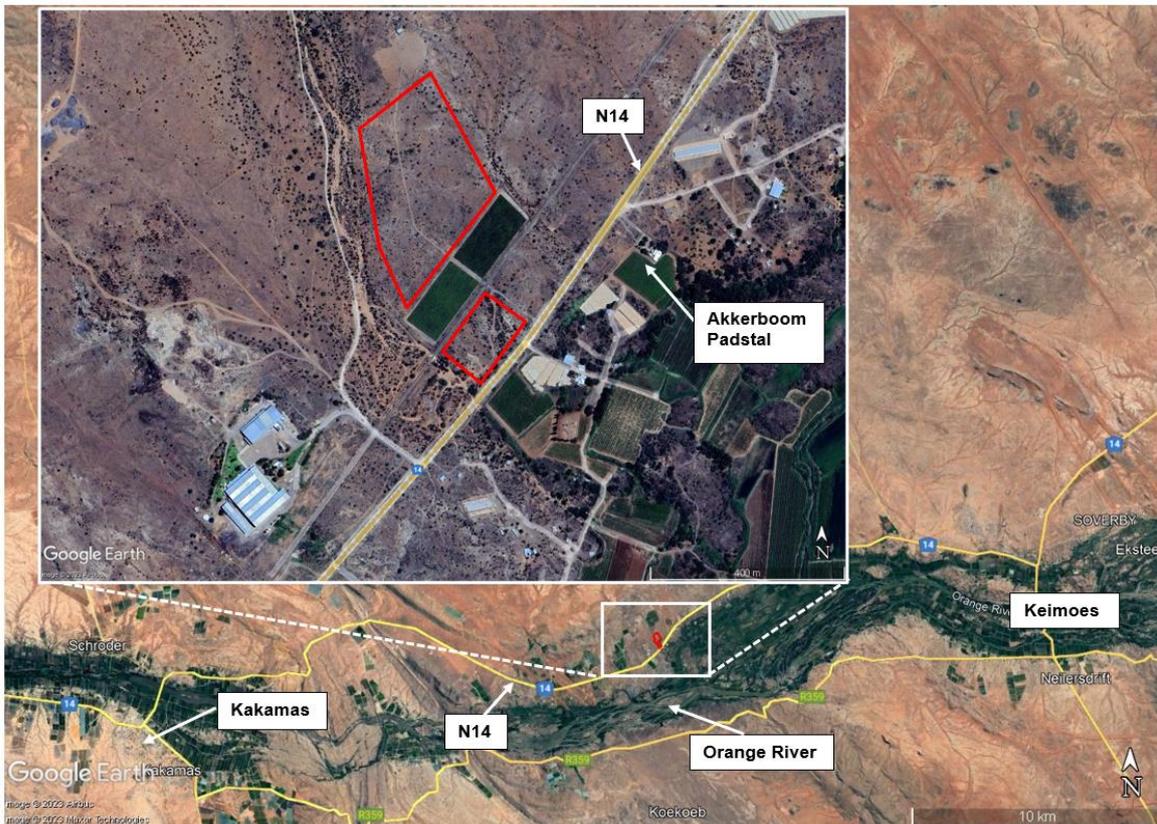


Figure 2. Google Earth Image Showing the Location of the Proposed Site at Akkerboom Padstal.

1.2.1 PROJECT DESCRIPTION

Zero Carbon Charge (ZCC) are proposing a network of electric vehicle (EV) charging stations, located approximately every 150 km along major routes across the country. Each charging station will be powered by an off-grid solar photovoltaic (PV) facility.

Each facility will cater either specifically for cars or for trucks. Car sites will include a farmstall, parking area and restrooms. Truck sites will include restrooms, shops, parking area (including overnight parking).
Project description to be added here

1.2.2 ACCESS

Access from major routes will require approval from SANRAL or provincial roads authority.

1.2.3 THE RECEIVING ENVIRONMENT

According to the Terrestrial Biodiversity Assessment the site is characterized by **Lower Gariep Alluvial Vegetation** and **Bushmanland Arid Grassland**, both classified as "Least Threatened." The area overlaps with **Critical Biodiversity Areas (CBA)** due to its location within an ecological corridor along the Orange River.

The project footprint includes **ephemeral drainage lines** that support biodiversity in the arid region. The vegetation is in good condition, though species diversity is low, likely due to a prolonged drought. Notable **protected species** include the **Camelthorn Tree (Vachellia erioloba)** and **Baobab Tree (Adansonia digitata)**, which must be preserved during construction. Faunal species of concern, such as the **Ludwig's Bustard**, may utilize the site, though the development is expected to have minimal impact on these species.

The site has low **archaeological** and **palaeontological sensitivity**, with isolated lithic artifacts and no significant fossils identified. The surrounding land is primarily used for agriculture, with existing vineyards and grazing areas. Although the development will intersect some critical biodiversity areas, with proper mitigation, the impact on ecological connectivity and biodiversity is expected to be manageable.

This environment is arid, receiving about **191 mm of rainfall annually**, with sudden thunderstorms and prolonged droughts shaping the landscape. The overall impact on the receiving environment is expected to be moderate, provided the recommended mitigation measures are followed.

1.2.4 VEGETATION TYPES EXPECTED

According to the Terrestrial Biodiversity Assessment the site is characterized by **Lower Gariep Alluvial Vegetation** and **Bushmanland Arid Grassland**, both classified as "Least Threatened." The area overlaps with **Critical Biodiversity Areas (CBA)** due to its location within an ecological corridor along the Orange River.

1. Lower Gariep Alluvial Vegetation:

This vegetation type will be affected by the development of the electric vehicle charging station and the first phase of the solar panels. **Conservation Status:** Classified as "**Least Threatened**" under the **National List of Ecosystems** in need of protection (GN. No. 2747 of 18 November 2022).

This vegetation type is associated with riparian zones along rivers such as the Orange River. It is important for stabilizing watercourses and providing habitat for various fauna. However, the area impacted by the project is limited and is not expected to have a significant ecological impact given the already transformed land.

2. Bushmanland Arid Grassland:

Phases 2-7 of the solar panels will primarily impact this vegetation type. **Conservation Status:** Also classified as "**Least Threatened**" according to the same national list.

This type of vegetation is found in arid, semi-desert areas and is characterized by low, sparse grass cover and drought-resistant shrubs. The Bushmanland Arid Grassland is not particularly rich in plant species and lacks endemic centers of biodiversity. The specific area is used for grazing livestock and game.

3. Key Considerations for Both Vegetation Types:

- **Critical Biodiversity Areas (CBA):** Both vegetation types are within or adjacent to Critical Biodiversity Areas (CBA 1 and CBA 2), which are crucial for maintaining ecological processes and connectivity. The proposed development will slightly impact these CBAs, particularly along an ecological corridor associated with the Orange River.
- **Vegetation Condition:** The **Nama-Karoo** biome in this region, including the Bushmanland Arid Grassland, was found to be in relatively good condition. However, species diversity was lower than expected, possibly due to the extended **7-year drought** in the area.
- **Protected Species:** The site includes some **protected plant species**, such as **Camelthorn (Vachellia erioloba)** and **Baobab (Adansonia digitata)**, which must be preserved during construction.

4. Impact and Sensitivity:

- Despite the presence of these vegetation types in Critical Biodiversity Areas, the proposed footprint is relatively small, affecting less than 11 ha. The impact is expected to be manageable with appropriate **mitigation** strategies to protect biodiversity, minimize habitat fragmentation, and conserve protected species. The cumulative impact is given as Medium, however with mitigation it can be reduced to **Medium-Low**.

In conclusion, the vegetation at the ZCC Akkerboom site is not classified as endangered, and the project's impact on the **Lower Gariep Alluvial Vegetation** and **Bushmanland Arid Grassland** is expected to be limited and controllable with mitigation.

1.2.5 SURFACE WATER

According to the Freshwater Report, the proposed development site is primarily characterized by **ephemeral drainage lines** that form part of the local hydrological system. The site is situated near the **Orange River**, although it does not directly interact with the river's flow.

Drainage Lines:

The site contains **ephemeral watercourses** or **dry drainage lines**, which only carry water after **infrequent, intense rainfall events** such as summer thunderstorms. These drainage lines are considered legitimate water resources under the National Water Act (NWA).

The drainage lines are driven by erratic rainfall patterns, with intense, short bursts of rain causing **sheet wash plains** and braided drainage systems to form across the site. These drainage lines spread water across wide areas, forming a fan-like network of water channels.

Hydrological Importance: Although the drainage lines do not contribute significant volumes to the **Orange River**, they are ecologically important. They support denser and taller vegetation compared to the surrounding arid landscape, contributing to **habitat diversity** and acting as **corridors for fauna**.

The drainage lines are ecologically sensitive as they provide essential microhabitats in the otherwise arid landscape. They enable higher vegetation density and are integral to biodiversity, particularly in terms of providing **migration corridors** and supporting **drought-resistant vegetation**.

The freshwater assessment indicated that the larger drainage lines in the region are **moderately disturbed**, primarily due to agricultural activities, such as sand mining and irrigation from nearby vineyards. Despite these disturbances, the drainage lines maintain their ecological importance.

The **aquatic biodiversity** rating for the site is considered **low**, as the watercourses are **dry for most of the year** and do not support permanent aquatic life. However, these drainage lines are part of a **Critical Biodiversity Area (CBA)**, and even though the aquatic biodiversity is limited, the drainage lines contribute to the overall ecological function of the area by supporting **riparian vegetation** and acting as wildlife corridors.

The development may alter the **drainage characteristics** of the area, potentially impacting surface water flow and the associated ecological functions of the drainage lines. However, these impacts can be **mitigated** through careful planning and adherence to regulations governing water use and surface water management.

The **cumulative impact** on the surface water environment, considering the project's limited footprint and intermittent nature of the watercourses, is expected to be **moderate**, with mitigation measures aimed at reducing runoff and preserving drainage line integrity.

In conclusion, while the proposed development will interact with **sensitive drainage lines**, which play a crucial role in maintaining local biodiversity and habitat, the impact on surface water can be managed. Proper mitigation and regulatory compliance will be key to minimizing potential negative effects on these ephemeral watercourses.

1.2.6 ARCHAEOLOGICAL, HERITAGE AND PALAEOLOGICAL RESOURCES

The archaeological resources identified are of low significance and will not be impacted by the development.

Heritage resources, including graves, historical structures, and cultural landscapes, were not found, and the impact on such resources is considered minimal.

The site's palaeontological sensitivity is very low due to its igneous geology, and no significant palaeontological resources are expected to be impacted.

No further mitigation is necessary, except for ongoing monitoring during construction in case subsurface artifacts or human remains are uncovered.

The Archaeological, Heritage and Palaeontological Resources assessment indicates that the proposed project poses minimal risk to archaeological, heritage, and palaeontological resources, and can proceed under the guidance provided by the HIA report.

1.3 RECOMMENDATIONS ON IMPACT MITIGATION/MINIMISATION

The following are site/project specific impact mitigation measures recommended by the Specialists and must be enforced if the proposed development were approved.

Agriculture:

No specific mitigation measures required.

Freshwater:

- Proper drainage infrastructure (e.g., swales and retaining ponds) should be constructed to manage flow paths and prevent erosion
- Install stormwater management infrastructure to regulate the flow of runoff
- Maintain proper standard operating procedures for panel cleaning
- Design the parking lot to capture and treat any potential runoff
- Stabilise and rehabilitate disturbed areas immediately after construction
- Maintain existing drainage lines without further canalization
- Manage grazing and prevent over-grazing
- Implement grazing control measures to prevent environmental degradation
- Use portable toilets serviced by a reputable company during construction

- Implement septic tanks and soak-away systems during operation
- Maintain strict waste collection and disposal protocols to eliminate litter

Biodiversity:

The proposed development site is considered of **Medium-Low** sensitivity in terms of terrestrial biodiversity. Impact minimisation should focus on the protection of the watercourse to the west of the solar site's footprint, the protection of mature *Vachellia erioloba* trees and mitigation measures during construction (and operational) phases, of which the overriding goal should be to clearly define the final layout and to minimise the disturbance footprint.

- All construction must be done in accordance with an approved construction and operational phase Environmental Management Plan (EMP), which must be developed by a suitably experienced Environmental Assessment Practitioner.
- A suitably qualified Environmental Control Officer must be appointed to monitor the construction phase in terms of the EMP and any other conditions pertaining to specialist studies.
- Before any work is done the footprint must be clearly demarcated. The demarcation must aim at minimum footprint and minimisation of disturbance.
- All efforts must be made to protect the small watercourse to the west of the proposed solar facilities (as demarcated in the site sensitivity map - Figure 9).
- All mature *Vachellia erioloba* trees, larger than 6 m, must be protected during development and operation. No development should be considered underneath the canopy of any of the trees remaining on Portion 47 of the Farm Frier's Dale No. 466.
- The *Vachellia erioloba* and *Adansonia digitata* trees remaining and planted within the parking and garden area of the Akkerboom farm stall (on Portion 19 of the Farm Frier's Dale no. 466) must be protected.
- A National Forest Act licence application must be submitted if any of the identified *Vachellia erioloba* or *Adansonia digitata* trees will be impacted.
- A Northern Cape Nature Conservation Act permit must be **obtained for impact on the protected species listed** in Table 10 of the Biodiversity Assessment.
- All alien invasive species within the footprint and its immediate surroundings must be removed responsibly.
 - Care must be taken with the eradication method to ensure that the removal does not impact or lead to additional impacts (e.g., spreading of the AIP due to incorrect eradication methods);
 - Care must be taken to dispose of alien plant material responsibly.
- Indiscriminate clearing of any area outside of these footprints may not be allowed.
- An integrated waste management approach must be implemented during construction.
 - Construction related general and hazardous waste may only be disposed of at approved waste disposal sites.
 - All rubble and rubbish should be collected and removed from the site to a Municipal approved waste disposal site.

Heritage:

No further mitigation is necessary, except for ongoing monitoring during construction in case subsurface artifacts or human remains are uncovered.

Socio-Economic:

- Engage with local businesses, especially existing farm stalls and guest houses, to assess impact and explore collaborative opportunities for stimulating the local economy
- Adhere to general Environmental Management Programme (EMPr) guidelines to mitigate noise and visual impacts in mixed residential areas
-

- No direct action required for Eskom overhead lines, but maintain situational awareness for potential local grid instability
- Develop marketing strategies to promote the unique selling point of the EV charging station, considering its potential to boost local economy and tourism
- Implement skills development programs targeting the local community to prepare them for job opportunities in construction and maintenance
- Engage with local agricultural stakeholders to minimize disruption and explore opportunities for collaboration
- Utilize existing internal farm gravel roads to minimize land use change
- Confirm with SANRAL that no future railway development plans are anticipated that may create potential conflicts
- Engage with local communities to identify and protect cultural and heritage sites

Visual:

- Implement natural vegetative buffers or earth berms around the facility to minimize its visual impact, especially near water features and residential areas
- Use non-reflective, earth-toned materials for all built structures to blend them into the natural landscape and reduce glare
- Post-construction, undertake a re-vegetation program using indigenous plant species to restore any disrupted areas and enhance the site's Visual Absorption Capacity (VAC)
- Implement dust control measures and restrict construction activities to daylight hours to minimize visual and atmospheric impacts
- Develop and implement a traffic management plan to control construction-related traffic, minimizing visual and safety impacts on the N14 highway and other local roads
- Conduct a comprehensive Heritage Impact Assessment (HIA) that specifically includes the graves identified on the neighboring farm to evaluate their cultural significance and potential visual impact. Based on the findings, implement protective measures that may include demarcation, buffering zones, or even relocation, if feasible and culturally appropriate. This will ensure that the development is sensitive to the newly identified cultural elements and maintains the integrity of the broader cultural and living landscape
- Install educational signage that explains the environmental benefits of the solar PV and EV charging facility, turning a potential visual intrusion into an educational opportunity if feasible
- Design the layout of solar panels to follow the natural contours of the land, reducing the visual impact and need for extensive land grading

1.4 ENVIRONMENTAL AUTHORISATION

The Conditions of approval of the Environmental Authorisation (EA) and other relevant approvals/licences from other authorities will be included as Appendix 1 in the final EMP. The conditions of approval must be adhered to as part of the EMP.

2. DEFINITIONS AND ABBREVIATIONS:

2.1 DEFINITIONS

Applicant:	The person or responsible person from an organization who applied for the proposed activity described in the Environmental Authorisation.
Audit (Site Completion):	Environmental Site Inspection and verification of construction activities to EMP
Bund:	Enclosure under / around a storage facility to contain any spillage
Batch plant:	A concrete or plaster mixing facility and associated equipment and materials.
Construction:	Means the period of the project during which the actual works are carried out, deemed to include site establishment, site preparation, the works, maintenance period and decommissioning.
Construction phase:	The construction phase period of a cellular communications Construction site is defined as from the commencement of site establishment up to and including the practical site handover.
Construction site:	Means the area influenced and affected by the construction activities or under the control of the Contractor often referred to as “the Site”.
Construction Supervisor:	The person responsible (appointed by the owner) to ensure that the construction is carried out to completion on time, within budget and that the Contractor fulfils his obligations in terms of the EMP.
Contaminated water:	Means water contaminated by the Contractor's activities, e.g. concrete water and runoff from plant/ personnel wash areas.
Contractor:	The principal persons / company and all other sub-contractors involved in the construction of the project.
Contractor's camp:	Means the designated and suitably demarcated areas on the Site within which all site offices and staff facilities are situated and within which equipment will be stored, for instance, batching plant, crusher plant, sand washing plant, workshop, offices, rest areas, ablution areas, etc., whichever is applicable.
Contaminated water:	Means water contaminated by the Contractor's activities, e.g. concrete water and runoff from plant/ personnel wash areas.
Declaration of understanding:	Form that is signed by all contractors involved in the construction works of their understanding and acceptance of the EMP and site-specific additions to the EMP.
Development site:	Boundary and extent of development works and infrastructure.
Environment:	Means the surroundings within which humans exist and that are made up of: <ul style="list-style-type: none"> • the land, water and atmosphere of the earth; • micro-organisms, plant and animal life; • any part of the combination of the above two bullets and the interrelationships between them; • the physical, chemical, aesthetic and cultural properties and conditions of the foregoing that influence human health and well-being
Environmental Aspect:	Any element of any construction activity, product or services that can interact with the environment

Environmental Audit Report:	Report done by the ECO and submitted by the Applicant to the satisfaction of the Chief Directorate Environmental Affairs, within six months after construction has been completed and also after the site(s) has been rehabilitated
Environmental Control Officer:	The registered Environmental Scientist (<i>in terms of section 20(3) of the Natural Scientific Professions Act, 2003 (Act 27 of 2003)</i>) responsible for overseeing the environmental aspects of the Construction phase of the EMP.
Environmental Completion Statement:	A report by the ECO to the relevant authorities stating completion of the project and compliance with the EMP and its conditions.
Environmental Impact:	Any change to the environment, whether adverse or beneficial, wholly or partially resulting from any construction activity, product or services.
Method statement:	A statement by the Contractor, describing the scope of <u>intended</u> construction works step-by-step, in order for the ECO and Construction Supervisor to understand the Contractors intentions and be able to comment on, so that they could assist with devising mitigating measures should it be necessary to avoid environmental impact.
No-Go Area(s):	An area of such (environmental/aesthetical) importance that no person or activity are allowed within a designated boundary surrounding this area.
Owner:	The owner, or dedicated person, responsible for the management of the property on which the proposed activity (in terms of the ROD) will be performed.
Stop Works Order:	An order which can be issued either by the ECO or Construction Supervisor to the Contractor (or any sub-contractor) if serious environmental damage is about to happen or is happening as a result of construction activities. On receiving such an order the Contractor must immediately stop all activities (or planned activities) relevant to the specific issue until an environmentally friendly resolution has been approved by the ECO.
Site:	The area and extent of the development works and infrastructure, including any areas off the main site on which works are to be carried out in order to allow the development to proceed successfully.
Site meetings:	Periodic (weekly or monthly) meetings between the ECO, Construction Supervisor and Contractor to discuss construction activities that relate to the environment or any other environmental issues that might arise.
Works:	The works to be executed in accordance with a contract.
On-site start-up meeting:	A start-up meeting held on site, before any construction has begun to discuss EMP and determine site specific additions that will be included as the basis for the EMP.
Potentially hazardous substance:	A substance, which, in the reasonable opinion of the Engineer, can have a deleterious (detrimental) effect on the environment.
Method statement:	A written submission by the Contractor to the Engineer or relevant responsible person.
Reasonable:	Means unless the context indicates otherwise, reasonable in the opinion of the Engineer/Project Leader after he has consulted with a person, not an employee of the client, suitably experienced in "environmental implementation plans" and "environmental management plans", both as defined in the Environmental Management Act (Act No 107, 1998).

Solid waste: Means all solid waste, including construction debris, chemical waste, excess cement/concrete, wrapping materials, timber, tins and cans, drums, wire, nails, food and domestic waste (e.g. plastic packets and wrappers).

Precautionary principle: Means the basic principle, that when in doubt or having insufficient or unreliable information on which to base a decision, to then undertake actions that will have minimum risk.

2.2 ABBREVIATIONS

CA	Competent Authority
CARA	Conservation of Agricultural Resources Act, 1983 (Act no. 43 of 1983)
CEMP	Construction phase Environmental Management Plan
DENC	Department of Environment and Nature Conservation
DFFE	Department of Forestry, Fisheries and the Environment
ECO	Environmental Control Officer: - Must be a suitably qualified independent environmental consultant appointed to ensure compliance to the EMP
EMP	Environmental Management Plan or Programme
ESO	Environmental Site Officer - Must be a person with adequate environmental knowledge to understand and implement the EMP by conducting on-site inspections determined by the ECO and the client
ER	Engineers' representative or Main contractors' representative
EA	Environmental Authorisation (Record of Decision) issued by relevant authority for the authorisation to commence construction under certain environmental compliances
MSDS	Material Safety Data Sheet(s)
NEMA	National Environmental Management Act, 1998 (Act no. 107 of 1998)
OEMP	Operational Environmental Management Plan
OSSM	On-site Start-up Meeting
SAHRA	South African Heritage Resources Agency

3. CONSTRUCTION PHASE EMP

3.1 STRUCTURE AND RESPONSIBILITY

Implementation of the EMP and environmental control and management of the construction phase will be achieved through the responsibility structure set out below. The role players include the Owner (ZCC), the Construction Supervisor, the Environmental Control Officer and the Contractor. All role players must familiarize themselves with the prescriptions of the EMP.

3.1.1 THE CLIENT / APPLICANT / OWNER

The client (or the designated responsible person appointed ZCC – further referred to as Owner) is responsible for:

- Appointing a suitably experienced ECO, the Construction Supervisor and the Contractor for the duration of the construction contract, and
- Ensuring that the Construction Supervisor and Contractor fulfil their obligations in terms of this EMP.

3.1.2 THE CONSTRUCTION SUPERVISOR

The Construction Supervisor is responsible to ensure that the construction is carried out to completion on time, within budget and that the Contractor fulfils his obligations in terms of the EMP. In addition, the Construction Supervisor and the ECO are expected to develop a close working relationship and to stay in contact with each other.

The responsibilities of the Construction Supervisor include:

- To issues site instructions to the Contractor
- To serve as conduit for all communication between the ECO and the Contractor [The only exception is where the ECO or the Construction Supervisor needs to issue a “**STOP WORKS**” order to the contractor if serious environmental harm is about to happen or is happening as a result of construction activity. The “**STOP WORKS**” order must be confirmed by the other party as soon as reasonably possible]
- Discussing any problems that might lead to environmental damage with the ECO
- When the ECO is not on site the Construction Supervisor will be responsible for the implementation of the EMP

3.1.3 THE CONTRACTOR

The Contractor shall be responsible to:

- Ensure that all sub-contractors, employees, suppliers, agents etc. are fully aware and adhere to the environmental conditions detailed in the EMP
- Liaise closely with the Construction Supervisor and the ECO
- Ensure that works on the site are conducted in an environmentally sensitive manner and in full accordance with the EMP
- Carry out instructions issued in the site instruction book
- Assist with solutions to environmental problems that may arise during the construction phase; and
- Ensure that all “**No-Go**” areas are adequately fenced off
- Will report any deviation from the requirements of this EMP to the Principal Agent, and any pollution or environmental contaminant spill events
- Agrees to work stoppage and/or payment of penalties as required by this EMP and directed by the ECO/Construction Supervisor
- Agrees to bear full costs for any work stoppage resulting from contravention of the requirements of this EMP, and/or the costs of remedying environmental damage resulting from their or their sub-contractors or employee’s contravention of the requirements of this EMP

NB: All contractors must sign the “Declaration of understanding” (Appendix 1) of this Environmental Management Plan before construction commences.

3.1.4 THE ENVIRONMENTAL CONTROL OFFICER (ECO)

ECO will be responsible for overseeing the environmental aspects of the Construction phase and will work in close coordination with the Construction Supervisor.

3.1.5 ECO QUALIFICATIONS

The ECO must be independent and suitably qualified (a diploma or degree in environmental management with at least 2 or more years of environmental site management experience) and must have a sound knowledge of the environment in which the activity will take place.

3.1.6 ECO DUTIES

An ECO must be appointed for the duration of the construction phase (or as required by the EA) and:

- Will be primarily responsible for ensuring the implementation of the EMP and will perform regular site inspections/audits with the specific aim to ensure environmental conformance by the Contractor
- Will visit the site on a regular basis while construction is in progress. Frequency of site visits is recommended at 1 x site visit per month, or as determined by the Competent Authority
- Will keep environmental records (including photographs) of the construction activities
- Must ensure that “No-Go” and “Open Space” areas are adequately protected and adhered to
- Must approve and be present during the demarcation of the necessary areas for storage of materials, ablutions, eating areas of contract workers etc.
- Will conduct a start-up meeting before construction commences, will provide environmental training at the beginning of the project and provide environmental awareness training throughout the life of the project
- Must be informed of site and technical meetings to be able to comment and report on environmental issues
- Will call for, and approve, method statements for construction activities that might pose an environmental impact and must ensure that method statements are approved before commencement of the work
- Must implement immediate mitigating action in the case of critical environmental impacts
- Must deal with public complaints/queries regarding environmental issues
- Will record his findings and all environmental non-conformances in an environmental completion report (which will be forwarded to the Client and the Construction Supervisor)
- Will conduct a closing down visit as soon as possible after completion of the Development
- Will commission an independent Environmental Compliance Audit within 6 months after completion of the contract

3.1.7 ECO AUTHORITY

The ECO has the authority to stop works if there is a serious threat to or impact on, the environment as a direct cause of construction. However, this authority is limited only to emergency situations where immediate consultation with the Construction Supervisor is not possible.

- The ECO is to inform the client/developer and site representative of the reasons for the stoppage as soon as possible. A relevant reason should be supplied as soon as possible after stoppage of such works
- Upon failure by the contractor or his employee to show adequate consideration to the environmental aspects of this contract i.e. wilful destruction of the environment, the ECO may recommend to the client/developer or site representative to have the contractor's representative or any employee(s) removed from the site or work suspended until the matter is remedied

- No extension of time will be considered in the case of such suspensions and all costs will be borne by the contractor

3.1.8 HEALTH AND SAFETY OFFICER

A Health and Safety (H&S) Officer for the project must be designated or appointed by the Contractor or Principal Agent, and his/her role is to support the successful implementation of the EMP through:

- Site evaluation on a regular basis
- Identifying issues relating to day-to-day construction activities and that can have a detrimental effect on the environment
- Subcontractor audits to ensure compliance
- Assist in the direct implementation of the EMP
- Ensure that the requirements of the EMP are communicated understood by personnel on site via induction sessions
- Ensure that the contractors on site develop, implement and monitor the required H&S management functions
- Evaluate the applicability and accuracy of the EMP and the method statements throughout the construction phase
- Coordinate all statutory requirements including permit authorisation and license requirements
- Conduct or have conducted a hazard analysis and take the necessary corrective action
- Where it is not possible to remove any remaining hazard's, inform employees thereof and what precautionary action is to be taken
- Detail mitigation measures required to be taken, and the procedures for their implementation to the project manager
- Representing H&S issues at the production meetings
- Coordinate H&S training of personnel
- Coordinating spill response personnel
- The H&S officer shall inspect the integrity of the hazardous waste containers/bins/skips on a weekly basis

3.1.9 HEALTH AND SAFETY OFFICER QUALIFICATIONS

The Health and Safety Officer must be independent and suitably qualified, with a sound knowledge of the Occupational Health & Safety Act (Act no. 85 of 1993) and must have experience of the implementation of the act with regards to the construction and environmental environments in which the activity will take place.

3.2 COMMENCEMENT OF WORKS

The site project contractors must timeously receive a copy of the construction phase EMP (CEMP) and any other further additional information that pertains to site conditions/amendments or deviations from original site plan.

- This EMP must be included to form part of the Contractors site specification documentation
- A copy of the EMP must be on site at all times and available for presentation to any authority requesting to see such document.

NO WORK ON SITE MAY TAKE PLACE UNTIL:

- The Declaration of Understanding/Environmental Contract is signed between the relevant parties
- At least one week's written notice (or as specified in the EA) given to the Department before commencement of any construction activity (As per EA – if required)
- On-Site Start-Up Meeting has been held
- Site and No-Go areas have been identified **and demarcated**
- Contractors are in possession of the EMP and other relevant documentation

- Contractors/Subcontractors have signed the Declaration of Understanding
- All mandatory site equipment is in place
- On Site Environmental Education and Awareness training session has taken place with all relevant construction personnel present

NB: Work refers to: Camp Establishment, Earthmoving activities and any preliminary construction activities.

3.3 ISSUES OF CONCERN

Issues of concern that were identified in the Pre-compliance notice and included in the EA must be addressed during the “On Site Start-Up Meeting” and must be included in the On-Site Start-Up Report. Issues of Concern include but shall not be limited or restricted to the following:

- Site demarcation
- Demarcation and protection of any “no-go areas”
- Establishment of temporary laydown areas
- Waste management and disposal
- Mandatory site equipment
- Establishment of construction site compound
- Above ground bulk fuel storage facilities (if required)
- Ablution & Toilet Facilities
- Refuse Management
- Concrete works & batching plant facilities (if required)
- Soil erosion and sediment control
- Firefighting equipment & emergency fire reaction plan
- Rehabilitation

3.4 SITE SPECIFIC ARRANGEMENTS & CONSTRUCTION PROCEDURES

Please note that all recommendations summarized in the S24G Application Report, must be addressed and read as part of the site-specific arrangements & construction procedures which will include:

- General recommendations
- Site specific mitigations
- Conditions of approval of the Environmental Authorisation (if required)

3.4.1 ON-SITE START-UP MEETING

The mandatory **On-Site Start-Up Meeting** must be conducted at least **14 days but not less than 5 working days** prior to commencement of any site/camp establishment, earthworks and/or construction activities and will relate to additional discussed information that must be complied with during the entire construction phase.

On-Site Start-Up Meeting points of discussion are:

- The Construction EMP & other relevant site documents
- Project to be discussed and all uncertainties are cleared
- Method statement/s to be discussed
- Road and construction area to be demarcated
- Materials stockpile and lay down areas to be demarcated
- Method of stockpiling to be discussed
- Firefighting procedures
- Mandatory firefighting equipment & fire preventative measures
- Solid waste removal intentions
- Placement, type and service of toilets to be agreed on

- Placement and type of rubbish bins and removal of rubbish to be agreed on
- Labour overnight camp to be demarcated and services agreed on
- Environmental Education and awareness training session to all contractors & onsite staff/labour
- Location & establishment of concrete batching plant facility

3.4.2 START-UP MEETING PARTICIPANTS

Minutes of the onsite Start-Up Meeting will be condensed to a report format and circulated to all attendees of the above-named meeting for their perusal and comments. The On-site Start-up Meeting report will form part of this EMP. If any discrepancies between the start-up report and the EMP arise then the EMP will take precedence until clarification on the discrepancy is clarified. If any discrepancies between the EMP and the EA arise, then the EA will take precedence until clarification on the discrepancy is clarified.

Participants to the start-up meeting can include:

- ZCC Representative
- Contractor/Contractor's Representative
- Resident Engineer
- Site foreman
- Environmental Consultant
- Environmental Control Officer

NB: It is the responsibility of the main contractors to ensure that all sub- contractors, that work on the site during and after the civils contract, are informed of the environmental conditions pertaining to the site.

3.5 ENVIRONMENTAL- & AWARENESS TRAINING

3.5.1 ENVIRONMENTAL AWARENESS COURSE

Environmental awareness training courses shall be run for all personnel on site. The ECO will be responsible for the initial awareness course which shall include all relevant management, the Construction Supervisor, the Contractor and all foremen. All attendees shall remain for the duration of the course.

The Contractor shall be responsible to ensure that all his personnel and subcontractors (if applicable) are informed and made aware of the environmental constraints and shall also supply the ECO with a monthly report indicating the number of employees used. If refresher courses are deemed necessary, for instance, where personnel disregard the requirements of the EMP, the time lost and the cost of the course would be for the account of the Contractor.

3.5.2 SPECIFIC TRAINING

All contractors and workers shall be informed about any special habitat, biodiversity feature, vegetation and/or rare plant species that might be present on the specific construction site (if applicable).

3.6 METHOD STATEMENTS

Method statements from the contractor will be required for specific sensitive actions on request of the authorities, the Applicant and/or ECO.

A method statement forms the base line information on which sensitive area work takes place and is a "live document" in that modifications are negotiated between the Contractor and ECO/applicant, as circumstances unfold.

All method statements will form part of the EMP documentation and are subject to all terms and conditions contained within the EMP main document.

These documents must be available to the authorities for inspection or on request.

A method statement describes the scope of the intended work in a step-by-step description in order for the ECO and Applicant to understand the contractors' intentions. This will enable them to assist in devising any mitigation measures, which would minimize environmental impact during these tasks.

The Contractor must submit the method statement before any construction activity is due to start. Work may not commence until the ECO and applicant have approved the method statement.

Method statements need to be compiled by the contractor for approval by Applicant and the ECO. The contractor must submit written method statements to Applicant for the purposes of the environmental specification, a "Method Statement" is defined as a written submission by the contractor to Applicant setting out the plant, materials, labour and method the contractor proposes using to carry out an activity, in such detail that Applicant and the ECO is able to assess whether the contractor's proposal is in accordance with the specifications and/ or will produce results in accordance with specifications.

The method statement must cover applicable details with regard to:

- Construction procedures
- Materials and equipment to be used
- Getting the equipment to and from site
- How the equipment/ material will be moved while on site
- How and where material will be stored
- Location & establishment of concrete batching plant facility
- The containment (or action to be taken if containment is not possible) of leaks or spills of any liquid or material (of any potential hazardous material) that may occur
- Timing and location of activities
- Compliance/ non-compliance with the Specifications, and
- Any other information deemed necessary by the Applicant and the ECO

The Contractor must abide by these approved method statements, and any activity covered by a method statement must not commence until the Applicant and the ECO has approved of such method Statement.

NB: No work may commence or take place before the Method Statement has been approved by all relevant parties.

List of possible Method statements include but shall not be limited or restricted to:

- Demarcation
- Demarcation and protection of "no-go areas"
- A traffic management plan for the site access road
- A storm water management plan
- An erosion management plan
- Clearing of vegetation and topsoil removal
- Clearing and disposing of alien vegetation
- Stockpiling
- Temporary storage facilities
- Construction camp and site offices
- Fuel storage
- Labourer's facilities
- Mandatory site equipment
- Waste control
- Cement mixing
- Construction vehicle maintenance
- Heavy earthmoving equipment

- Dust control
- Noise control
- Rehabilitation

3.6.1 ADDITIONAL METHOD STATEMENTS

Any additional method statements (with regards to a specific aspect of construction) that may be required must be **submitted** and approved before commencement of the specific works and must be available at the site offices.

3.7 NON-COMPLIANCE

Applicant (on recommendation by the ECO) reserves the right at all times for the duration of this agreement to impose restrictions and associate penalties on the contractor with respect to the specific nature, timing and extent of construction activities on environmentally sensitive sites.

3.7.1 CORRECTIVE ACTION INSTRUCTION

The ECO may issue an onsite corrective action instruction to the site agent, or, by means of an entry into the Site Instruction Register for remedial work to be carried out to rectify any non-compliance that has been carried out within a reasonable agreeable time frame to carry out and complete the remedial work.

3.7.2 WRITTEN WARNING

In instances of non-compliance with the EMP by the contractor (or any of their employees) or sub-contractor/s (or any of their employees) that move on or off the site, the ECO must issue a written warning indicating the non-conformance to the contractor.

If repeated instructions by the ECO to the site agent to respond to the corrective action instruction have not been carried out, the ECO can issue a written warning notation instructing the site agent to timeously carry out the corrective measures as per the original non-compliance.

3.7.3 PENALTY FINES

In the event of the site agent negligence to respond and correct the noted non-compliance the ECO may in collaboration with the relevant parties recommend that a penalty fine be imposed on the contractor.

- The applicant, in consultation with the ECO must determine the amount of the penalty applicable in accordance with the penalties for Non-Compliance Schedule of Tariffs
- Such penalty amount must be in writing and presented to the contractor within seven (7) days of the written warning
- Applicant may recover penalties by deducting the fine from the offending contractor
- The contractor will be responsible for all costs incurred where emergency procedures are implemented to deal with accidents impacting on the environment as well as the rehabilitation of such damage in conjunction with the ECO and site engineer
- In serious cases, at the discretion of Applicant and the Environmental Consultant/ECO, any multiple offences can be added together

3.7.4 STOP WORKS

The ECO (after consultation with Environmental Consultant/Applicant/Engineer) may also stop the works or part thereof until the situation is resolved; no extension of time is claimable by the contractor. These penalties do not preclude any prosecution under any law or regulation.

3.8 CHANGES TO EMP

Although care has been taken to address all known relevant environmental issues for the construction phase, it may become necessary to add or amend certain procedures or instructions to improve the efficiency of the Environmental Management Plan (EMP).

- Only those additions or amendments of this EMP that will either improve environmental protection or can be proved not to have any negative effect to the immediate and surrounding environment will be considered
- Changes or deviations have to be motivated in writing by means of a Method Statement and the same procedures for a standard Method Statement have to be followed
- Any additions or amendments must be submitted by the ECO to the Competent Authority (if so requested and required) after the ECO has consulted with the Environmental Consultant and Applicant
- No deviation from the contents of the EMP is allowed without the above-named prescribed procedures

3.9 RECORD KEEPING

All records relating to the implementation of this Environmental Management Plan must be kept together, be readily retrievable and available for scrutiny by any relevant authority. Records include the following:

- Declarations of understanding
- ECO Checklist, audits and/or diary
- Method Statements
- Environmental incident reports
- Photographs (must be taken before, during and immediately after construction as a visual reference)
- The Environmental completion statement

These records must be available for scrutiny by any relevant authorities.

3.10 STANDARD MANAGEMENT PROCEDURES

3.10.1 ACCESS AND HAUL ROUTES

The Contractor must control all access (vehicles and plant) to and from the construction site, including that of suppliers used, to ensure that they remain on the pre-approved designated routes. In addition, such vehicles and plant must be so routed and operated as to minimise disruption to regular users of the routes.

- Where heavy duty vehicles and construction plant are required, both the type of vehicles/machinery and the area/s these are to access shall be specified in a Method Statement and/or Traffic Management Plan
- Access routes/haul roads will utilise only existing roads or tracks, unless such routes are not available or new routes are to be constructed as part of the project, in which case a Method Statement must be submitted for the construction of any new access/ haul roads (including temporary routes)
- No new roads or tracks may be created except where such routes are specifically approved by the ECO, in the EA or in this EMP
- Any new access roads/haul roads must be designed to minimise erosion and must run across slopes and not directly up-hill
- All vehicles and access to the site must remain within demarcated access routes and working areas on site
- All reasonable measures must be implemented to minimize impacts on road users
- On gravel or earth roads on site, the vehicles of the Contractor and his suppliers may not exceed a speed of 25 km/h
- On public roads adjacent to the site, vehicles will adhere to municipal and provincial traffic regulations
- Any temporary access routes must be rehabilitated at the end of the contract to the satisfaction of the ECO

- All vehicles used for transportation or construction purpose must be limited to the designated routes to avoid unnecessary compaction of topsoil or to prevent disturbance of animals and plants outside of construction areas
- The access roads must be covered with gravel to minimize dust pollution and the gravel must be extracted from a permitted quarry

If required by the owner of the land the following may also apply with regard to access and vehicular movement on site:

- All Contractors, subcontractors and staff shall be identified by clothing with company logos and be in possession of valid SA identity documents
- Deliveries, removals etc. to be completed during normal working hours (unless otherwise agreed upon by the Construction Supervisor)
- No personnel shall stay permanently on site, unless permission to stay on site provided as part of the construction contract
- Access route diversions must be clearly demarcated by orange twine/danger tape on steel posts or temporary fencing
- The Contractor shall at their own cost document the existing condition of all access roads prior to commencement
- Should any damage occur to the access road as a result of the upgrade activities, the road will be rehabilitated to its original state with all costs borne by the contractor

3.10.2 APPROPRIATE USE OF MACHINERY

Contractor must always carefully consider what machinery is appropriate to the task while minimizing the extent of environmental damage.

- The contractor may not operate any machinery including a fuel driven compressor outside the demarcated area
- All vehicles and equipment must be routinely inspected for fuel and oil leaks and kept in good working order and serviced regularly. Leaking equipment must be repaired immediately or removed from the Site. When servicing equipment, drip trays must be used to collect the waste oil and other lubricants. Drip trays must also be provided in construction areas for stationary plant (such as compressors) and for "parked" plant (such as scrapers, loaders, vehicles). Drip trays will be kept free of water that will float the oil to overspill. All drip trays/bungs to attain a 120% capacity of the plant fuel/oil capacity
- Where practical, all maintenance of plant and machinery on site must be performed in workshops. If it is necessary to do maintenance outside of a workshop area, the Contractor must obtain the approval of the Engineer and the ECO prior to commencing activities
- Appropriate 4.5 kg (minimum requirement) dry powder SABS approved and service certified fire extinguisher must be a mandatory item on all vehicles working and moving on or off the construction site
- The servicing, repairs and maintenance of all construction machinery must take place at the designated service and maintenance yard and not along the proposed new road construction route

3.10.3 "No-Go" AREAS

Specifications of the Environmental Authorisation (EA), the Environmental Management Plan (EMP) or the On-Site Start-Up Meeting (OSSM) can require that certain areas are to be considered as "No go" areas as a result of their environmental significance or proximity to environmental significant features.

- Any and all areas identified in site sensitivity overlays as "no-go" areas are to be considered as such, and appropriately demarcated as such
- All areas of natural vegetation and streams/rivers outside of the development footprint should be considered "no-go" areas

- A Method Statement is to be submitted to the ECO by the Contractor, detailing the method of demarcation for protection of such conservation areas
- No-Go areas are out of bounds to the Contractor and staff, sub-contractors and staff or suppliers and staff or any other person involved in the project, without the written permission specified by the ECO
- The Contractor must ensure that, insofar as he has the authority, no person, machinery, equipment or material enters the designated "No Go" areas at any time
- All contractors must be made aware of the importance of these features and the consequences of non-compliance. All staff are to be made aware of the "no-go" areas in the induction and environmental awareness training
- Any areas identified by the applicant/landowner within the property outside of the development footprint
- All private property/farms outside of the works area are considered "no-go" areas, unless permission has been received from the ECO and written permission has been received from the landowner
- Natural vegetation outside of the development area will be considered no-go areas, unless for the purpose of alien vegetation clearing
- All drainage lines and watercourses outside the development footprint will be regarded as "no-go" areas

3.10.4 RESTRICTION OF WORKING AREAS

The approved layout plans will be used to establish the site demarcation (footprint). All relevant parties responsible for the day-to-day activities on the site will be present and made aware of the implication of the site demarcation. They include the:

- Environmental Consultant: EnviroAfrica
- Principle Agent
- Main Contractor: Project Site Manager
- Sub-contractor: Project contractor
- ECO: Environmental Control Officer

The proposed site will be demarcated prior to the commencement of any construction whatsoever, this includes site establishment, the moving of construction material or any other items onto the site, etc.

- The site will be demarcated with appropriate dropper poles. A single strand of orange baler twine is to be attached to the dropper poles to indicate boundaries and no-go areas for site personnel and vehicular movement. (Alternative fencing may be decided upon dependent on-site requirements). Other demarcation measures can be used if approved by the ECO
- The construction area i.e. road, stockpile areas and development footprint etc. must be demarcated and fenced off with dropper poles and orange baler twine approximately 1m high is considered adequate. The demarcation will be agreed on during the start-up meeting
- All fencing and fence placement/positioning must be approved by the ECO on site
- Work areas and access routes must be clearly demarcated to minimise environmental impact
- In the event that sensitive features are threatened by construction activities, temporary fencing off of these areas (for individual areas such as trees or rocks) or the construction area (when working in a mainly natural environment) is recommended
- NB: Also note the requirements discussed under the following paragraphs: 3.10.5; 3.10.2; 3.10.8; 3.10.6; 3.10.7
- The Contractor must maintain in good order all demarcation, fencing and barriers for the duration of construction activities, or as otherwise instructed
- Demarcation may not be moved, re-located or altered or changed without the approval of the ECO
- Any temporary fencing removed for the execution of any portion of the works is to be reinstated by the Contractor as soon as practicable.
- The Contractor at the end of the contract must remove all demarcation, fencing or barriers not forming part of the final works on site

3.10.5 PROTECTION OF NATURAL VEGETATION

Habitat fragmentation is usually defined as a landscape-scale process involving both habitat loss and the breaking apart of habitat. Habitat loss has large, consistently negative effects on biodiversity. Habitat fragmentation per se, has much weaker effects on biodiversity, but could be just as negative. As such the construction activities must endeavour to minimise its impact on any remaining natural features and natural corridors.

- All significant biodiversity features identified during the environmental assessment stage, must be mapped and identified as “No-Go” areas on the site plans and protected measures must be installed (demarcated). Only alien vegetation clearing may take place within the natural areas outside the demarcated works area
- Except to the extent necessary for the carrying out of the works, no natural indigenous flora may be removed, damaged or disturbed
- Trapping, poisoning and/or shooting of animals is strictly forbidden. No domestic pets or livestock are permitted on Site
- Where the use of herbicides, pesticides and other poisonous substances are to be used, the Contractor must submit a Method Statement
- The Contractor may not deface, paint, damage or mark any natural features, if these should occur (e.g. trees, rock formations, buildings, etc.) situated in or around the Site for survey or other purposes unless agreed beforehand with the Engineer and the ECO. Any features affected by the Contractor in contravention of this clause must be restored/rehabilitated to the satisfaction of the Engineer and the ECO
- All incidents of harm to any animal or natural vegetation (apart from the agreed upon areas) must be reported to the ECO

3.10.6 PROTECTION OF FAUNA AND AVI-FAUNA

Trapping, poisoning and/or killing of animals and birds is strictly forbidden. No domestic pets or livestock are permitted on site. Many slow-moving animals, local amphibian and other species follow instinctive movements along roadside corridors where they travel from place to place.

- Every effort must be implemented on a daily on-going basis by the contractor to ensure that the construction areas have been checked for any animals and to ensure their removal and protection from direct and in-direct impacts during the construction activities. Special cognisance of tortoises must be taken on site
- Any open trenches must not be left open for extended periods of time. If trenches are to be left open for extended periods, these should be fenced/secured to prevent livestock and other animals from falling into trenches
- The removal of fauna from the site must be done in accordance with the requirements of the Nature Conservation Ordinance regulating these activities
- Environmental corridors and “No-Go” areas must be demarcated and protected

3.10.7 CLEARING OF VEGETATION, STRIPPING AND CONSERVATION OF TOPSOIL

The contractor shall take all reasonable steps to minimise the impact of his activities on the environment. If natural vegetation must be removed for construction purposes, the natural vegetation shall be rescued, re-used (e.g. stabilizing the area after construction or re-vegetating other impacted areas) in such a way that it enhances the remaining natural veld. By the same principle, topsoil (which contains the remaining natural seeds as well as possibly many bulb species) must be carefully removed and stored or re-used for rehabilitation or impacted areas in the immediate vicinity.

Vegetation clearing:

- A Method Statement must be submitted detailing the methods to be used for vegetation clearing
- All cleared areas must be stabilised as soon as possible
- Burning of cleared vegetation on site is prohibited

- The burying of cleared vegetation or use as part of backfill or landscape shaping is prohibited unless written approval is obtained from the ECO
- Cleared vegetation may be used for mulch or slope stabilisation of the Site
- Should bulk vegetation be removed from the designated working areas (footprint area) then tall vegetation shall first be removed through brush cutting and chipping of larger shrub material; this may be added to the topsoil material stockpiles as mulch
- Unless otherwise agreed upon, only indigenous plant material shall be used for this purpose

Topsoil removal

- Prior to any activities within the demarcated work areas, topsoil material shall be removed to a depth of 300 mm or deeper if specified by the engineer in consultation with the ECO, and stockpiled in a designated area for use in rehabilitation of the site post construction. Only sufficient topsoil is to be stored for rehabilitation purposed
- Topsoil from the still relatively natural area (the top 15 -20 cm) should be removed and be used for rehabilitation after construction on site or in the immediate vicinity of the site
- Any area where the topsoil will be impacted by construction activities, including the construction offices and storage areas, must have the topsoil stripped and removed and covered with herbaceous vegetation (other than alien species), overlying grass and other fine organic matter and stockpiled for subsequent use in rehabilitation
- Topsoil storage areas must be convex and should not exceed 2 m in height. The Contractor must ensure that the material does not blow or wash away. The use of a bund wall should be considered, if appropriate, for the storage of the topsoil
- The topsoil should be stored outside the 1:50 flood level within demarcated area
- Topsoil shall be kept separate from overburden and shall not be used for building or maintenance of access roads
- Topsoil must be treated with care, must not be buried or in any other way be rendered unsuitable for further use (e.g. by mixing with spoil) and precautions must be taken to prevent unnecessary handling and compaction
- In particular, topsoil must not be subject to compaction greater than 1 500 kg/m² and must not be pushed by a bulldozer for more than 50 m. Trucks may not be driven over the stockpiles
- Topsoil from different soil types must be stockpiled separately and replaced in the same areas from which they were taken if this proves to be the case. Specific attention should be given to the areas that may house rare and threatened species
- Topsoil areas must be demarcated in order to ensure the safekeeping of topsoil and to separate different stockpile types

3.10.8 EROSION AND SEDIMENTATION CONTROL

The Contractor must take appropriate on-going and active measures to prevent erosion resulting from his own construction activities and operations as well as storm water control measures to the satisfaction of the ECO. During construction the Contractor must protect areas susceptible to erosion by installing all the necessary temporary and permanent drainage works as soon as possible.

In order to achieve erosion and sediment control, the following are applicable to all sites:

- No new development, without written authority approval, will be allowed on slopes greater than 12% (CARA, regulation 3). If applicable terraces will be made in accordance with agricultural regulations.
- Install erosion and sediment controls before work starts and maintain these features throughout the construction and operational phases (as applicable)
- Leave as much vegetation as possible
- Install temporary fences to define “No Go” areas in those areas that are not to be disturbed.
- Divert run-off from upslope away from the site, but ensure that it does not cause downstream erosion For example, dig drainage channels (catch drains sized to accommodate the upslope catchment)

- Install sediment controls down slope of the site to catch sediment (if applicable)
- Inspect and maintain erosion and sediment controls regularly
- Limit vehicle movement to the site and control access points. Clearly mark such access points and inform all suppliers
- Save and re-use topsoil during revegetation. Never store topsoil around trees as this may kill them. Spread the topsoil back when the work is finished and revegetate the site as soon as possible to control erosion. Remove the sediment and erosion controls only after revegetation was successfully implemented
- Store all stockpiles and building materials behind sediment fences. Cover them with plastic to prevent erosion by wind
- It is illegal to discharge water into a public stream if the quality does not conform to the required health or water standards. Other measures as may be necessary must be taken to prevent the surface water from being concentrated in streams and from scouring the slopes, banks or other areas. Any potential hazardous fluids / materials must be protected from the rain to prevent them being washed into storm water channels. All such measures must be discussed with and approved by the ECO
- If required, build a dam below any works areas. Surround the wash-out area with a sediment fence that slows down the water flow. Filter or settle-out all water pumped off the site. The water must be clear before it enters the storm water system or creeks. Gypsum can be applied to muddy (turbid) water to help clay particles settle
- Fill in all trenches immediately after services have been laid
- As far as possible, work must be done during the dry season, low flow conditions
- Downstream placement of sediment containing measures
- Due diligence to limit sediments washing down the river
- Vegetation of ramps and shoulders

3.10.9 ALIEN INVASIVE MANAGEMENT PLAN

In accordance with Regulation 15 and 16 of the Conservation of Agricultural Resources Act, 1983 (Act no. 43 of 1983) (CARA) as amended, all listed alien invasive plant species must be managed on any land in SA. As such an alien invasive management plan may be required to be implemented during construction and operation phase of the project. If such a plan is required, it must include mitigation measures to reduce the invasion of alien species and ensure that the removal of alien species is undertaken. Wetlands and rivers are especially susceptible to many of species.

- In accordance with CARA all identified alien invasive plants encountered on the property and its immediate surroundings must be controlled
- All invasive alien plants must be cleared from the site and remainder of the landowner's property
- An invasive alien plant monitoring, eradication and control plan should be compiled to effectively remove all infestations on the property. This will allow for a degree of natural passive restoration of natural vegetation
- All alien invasive species must be identified and removed from each site and its immediate surroundings. This is especially true for any remaining natural corridor on site
- Any exotic trees currently growing in riparian zones on site should be cut and the stumps treated with herbicide to prevent re-growth
- No vegetation may be buried or burned on site
- Where the use of herbicides and other poisonous substances are to be used, the Contractor must submit a Method Statement

The invader status of the various invasive alien species in South Africa is described in accordance with Regulation 15 and 16 of the Conservation of Agricultural Resources Act, 1983 (Act no. 43 of 1983) (CARA) as amended (the 3 categories and its control are summarised underneath).

Category 1 (Declared Weed)

- Prohibited on any land or water surface in South Africa
- Must be controlled or eradicated (except in biological control reserves)

Category 2 (Declared Invader – commercial value)

- Allowed only in demarcated areas under controlled conditions
- Outside of controlled areas invaders must be controlled or eradicated where possible
- Prohibited within 30 m off the 1:50 year flood line of watercourses or wetlands unless authorization has been obtained

Category 3 (Plant Invaders – ornamental value)

- Allowed only in areas where they were already in existence with the promulgation of the regulations.
- Prohibited within 30 m of the 1:50 year flood line of watercourses or wetlands unless authorization has been obtained.
- All reasonable steps must be taken to ensure that they do not spread.
- Propagative materials of these plants (e.g. seeds or cuttings) may no longer be planted, propagated, imported, bought, sold or traded in any way.

3.10.10 PROTECTION OF ARCHAEOLOGICAL & PALEONTOLOGICAL REMAINS

Archaeological remains are ancient man-made objects, structures, or ancient burials that have been preserved on the earth's surface, underground, or underwater and serve as the historical sources that make it possible to reconstruct the past history of human society, including mankind's prehistory. Palaeontology, on the other hand, is the study of prehistoric life. It includes the study of fossils to determine organisms' evolution and interactions with each other and their environments (their paleoecology). Palaeontology lays on the border between biology and geology, and shares with archaeology a border that is difficult to define.

- Basic archaeological remains include work tools, weapons, domestic utensils, clothing, and ornaments; settlements including campsites, fortified and unfortified settlements, and separate dwellings; ancient fortifications; the remains of ancient hydraulic structures; ancient agricultural fields; roads; mining pits and workshops; ancient burial grounds and various burial and religious structures (stelae, stone figurines, stone fish monoliths (vishaps), menhirs, cromlechs, dolmens, sanctuaries); drawings and inscriptions carved into individual stones and cliffs; and architectural monuments. Archaeological remains also include ancient ships and their cargoes that sank in rivers and seas and settlements that came to be underwater as a result of shifts in the earth's crust
- Should any archaeological remains or palaeontological resources (including but not limited to fossil bones and fossil shells, coins, indigenous and/or colonial ceramics, any articles of value or antiquity, stone artefacts and bone remains, structures and other built features, rock art and rock engravings) are discovered during construction they must immediately be reported to SAHRA and must not be disturbed further until the necessary approval has been obtained from SAHRA
- Should any human remains/burial or archaeological material be disturbed, exposed or uncovered during construction, these should immediately be reported to the South African Heritage Resources Agency (021 462 4502). The ECO and ER are also to be informed. An archaeologist will be required to remove the remains at the expense of the developer
- Note that the Contractor may not, without a permit issued by the responsible heritage resource authority; destroy, damage, excavate, alter, deface or otherwise disturb any archaeological site or archaeological material. The latter is a criminal offence under the Heritage Resources Act
- A Fossil Find Procedure must be implemented, should any fossil material be discovered during construction, this must be safeguarded (preferably *in situ*) and the Environmental Control Officer (ECO) should alert SAHRA so that appropriate mitigation (e. g. recording, sampling, or collection) can be taken by a professional palaeontologist

3.10.11 STORAGE OF CONSTRUCTION MATERIAL AND STOCKPILING

The Contractor must provide a method statement (for approval by the ECO) of the construction activities which will indicate:

- The type and quantity of material to be stored
- Whether any oil contaminated/containing equipment will be stored
- How (including what type of vehicles will be required) it will deliver the material on site at the necessary storage area
- Whether there is any risk of spill or runoff of any building materials or chemicals and how this is to be mitigated
- No material is to be stored or stockpiled within any riparian zones or areas of natural vegetation. Disturbed areas, should be used for stockpiling

In addition:

- The Contractor must ensure that any delivery drivers are informed of all procedures and restrictions (including "no-go" areas) required to comply with the Specifications. The Contractor must ensure that these delivery drivers are supervised during off-loading, by someone with an adequate understanding of the requirements of the Specifications
- All manufactured and/or imported material must be stored within the demarcated area, and, if so required, out of the rain. All lay down areas outside of the construction camp must be subject to the Engineer and the ECO's approval in such a way as not to cause a nuisance or environmental damage
- All building materials are to be prepared at the batching plant, to enable the effects of cement and other substances, and the resulting effluent to be more easily managed
- It is essential that any imported material i.e. base material for road works, building sand, bedding base sand for pipe / cable lines etc. must be screened and of which the origins must be identified prior to arriving at the receiving environment, this must be approved by the Engineer/ECO
- Special care must be taken to prevent bringing in materials contaminated with seed of Invasive Alien Plants. Contractors shall not import construction materials such as sand, gravel or fill contaminated with seed of Invasive Alien Plants, or quarried from areas surrounded by Invasive Alien plant species such as Port Jackson or Rooikrans
- The Contractor must negotiate appropriate space on for this purpose on an area away from natural vegetation and any wetland habitat with the ECO
- The Contractor must ensure that all staff, contractors and subcontractors are aware of and keep material within these designated storage areas. The Construction Supervisor shall ensure that the consultant team is familiar with same
- Contractors will not be allowed to store new construction material on the sides of the access road, or within natural vegetation or next to the existing access road
- Stockpiling of gravel, cut, fill or any other material including spoil should only be allowed in degraded areas or areas within the development footprint.
- Any area used for stockpiling and not covered by building development must be returned to at least the state they were in before stockpiling and it must be ensured that the erosion potential of these areas is not increased
- The Contractor must ensure that the material does not blow or wash away (especially into riparian zones) or mix with each other. If the stockpiled material is in danger of being washed or blown away, the Contractor must cover it with a suitable material, such as hessian, netting or plastic

3.10.12 OIL STORAGE AND MANAGEMENT

An important potential environmental impact is oil spills from any oil filled equipment and machinery that may occur during transportation, operation or storage. The following conditions shall apply:

- Vehicles must be checked for oil leaks prior to going on site
- Care should be taken to prevent any potential oil spillage during upgrading activities

- Sufficient measures should be put in place to ensure that any potential oil spills are mitigated
- An oil spill kit should be available on site at all times during the construction activities
- Oil containment facilities should be provided for any oil filled equipment onsite
- All oil spills must be reported to the ECO within 24 hours, indicating the containment and rehabilitation measures implemented

3.10.13 STORING OF PETROLEUM PRODUCTS

Petroleum fuels contain harmful substances known to cause health problems and can easily have adverse effects on water quality, and the environment. Petroleum spills can move rapidly into the soil and quickly contaminate drinking water. In order to prevent pollution, it is important to use proper methods when handling, using, and storing diesel fuel, gasoline, kerosene, or other petroleum products.

The South African National Standards pertaining to the installation of a storage tank include:

- Sans 310, which requires that an aboveground storage tank be of sufficient structural strength, based on sound engineering practices, to withstand normal operations and use
- Sans 1668, for fibre-reinforced plastic tanks for the underground storage of petroleum products
- Sans 10089-1, which deals with the storage and distribution of petroleum products in aboveground bulk installations
- Sans 1535, for glass- reinforced polyester-coated steel tanks, for the underground storage of hydrocarbons and oxygenated solvents, which are intended to be buried horizontally

Above ground fuel storage tanks (if required)

Any fuel storage proposals must be cleared by the ECO before any storage or stockpiling takes place. If the contractor proposes to install above-ground fuel storage tanks for use during the construction phase of the project, the following basic requirements must be adhered to:

- A Method Statement, explaining the method of storage and mitigation measures to prevent spillages must be submitted to the ECO and accepted prior to the installation of such a fuel storage facility (please note that storage of any dangerous goods/fuel of 30 cubic meters or more require environmental authorisation)
- The fuel tank must be placed within a completely sealed concrete bund (containment structure) which must be able to contain at least 120% of the total capacity of the fuel tank
- The bunded area should be built to be at least a third wider (on all sides) than the base of the fuel tank in order to maximise its capability to contain spillages and leakages
- The fuel distributor must also be located within bunded area to better prevent against accidental spillages during refuelling
- In addition, drip trays are to be used during refuelling
- All vehicles, equipment, fuel and petroleum services and containers must be maintained in a good condition that prevents leakage and possible contamination of soil or water supplies
- Fuel storage areas must comply with general fire safety requirements
- Fuel storage areas must be at least 100m from any watercourses

Storing of smaller quantities of fuel or oil

Any fuel storage proposals must be cleared by the ECO before any storage or stockpiling takes place. If the contractor proposes to use only small fuel storage facilities (<200 litres) the following basic requirements must be adhered to:

- Fuels and oils must be safely located out of harm's way from the elements and safety and fire prevention must be strictly adhered to
- All fuel oil containers must be placed within suitable drip trays to prevent accidental spillage of oils and fuels

- A suitable leak proof container for the storage of oiled equipment (filters, drip tray contents and oil changes etc.) must be established
- All spills are to be recorded in the ECO diary

3.10.14 STORING OF HAZARDOUS SUBSTANCES

If potentially hazardous substances are to be stored on site, the Contractor must submit a Method Statement detailing the substances and/or materials to be used, together with the storage, handling and disposal procedures of the materials to the ECO.

- Hazardous materials must be stored under lock and key in designated areas with properly displayed and visible warning signs
- No works related to the submitted Method Statement may commence until the Method Statement has been studied and approved in writing
- An effective monitoring system to detect any leakage or spillage of all hazardous substances during their transportation, handling, use and storage must be implemented. This must include precautionary measures to limit the possibility of oil and other toxic liquids from entering the soil or storm water systems
- Measures to protect hydrological features such as streams, rivers, pans, wetlands, dams and their catchments, and other environmental sensitive areas from construction impacts including the direct or indirect spillage of pollutants must be implemented
- **Paints:** No paint products may be disposed of on Site and brush/roller wash facilities must be established to the satisfaction of the Engineer and the ECO. Oil based paints and chemical additives and cleaners such as thinners and turpentine must be strictly controlled. A Method Statement detailing the paint management procedures is required
- **Hazardous building materials:** Hazardous building materials must be identified and dealt with in accordance with the relevant safety and health legislation. All such material must be separated on Site and disposed of at appropriate licensed disposal sites. The Contractor must supply the ECO with a certificate of disposal

3.10.15 USE OF CEMENT OR CONCRETE

The Contractor is advised that cement and concrete are highly hazardous to the natural environment because of the high pH levels of the material, and the chemicals contained therein. Wash-out water with high pH is the number one environmental issue for the ready-mix concrete industry. The alkalinity levels of wash water can be as high as pH 12, which is toxic to fish and other aquatic life.

The Site Supervisor or Contractor must indicate the need for and the proposed location of concrete batching plants which includes the location of cement stores, sand and aggregate stockpile areas. A Method Statement indicating the layout, type of concrete batching preparation (dry or wet mix). The site agent must indicate on the Method Statement proposed total volume of concrete that is needed for the completion of the entire project.

Concrete/cement mixing:

- Concrete and cement may only be mixed on existing hard surfaced areas, or edged mortar boards or a suitable container. Concrete may not be mixed or stored directly on the ground under any circumstances
- The visible remains of the batch and concrete, either solid, or from washings, must be physically removed immediately and disposed of as hazardous waste
- Washing of equipment shall be done in a container to prevent any runoff of contaminated washing water
- Extreme care must be taken to limit the amount of water contaminated by washing equipment. Water from concrete washing can be re-used in concrete mixes or must be stored in drums, then removed from the site and disposed of at a licensed municipal dump site

Concrete batching areas

The following procedures must be implemented to control wastewater run-off from concrete batching plant locations:

- The location of concrete batching areas must be approved by the ECO (if possible/appropriate, the use of ready-mix concrete is preferred)
- Concrete batching facilities must have suitable bunding methods in place to ensure minimal wastewater run-off occurs during batching operations
- Contaminated water may not enter a natural or man-made (e.g. trench/sloot or dam) water system. Preventative measures include establishing sumps from where contaminated water can be either treated in situ or removed to an appropriate waste site
- Dry mixing batching areas to be carefully placed in consultation with the ECO
- Cement bags are to be stored securely out of harm's way from the elements (wind and rain). Bags have to be covered and placed on plastic sheeting. Used cement bags must be disposed of on a regular basis via the solid waste management system, and must not be used for any other purpose
- Sand and stone used for cement or concrete batching must be stored on plastic layers (or on ECO approved disturbed areas) in order to prevent contamination of the natural environment
- Cleaning of equipment and flushing of mixers must not result in pollution of the surrounding environment. All wastewater resulting from batching of concrete must be disposed of *via* the contaminated water management procedure
- Excess or spilled concrete must be confined within the works area and all visible remains of excess concrete must be physically removed and disposed of on completion of cement work. Washing the remains into the ground is not acceptable. All excess aggregate must also be removed
- Wash-down areas must be confined to within the concrete batching areas only

3.10.16 FIREFIGHTING

Adequate firefighting equipment according to the fire hazard during the construction period must be available on site and in good working order (at least one type of ABC (all purpose) minimum 4.5 kg extinguisher and 3 fire beaters per working area). The persons on site must be trained in the use of such equipment.

- The main contractor must provide a list of all authorities involved in firefighting in the region. This list must include emergency contact numbers and must be visible at the site office
- Welding, gas cutting or cutting of metal will only be permitted inside the working areas
- The Contractor must pay the costs incurred to organizations called to put out any fires started by him. The Contractor must also pay any costs incurred to reinstate burnt areas as deemed necessary by the landowner
- It is required that contractors have available the emergency telephone numbers of the nearest local Fire Fighting Station and that an emergency firefighting re-action plan has been drawn up with on-site workers and the resident landowner / farmer
- No on-site fires are permitted
- No firewood may be collected on site or from the surrounding natural area

3.10.17 EMERGENCY PROCEDURES

It is the responsibility of the contractor to assess the potential risks to the environment as a result of the project. As such, the contractor must have the necessary standard emergency operating procedures in place to deal with any potential emergency such as oil spills or fire.

- All staff should be made aware of the necessary basic emergency procedures in the event of an emergency including injuries to staff. The appropriate equipment and identified personnel to deal with such basic emergencies should be available on site
- All staff on site should wear hi-viz vests when on site

- **Fire:** The Contractor must advise the relevant authority of a fire as soon as one starts and must not wait until he can no longer control it. The Contractor must ensure that his employees are aware of the procedure to be followed in the event of a fire
- **Hazardous Material Spills:** The Contractor must ensure that his employees are aware of the procedure to be followed for dealing with spills and leaks, which must include notifying the Engineer, the ECO and the relevant authorities. Treatment and remediation of the spill areas must be undertaken to the reasonable satisfaction of the ECO and Local Authority

3.10.18 SOLID WASTE MANAGEMENT

Waste refers to all solid waste, including domestic waste, hazardous waste and construction debris. The Contractor is responsible for the establishment of a refuse control system (which must consider recycling wherever possible) that is acceptable to the ECO. Disposal arrangements must be made in advance and cleared with the ECO before construction starts.

- No littering or on-site burying or dumping of any waste materials, vegetation, litter or refuse may occur.
- All solid waste must be disposed of offsite at an approved landfill site in terms of section 20 of the Environment Conservation Act (Act No. 73 of 1989). The Contractor must supply the ECO with a certificate of disposal
- The Contractor must provide problem animal- and weatherproof bins with lids of sufficient number and capacity to store the solid waste produced on a daily basis. The lids must be kept firmly on the bins at all times. Bins must not be allowed to become overfull and must be emptied regularly
- Waste from bins may be temporarily stored on Site in a central waste area that is weatherproof and scavenger proof and which the Engineer and the ECO has approved
- Any hazardous waste must be disposed of at a registered hazardous waste disposal site and certificates of safe disposal must be obtained
- All waste generated during the decommissioning and reconstruction activities must be removed by the Contractor as soon as possible, and within the period specified in the EMP and disposed of at a registered landfill site
- The Contractor must make provision for workers to clean up the Contractor's camp and working areas on a daily basis so that no litter is left lying around and so that the site is in a neat and tidy state. The Contractor must remove from site the refuse collected at least once a week
- Waste and any excess material (and concrete slabs and pipes) should not be dumped into any riparian zones

3.10.19 TOILETS AND ABLUTION FACILITIES

The Contractor must provide suitable sanitary arrangements at designated points of the construction site for all site employees. A minimum of one toilet must be provided per 15 persons at each working area (station) or as stipulated in the Management plan.

- The toilet must be within easy reach (max 300 m) of the working area and be in good working condition and cleaned on a daily basis. Toilet paper must be provided. The toilets must be emptied on a weekly basis or when full or when instructed by the ECO on site
- Toilets should be placed at least 50m from any watercourses
- Toilets should be adequately screened from any public areas or residences
- Disposal arrangements must be made in advance and cleared with the ECO before construction starts. Sanitation provision and servicing must be to the satisfaction of the ECO
- The Contractor must ensure that toilets are emptied prior to any builders' holidays, and/or weekends
- Toilets must be of a neat construction and must be provided with doors and locks and must be secured to prevent them blowing over
- NB: No burying of any waste material on or near the construction site nor anywhere on the surrounding property is permitted

3.10.20 DISCHARGE OF CONSTRUCTION WATER

Potential pollutants of any kind and in any form must be kept, stored, and used in such a manner that any escape can be contained and the water table not endangered. This particularly applies to water emanating from runoff from construction areas/fuel depots/workshops/truck washing areas.

- The contractor, being responsible for the construction and effective containment and maintenance of settlement ponds must ensure that the surrounding environment is not adversely affected as a result of construction activities
- Wash down areas must be placed and constructed in such a manner so as to ensure that the surrounding areas are not polluted. Contaminated water includes water that is carrying excess sediment due to construction activities
- Contaminated water storage facilities must not be allowed to overflow and appropriate protection from rain and flooding must be implemented
- Contaminated water that is removed from site must be disposed of at a facility approved by the ECO and Local Authority
- No contaminated water that does not meet the water quality standards and criteria under the National Water Act may be released into a natural system, whether it is to surface or groundwater
- All cement effluent from mixer washings, and run-off from batching areas and other work areas must be contained in suitable sedimentation ponds
- Sedimentation ponds must be allowed to dry out on a regular basis to allow for solid material to be removed
- This material must be disposed of in a suitable manner, depending on the nature of the material, and to the discretion of the ECO

3.10.21 EATING FACILITIES

The Contractor must designate eating areas for the approval of the ECO, which must be clearly demarcated. No eating of meals must take place outside these designated areas without the approval of the Contractor/ESO.

- The feeding, or leaving of food for animals are strictly prohibited
- Sufficient waste bins must be present in this area and emptied regularly
- The contractor must supply cooking facilities that are suitable for the environment and are not liable to cause the outbreak of fires
- The contractor must supply all construction staff with adequate clean water, and may not be sourced from surrounding farms/ landowners, unless written permission is granted by the landowner
- No overnight camping/stay on site allowed. If overnighing is necessary for security purposes then it must be cleared with the ECO on site
- No washing in dams or streams are allowed
- Eating areas that are allocated for workers must be established in an environmentally acceptable manner and in line with all Environmental Health & Safety Act regulations. All on site and on route workers temporary eating areas must have acceptable toilet and refuse management systems in place and these areas must have suitable refuse receptacles' available for the containment and disposal of general litter and refuse

3.10.22 DUST CONTROL

The Contractor must take all reasonable measures to minimize the generation of dust as a result of construction activities (but must also take into account possible water constrictions of the area).

- The onsite construction site agent must take into account prevailing wind strength and wind direction and must have preventative measures on standby to minimize dust pollution that may cause damage to people and property
- The liberation of dust into the surrounding environment shall be effectively controlled by the use of, inter alia, water spraying and/or other dust-allaying agents. The speed of haul trucks and other vehicles

must be strictly controlled to avoid dangerous conditions, excessive dust or excessive deterioration of the road being used

- In agricultural areas, earth-works should be done after the harvest season, or as agreed upon by the landowner

3.10.23 RESTORATION AND REHABILITATION

The Contractor must ensure that all structures, equipment, materials and facilities used or created on site for or during construction activities are removed once the project has been completed. On completion of the project or phase, all areas impacted by the construction activities must be reinstated and/or rehabilitated to the satisfaction of the ECO with emphasis on the following:

- Immediately after the demolition of the camp site or once construction has been completed, the contractor shall restore the site to its original state, paying particular attention to its appearance relative to the general landscape. This must be done as soon as possible after construction has ended to ensure no possible environmental degradation of the site as a result of erosion, alien vegetation establishment etc.
- The contractor's procedure for rehabilitation shall be approved by the ECO and Engineer
- Site offices must be removed and the areas rehabilitated or reinstated to the satisfaction of the ECO
- Labourer's facilities (if applicable) must be removed and the areas rehabilitated or reinstated to the satisfaction of the ECO
- All construction site areas must be rehabilitated or reinstated to the satisfaction of the ECO
- All temporary fencing and demarcation must be removed and the areas reinstated to the satisfaction of the ECO
- Temporary storage areas must be rehabilitated or reinstated to the satisfaction of the ECO
- All remaining construction material must be removed and the areas rehabilitated or reinstated to the satisfaction of the ECO
- Any old road sections not used for operational purposes during the operational phase should be rehabilitated after construction to allow for regrowth of vegetation

Any additional **disturbed** areas must be rehabilitated or reinstated to the satisfaction of the ECO. This shall include but not be limited to:

- Earthworks to reinstate the physical characteristics of the site. Here attention to the natural vertical and lateral heterogeneity in landform shall guide the reinstatement of natural areas
- Replacement of topsoil material – care shall be taken to ensure that the same material that was removed from each area is replaced there, since this will carry the seed complement appropriate for re-establishment of each plant community type
- Final landscaping by machine, but landscaping by hand may be required in many areas under rehabilitation
- Re-seeding and / or replanting of rehabilitated areas
- The Contractor shall not be permitted to use fertilisers or pesticides
- It is imperative that any potential erosion problems are addressed. This may require subsequent site visits to monitor the efficacy of erosion control measures

3.10.24 LAND MANAGEMENT

- Vehicles accessing the construction site must be made aware of driving in hazardous road conditions, sharp bends, narrow roads, bad weather, on or near children or domestic animals along the road
- Vehicle movements should be kept to a minimum during rain to avoid damage to access roads
- No fences or gates on the relevant construction property must be damaged. All access gates to the property (construction site) to be kept closed at all times to prevent domestic and or wild animals from getting out. Access by unauthorised personnel should be controlled. The access gates to the construction areas must always be closed

- Soil erosion must be prevented at all times along the access roads and around construction areas

3.10.25 SOCIO-CULTURAL ISSUES

- Neighbouring community, adjacent landowners and occupiers etc. must be treated with respect and courtesy at all times
- The cultural lifestyles of the communities living in close proximity to the construction areas must be respected
- Hours of work on the site shall be limited to normal working hours, as accepted by the local authority
- Should construction be required outside of these times, permission is to be obtained from the local municipality, in consultation with the ECO and the surrounding landowners

3.11 EMERGENCY PREPAREDNESS & RESPONSE

The following potential emergency situations have been identified and include the procedure for responding to, and for preventing and mitigating the environmental impacts that may be associated with them (also refer to Penalties and Fines).

3.11.1 ACCIDENTAL FIRES

Fire safety is a very real risk and must be stringently controlled. No fires will be permitted on site for any reason. If required, a designated smoking area will be provided, and clearly demarcated and signposted, with a facility for safe containment and disposal of cigarette butts.

The following measures must be implemented:

- Adequate firefighting equipment must be available on site and in good working order (including at least one type of ABC (all purpose) minimum 4.5 kg fire extinguisher and 3 fire beaters per working area). The persons on site must be trained in the use of such equipment
- The main contractor must provide a list of all authorities involved in firefighting in the region. This list must include emergency contact numbers and must be visible at the site office
- The contractors must establish an emergency procedure (with contact numbers) to the satisfaction of ECO (whenever work is done in any fire prone areas)

3.11.2 HYDROCARBON SPILLS

Since the project is relatively small, no fuel storage or distribution facilities are expected to be established. As a result, the significance of any spill is much reduced. The following must be observed:

- Vehicles will arrive on site already fuelled for the project
- If additional fuel is needed, it will be brought in as needed (minimal volumes) and refuelling will be done using a pump and not a funnel (to minimize the risk of spills)
- Spill trays shall be used during re-fuelling
- In the case of accidental spillages or leakage, the contractor will be responsible for immediate containment and corrective action (e.g. stopping the leakage), and to inform the Construction Supervisor and ECO
- The ECO will recommend the best possible environmental solution
- The Contractor will be liable for any costs incurred

3.11.3 CONCRETE/CEMENT SPILLAGES

The Contractor/supplier will be liable for the safe and correct deliverance of substantial loads of concrete or cement.

- Should a spill occur the Contractor/supplier will be liable for all costs of the rehabilitation needed

4. OPERATIONAL EMP (OEMP)

The most important part of the operational phase will be to ensure that the site is meticulously maintained and that the operations are carefully monitored. Zero Carbon Charge will remain overall responsible for the environmental performance of the site and must be aware of the legal requirements and obligations. The applicant must also be aware of the legal action that can be taken against him/her as a person with regards to negligence leading to environmental pollution.

The owner or delegated responsible person must implement an operational and maintenance management plan for the lodge development. This plan must include:

- Water management and monitoring
- Erosion management
- Waste and pollution management
- Fire Management
- Minimise dust
- Protection of indigenous natural vegetation and fauna
- Alien vegetation removal
- Specific monitoring and operational instructions
- Emergency plans which will cover all reasonable aspects of the operations which might lead to environmental pollution or degradation

4.1 TRAFFIC ACCESS ROUTES AND HAUL ROADS

The Operator of the site must control the movement of all vehicles and plant including that of his suppliers so that they remain on designated routes. In addition, such vehicles and plant must be so routed and operated as to minimise disruption to regular users of the routes not on the Site.

- A Traffic Management Plan should be compiled for each site, with cognisance of vehicles entering and exiting the facility along major roads
- On public roads adjacent to the Site, vehicles will adhere to municipal and provincial traffic regulations.
- Only approved access roads may be used.
- All measures must be implemented to minimize impacts on local commuters e.g. limiting maintenance/service/operational vehicles travelling on public roadways during the morning and late afternoon commute time and avoid using roads through densely populated built-up areas so as not to disturb any existing retail and commercial operations.

4.2 ENERGY MANAGEMENT

All reasonable steps must be taken to ensure the efficient management of energy. Energy management and conservation measures must be propagated and encouraged. The objective of energy management will be to encourage the conservation of energy, for example:

- Ensure that cooling units are located and operated to conserve energy
- Install energy-efficient appliances
- Install energy efficient lightning
- Insulate water heaters and hot water pipes (insulating hot water pipes from the water heater to the source are another way to conserve)
- Disconnect or switch- off units/appliances which are not in use
- Monitor different energy uses (e.g. electricity, fuels and gas)

4.3 WATER MANAGEMENT

- Ensure that all additional water uses are correctly registered with the Department of Water and Sanitation (e.g. agri-industrial use) (if required)
- Water conservation measures such as low flow taps, high pressure hoses, dual flush toilets, water wise gardens, rainwater harvesting and tanks etc. must be encouraged and implemented
- Every reasonable effort must be made to reduce the long-term water demand
- Environmental training of personnel must include water conservation awareness
- A monthly water monitor program with the aim of ever reducing the water usage must be implemented (records must be kept)

4.4 EROSION AND SEDIMENT CONTROL

Soil erosion (through wind & water) removes valuable topsoil which is the most productive part of the soil profile (containing plant nutrients, seeds and bulbs). Development disturbs and loosens soils which can easily lead to erosion. The plants and animals that depended on that soil can no longer survive, and the plants that once grew that cannot re-establish itself because the seed store is gone. Soil may then have to be brought back from elsewhere, increasing the cost of the project and the risk of importing weeds and other waste or toxic material. In accordance with the Conservation of Agricultural Resources Act, 1983 (Act No. 43 of 1983) (CARA), the aim of erosion management is to prevent any form of soil erosion through proactive thinking and prevention as well as immediate rehabilitation.

In order to achieve erosion and sediment control, the following are applicable to all properties:

- Inspect and maintain erosion and sediment controls on a regular basis and ensure that it can accommodate the upslope catchment
- Leave as much vegetation as possible
- Install permanent fences to define 'no go' areas in those areas that are not to be disturbed
- Install sediment catchment controls down slope of the site to catch sediment (if applicable). This must be done as soon as possible by the Applicant and should be permanent
- Driving off road, or over the edge of the road to avoid puddles, or obstacles, should be avoided. Obstacles should be removed to avoid vehicles from having to drive off the road surface
- The road surface must be maintained
- Maintain storm water management infrastructure
- Due diligence to limit sediments washing down the river

4.5 WASTE & POLLUTION MANAGEMENT

An integrated waste management approach based on waste minimisation (e.g. reduction, recycling, re-use and disposal) must be encouraged. Poor waste management can lead to adverse environmental impacts (e.g. odours, pollution and visual impact) as well as health risks. Sound waste management is thus non-negotiable.

- No on-site burying or dumping of any waste materials, vegetation, litter or refuse may be allowed
- Organic waste can be disposed of, buried on-site or used as mulch
- Domestic waste must be stored in approved containers (e.g. bins with removable lids)
- All solid waste will be disposed of at a landfill licensed in terms of section 20 of the Environment Conservation Act (Act No. 73 of 1989)
- No material should be disposed into any riparian zone, including organic waste
- All possible pollution sources must be identified and all reasonable steps taken to prevent pollution or accidental spillages
- Ensure that all concentrated potential sources of pollution are protected (bunded) in order to minimise the risk of accidental spillage or pollution. Storage tanks should be bunded in such a way to contain at least 120% of the storage tank's capacity

4.6 MINIMISE DUST AND EMISSIONS

Refer to erosion and sedimentation control paragraph 4.4.

4.7 MANAGEMENT OF NATURAL AREAS

The objective regarding the management of natural areas is to identify critical or conservation worthy features and to manage such areas and gardens in such a manner as to promote biodiversity and ecological processes.

- Natural areas must be managed as close to natural as possible (no interference wherever possible)
- Alien vegetation should be removed from the remaining natural areas and disturbed areas that are within or adjacent to any riparian zone and the areas should be kept clear of alien vegetation. This should be implemented as soon as possible, and the alien vegetation removal programme be in place permanently to address any new growth which may occur. The landowner is responsible for the implementation of the alien vegetation removal and control on the site and the property
- All listed invasive alien vegetation must be removed in accordance with CARA legislation (The Conservation of Agricultural Resources Act, 1983 (Act No. 43 of 1983)) as revised

4.8 EMERGENCY PREPAREDNESS AND RESPONSE

The following potential emergency situations have been identified and include the procedure for responding to, and for preventing and mitigating the environmental impacts that may be associated with them.

4.8.1 ACCIDENTAL FIRES

The following measures must be implemented:

- Adequate firefighting equipment must be available at an area where works or maintenance is taking place and in good working order (including at least one type of ABC (all purpose) minimum 4.5 kg fire extinguisher and 3 fire beaters per working area). The persons on site must be trained in the use of such equipment
- The owner must provide a list of all authorities involved in firefighting in the region, including neighbouring landowners. This list must include emergency contact numbers and must be visible at the office
- The owner must establish an emergency procedure (with contact numbers)
- Accidental fires are to be dealt with in terms of the local fire protection association or local regulations

4.9 CHEMICAL MANAGEMENT

Proper chemical management is required to minimize or eliminate the risk of environmental damage, as well as the risk of fatalities, illnesses, injuries and incidents arising from the storage, handling, transport and disposal of hazardous material.

- Compliance with the Occupational Health and Safety Act of 1983
- An emergency plan must be made to comply with section 30 (Control of emergency incidents) of the National Environmental Management Act (NEMA), No. 107 of 1997
- In case of a spill or leak of product, such incident must be reported to all relevant authorities and the Directorate: Pollution Management in accordance with Section 30 (10) of NEMA, No. 107 of 1997
- All staff on the site must be well trained and have the appropriate PPE in all aspects of the Occupational Health and Safety procedures pertaining to activities of the solar PV facility
- Access to chemical storage areas must be strictly restricted authorised personnel

- Material Safety Data Sheets (MSDSs) shall be readily available on site for all chemicals and hazardous substances to be used on site. Where possible the available, MSDSs must additionally include information on ecological impacts and measures to minimise negative environmental impacts during accidental releases or escapes
- A system shall be in place to ensure that MSDS are available to all personnel (including first-aiders and medical personnel) involved in the transportation, storage, handling, use and disposal of hazardous materials on site
- Labelling shall be in place on all storage vessels, containers and tanks, where significant risks exist (based on a risk assessment). Labelling shall clearly identify the stored material
- Personnel using and handling chemicals shall have received proper training for this purpose, using information available from the MSDS
- For each site establishment, yard or other temporary chemicals storage area, a map indicating the potential sources of pollution and corresponding location of spill kits will be prepared. Spill kits will be placed at sufficient proximity in accordance with the degree of risk for spillage, and a responsible person designated for each
- Emergency response equipment for spillage containment, fires, explosions, burns, first aid, etc. must be made available
- Visible safety signs must be placed in areas of potential hazard, e.g. where tap water is not to be used for drinking purposes, indicating the dangers of chlorine or informing of the safety equipment to be worn when entering a certain area, etc.

4.10 BATTERY ENERGY STORAGE SYSTEM (BESS) MANAGEMENT

Prevent contamination of soil or water resources through spills, leaks etc. from the BESS:

- The battery storage system must be designed by professionals and installation must comply with all norms and standards
- Batteries that have reached the end of their life-cycle are to be appropriately removed, preventing any spills or contamination, and are to be appropriately transported to a licenced recycling facility or hazardous waste disposal site
- Any hazardous materials should be stored in an appropriate manner to prevent contamination of the site
- A Material Safety Data Sheet, supplier user guidelines and safety specifications for the battery must be readily available on site
- Operate, maintain and monitor the BESS as per the supplier specifications
- Method statements for battery cell, electrolyte and battery cell / container replacement to be compiled. These should be approved by the technical manager and SHEQ manager
- Maintain strict access control to the battery storage area
- Sufficient and appropriate signage, specifying the types of batteries being used and the risk of exposure to hazardous material and electric shock, to be provided
- Undertake regular visual inspections of the batteries and electrical equipment to identify any defects, damage or leaks
- Any accidental spills (chemicals, fuel, oil etc) that occur must be cleaned up in an appropriate manner. Contaminated soil, material etc. will need to be appropriately disposed of at a licenced facility
- The fire suppression system must also be checked on a regular basis

4.11 SOLAR PANEL ARRAY AND ASSOCIATED INFRASTRUCTURE MANAGEMENT

The following must be implemented during the operations and maintenance of the solar panels and associated electrical infrastructure:

- Maintain strict access control to the solar panel array area
- Sufficient and appropriate signage indicating the risk of exposure to electric shock to be provided
- Undertake regular ground inspections of the solar array and electrical equipment to identify any defects or damage
- Should panels be required to be replaced, materials and panels are to be stored within an approved laydown area. No disturbance of areas outside of these areas should occur
- Areas under solar panel array should be regularly mowed, brush cut or cleared of excessive grass and/or vegetation growth to minimise the risk of fires
- Full clean-up of all materials must be undertaken after the removal and replacement of the solar panel arrays and associated infrastructure is complete, and disturbed areas appropriately rehabilitated
- All material that can be reused or recycled must be recovered, and transported off-site to an appropriate facility
- No waste materials may be left on-site
- Waste material which cannot be recycled shall be disposed of at an appropriately licensed waste disposal site or as required by the relevant legislation
- Cognisance of water usage and water run-off during the washing of panels must be taken. Where possible, water-less cleaning methods should be considered. If not, the use of rain captured water or other responsibly sourced water should be considered

5. ENVIRONMENTAL AUDIT PROGRAMME

A Final Construction Phase Audit Report is to be undertaken 6 months post construction. This must be undertaken by a qualified Independent Environmental Auditor and is to be submitted to the Competent Authority.

Since the development includes an operational phase, annual audits for the initial two years are recommended.

In terms of the 2014 EIA Regulations, Audit Reports must be submitted to the registered Interested & Affected Parties within 7 days of submission to the competent authority.

6. DECOMMISSIONING PHASE

The facility is expected to have a lifespan of 20+ years (i.e. with routine maintenance). The facility infrastructure would only be decommissioned and rehabilitated if it becomes outdated or inadequate, in which case the facility will normally be upgraded and not decommissioned.

It is thus considered unlikely that the facility will be decommissioned. However, it is likely that the facility may be upgraded or enlarged as part of maintenance and replacement of individual components with more appropriate technology/infrastructure available at that time.

In the event that decommissioning of the site occurs after approximately 20 years, **the mitigation measures outlined in the Construction Phase (Section 3) should be applied during the decommissioning process.** Therefore, these measures are not repeated here, except for the following general principles:

- Site preparation activities will include confirming the integrity of the access to the site to accommodate required equipment, preparation of the site (e.g. lay down areas, construction platform) and the mobilisation of construction equipment
- Disassembled components will be reused, recycled, or disposed of in accordance with best practise or any relevant legislation at the time
- Specific consideration must be given to ways to minimise waste and wastage in maintenance and the decommissioning phase of the proposed development. Where waste cannot be recycled or re-used, it must be disposed of at an appropriate licenced/registered facility or landfill. Records of disposal must be kept
- Equipment used in the plant must be recycled and re-used where possible to avoid the filling of already limited landfill space
- As far as possible, local labour must be used for the disassembly and sorting of components for recycling.
- Batteries must be re-used, recycled or disposed of at a licenced facility. A Method Statement must be compiled for the safe decommissioning of the battery storage, and which will consider the appointment of accredited battery recyclers.
- A final public road integrity inspection in conjunction with the provincial traffic authority must take place to ensure that roads which serviced the facility are not left in a degraded state
- All areas impacted areas must be appropriately rehabilitated. Re-vegetation of exposed soil surfaces must be undertaken to ensure no erosion in these areas

7. IMPACT MANAGEMENT OUTCOMES

Impact Management Outcomes

Planning, Design and Pre-Construction					
Impact	Management Outcomes	Management Actions	Responsible Person/Party	Implementation Monitoring Method	Monitoring Frequency
Demarcation of work areas	Prevent impacts on “no-go areas”, including undisturbed areas, drainage lines and/or natural vegetation	<ul style="list-style-type: none"> The site will be demarcated with appropriate dropper poles. Alternative fencing may be decided upon dependent on site requirements). Other demarcation measures can be used if approved by the ECO Work areas and access routes must be clearly demarcated to minimise environmental impact 	Contractor	Method Statement	Once-off
Demarcation of no-go areas	Prevent impacts on sensitive features on site, seasonal streams and natural vegetation on or adjacent to the site	<ul style="list-style-type: none"> No-Go areas will be demarcated and indicated on a site plan Natural vegetation outside of the development area will be considered no-go areas, unless for the purpose of alien vegetation clearing 	Contractor	Method Statement	Once-off
Site camp establishment and access roads	Prevent unnecessary impacts on natural vegetation through the establishment and operations of the site camp and access roads.	<ul style="list-style-type: none"> The site camp, lay down areas, and access roads must be clearly defined on a plan, taking no-go areas into consideration, as well as proximity to water resources 	Contractor	Method Statement	Once-off
Fuel Storage (if required)	Prevention of fuel spillages and contamination of the soil and/or water resources	<ul style="list-style-type: none"> The fuel tank must be placed within a <u>completely sealed concrete bund</u> All fuel oil containers must be placed within suitable drip trays to prevent accidental spillage of oils and fuels 	Contractor	Method Statement	Once-off

		<ul style="list-style-type: none"> • A suitable leak proof container for the storage of oiled equipment (filters, drip tray contents and oil changes etc.) must be established • Fuel storage areas must be at least 100m from any watercourses 			
Mandatory site equipment	Ensure the correct equipment is on site to meet environmental requirements as per the EMP	<ul style="list-style-type: none"> • Adequate firefighting equipment must be available on site and in good working order (including at least one type ABC (all purpose) minimum 4.5 kg fire extinguisher and 3 fire beaters per working area • Drip trays to be used during refuelling or storage of small quantities of fuel on site • Adequate toilet and ablution facilities must be provided on site. Toilets should be placed at least 50m from any watercourses. Toilets are to be serviced and cleaned on a regular basis • Adequate waste bins to be provided on site 	Contractor	Method Statement	Once-off
Waste Management	To prevent and minimise waste generation and contamination of the site and surrounding areas	<ul style="list-style-type: none"> • No littering or on-site burying or dumping of any waste materials, vegetation, litter or refuse may occur • All solid waste, except for the organic waste from the removed vineyards and natural vegetation, must be disposed of offsite at an approved landfill site in terms of section 20 of the Environment Conservation Act (Act No. 73 of 1989). The Contractor must supply the ECO with a certificate of disposal • The Contractor must provide problem animal- and weatherproof bins with lids of sufficient number and capacity to store the solid waste produced on a daily basis. The lids must be kept firmly on the bins at all times. Bins must not be allowed to become overfull and must be emptied regularly 	Contractor	Method Statement	Once-off

<p>Fire Management</p>	<p>Prevent unnecessary fires which may cause damage and risk to the environment, property and human health, and adequately deal with any fires that may occur on site</p>	<ul style="list-style-type: none"> • Adequate firefighting equipment according to the fire hazard during the construction period must be available on site and in good working order (at least one type ABC (all purpose) minimum 4.5kg extinguisher and 3 fire beaters per working area). The persons on site must be trained in the use of such equipment • The main contractor must provide a list of all authorities involved in firefighting in the region. This list must include emergency contact numbers and must be visible at the site office 	<p>Contractor</p>	<p>Method Statement</p>	<p>Once-off</p>
------------------------	---	--	-------------------	-------------------------	-----------------

Construction					
Impact	Management Outcomes	Management Actions	Responsible Person/Party	Implementation Monitoring Method	Monitoring Frequency
Topsoil removal	Topsoil to be removed (if necessary), protected and stockpiled for rehabilitation after construction	<ul style="list-style-type: none"> • Prior to any activities within the demarcated work areas, topsoil material shall be removed to a depth of 300mm or deeper if specified by the engineer in consultation with the ECO, and stockpiled in a designated area for use in rehabilitation of the site post construction • Topsoil from the still relatively natural area (the top 15 -20 cm) should be removed and be used for rehabilitation after construction on site or in the immediate vicinity of the site 	Contractor	Method Statement	Once-off
Stockpile Management	Avoid impacts on natural areas and watercourses from stockpiling of material, waste etc.	<ul style="list-style-type: none"> • Topsoil stockpiles to be separated from waste, building material etc. stockpiles. • Stockpile areas to be demarcated prior to construction 	Contractor	Method Statement	Once-off
Erosion Management	Prevent erosion as a result of construction activities on site	<ul style="list-style-type: none"> • Install erosion and sediment controls before work starts and maintain these features throughout the construction and operational phases • Leave as much vegetation as possible. • Implement the Stormwater Management Plan. Adherence to the EMP & Implementation of Standard Management Procedures in terms of erosion and sedimentation. 	Contractor	Method Statement	Continually during construction
Cement mixing	Prevent contamination from cement mixing and cement waste water on the natural environment, particularly water	<ul style="list-style-type: none"> • Concrete and cement may only be mixed on existing hard surfaced areas, or edged mortar boards or a suitable container • The visible remains of the batch and concrete, either solid, or from washings, must be 	Contractor	Method Statement	Continually during construction

	<p>resources. Due to the high alkaline pH of cement, it is highly hazardous to the natural environment</p>	<p>physically removed immediately and disposed of as hazardous waste</p> <ul style="list-style-type: none"> • Washing of equipment shall be done in a container to prevent any runoff of contaminated washing water • Extreme care must be taken to limit the amount of water contaminated by washing equipment. Water from concrete washing can be re-used in concrete mixes or must be stored in drums, then removed from the site and disposed of at a licensed municipal dump site. • Concrete batching facilities must have suitable bunding methods in place to ensure minimal waste water run-off occurs during batching operations • Cleaning of equipment and flushing of mixers must not result in pollution of the surrounding environment. All wastewater resulting from batching of concrete must be disposed of via the contaminated water management procedure. 			
<p>Dust Control</p>	<p>Prevent and minimise dust generation on site which can become a nuisance to neighbouring landowners and residents, as well as being a health risk</p>	<ul style="list-style-type: none"> • The Contractor must take all reasonable measures to minimize the generation of dust as a result of construction activities resulting from along-construction-route activities (but must also take into account possible water constrictions of the area) • The onsite construction site agent must take into account prevailing wind strength and wind direction and must have preventative measures on standby to minimize dust pollution that may cause damage to people and property • The liberation of dust into the surrounding environment shall be effectively controlled by the use of, inter alia, water spraying and/or 	<p>Contractor</p>	<p>Method Statement</p>	<p>Continually during construction</p>

		other dust-allaying agents. The speed of haul trucks and other vehicles must be strictly controlled to avoid dangerous conditions, excessive dust or excessive deterioration of the road being used.			
--	--	--	--	--	--

Rehabilitation					
Impact	Management Outcomes	Management Actions	Responsible Person/Party	Monitoring Method	Monitoring Frequency
Rehabilitation of the Construction site	Rehabilitation of areas impacted by construction activities	<ul style="list-style-type: none"> • All structures, equipment, materials and facilities used or created on site for or during construction activities are removed once the project has been completed. On completion of the project or phase, all areas impacted by the construction activities must be reinstated and/or rehabilitated to the satisfaction of the ECO • Immediately after the demolition of the camp site or once construction has been completed, the contractor shall restore the site to its original state, paying particular attention to its appearance relative to the general landscape. This must be done as soon as possible after construction has ended to ensure no possible environmental degradation of the site as a result of erosion, alien vegetation establishment etc. • The contractor's procedure for rehabilitation shall be approved by the ECO and Engineer. • Site offices must be removed and the areas rehabilitated or reinstated to the satisfaction of the ECO • Earthworks to reinstate the physical characteristics of the site. Here attention to the natural vertical and lateral heterogeneity in landform shall guide the reinstatement of natural areas • Replacement of topsoil material – care shall be taken to ensure that the same material that was removed from each area is replaced there, since this will carry the seed complement 	Contractor	Method Statement	Once-off

		appropriate for re-establishment of each plant community type • Final landscaping by machine, but landscaping by hand may be required in many areas under rehabilitation			
--	--	---	--	--	--

Operation					
Impact	Management Outcomes	Management Actions	Responsible Person/Party	Monitoring Method	Monitoring Frequency
Erosion Management	Avoid valuable topsoil removal	<ul style="list-style-type: none"> Inspect and maintain erosion and sediment controls on a regular basis and ensure that it can accommodate the upslope catchment Leave as much vegetation as possible Install permanent fences to define 'no go' areas in those areas that are not to be disturbed If required, install sediment catchment controls down slope of the site to catch sediment (if applicable). This must be done as soon as possible by the Applicant and should be permanent Avoid driving off road, or off the road surface, to avoid puddles or obstacles. During the operational phase of these gravel roads, prone to erosion exacerbated by heavy rainfall, running water must be deviated from the roads with appropriate storm water management infrastructure. Next to the road shoulders, paved swales will probably be necessary to prevent running storm water to erode deep trenches 	Owner	Visual monitoring	Weekly/after major rain events
Waste and Pollution Management	Avoid contamination of soil and water resources with pollutants.	<ul style="list-style-type: none"> No on-site burying or dumping of any waste materials, vegetation, litter or refuse may be allowed Organic waste can be disposed of, buried on-site or used as mulch Domestic waste must be stored in approved containers (e.g. bins with removable lids). All solid waste will be disposed of at a landfill licensed in terms of section 20 of the 	Owner	Visual monitoring	Daily - Weekly

		<p>Environment Conservation Act (Act No. 73 of 1989)</p> <ul style="list-style-type: none"> • No material should be disposed into any riparian zone, including organic waste. • All possible pollution sources must be identified and all reasonable steps taken to prevent pollution or accidental spillages • Septic tanks are to be checked and serviced on a regular basis • Properly maintain the sewerage system 			
Emergency Preparedness - Fire	Prevent unnecessary fires which may cause damage and risk to the environment, property and human health, and adequately deal with any fires that may occur on site	<ul style="list-style-type: none"> • Adequate firefighting equipment must be available on site and in good working order (including at least one type ABC (all purpose) minimum 4.5 kg fire extinguisher and 3 fire beaters per working area). The persons on site must be trained in the use of such equipment • The owner must provide a list of all authorities involved in firefighting in the region, including neighbouring landowners. This list must include emergency contact numbers and must be visible at the office • The owner must establish an emergency procedure (with contact numbers) • The project facility must register with the local Fire Fighters Organisation and periodically conduct drills in conjunction with the local fire fighters unit. Fire management and Protection plan should be developed to implement measures that minimise the potential for human cause fires 	Owner	Visual monitoring	Daily- weekly / when required
Battery Energy Storage Systems (BESS)	Prevent contamination of soil or water resources through spills, leaks etc. from the BESS	<ul style="list-style-type: none"> • The battery storage system must be designed by professionals and installation must comply with all norms and standards. • Batteries that have reached the end of their life-cycle are to be appropriately removed, 	Owner	Visual monitoring	Daily - weekly

		<p>preventing any spills or contamination, and are to be appropriately transported to a licenced recycling facility or hazardous waste disposal site.</p> <ul style="list-style-type: none"> • Any hazardous materials should be stored in an appropriate manner to prevent contamination of the site. • Any accidental spills (chemicals, fuel, oil etc) that occur must be cleaned up in an appropriate manner. Contaminated soil, material etc. will need to be appropriately disposed of at a licenced facility. 			
Management of Natural Areas	Prevent impacts on, and loss of, adjacent natural vegetation	<ul style="list-style-type: none"> • Natural areas must be managed as close to natural as possible (no interference wherever possible) • Alien vegetation should be removed from the remaining natural areas and disturbed areas that are within or adjacent to any riparian zone and the areas should be kept clear of alien vegetation. This should be implemented as soon as possible, and the alien vegetation removal programme be in place permanently to address any new growth which may occur. Landowner is responsible for the implementation of the alien vegetation removal and control on the site and the property • All listed invasive alien vegetation must be removed in accordance with CARA legislation (The Conservation of Agricultural Resources Act, 1983 (Act No. 43 of 1983)) as revised 	Owner	Visual monitoring	Weekly

APPENDIX 1: DECLARATION OF UNDERSTANDING

ELECTRIC VEHICLE CHARGING STATION AND SOLAR PV FACILITY

DECLARATION OF UNDERSTANDING

I _____

Representing: _____

Declare that the conditions of the EMP were brought to my attention and that I have read and understood the contents of this Environmental Management Plan as prepared by EnviroAfrica, of which a copy has been made available to me.

Site: _____

Date: _____

I also declare that I understand my responsibility in terms of enforcing and implementing the Environmental Specifications as set out in this Environmental Management Programme.

I also undertake to inform all persons under my supervision of these specifications and the contents of the Environmental Management Programme.

Signed: _____

Place: _____

Date: _____

Witness 1: _____

APPENDIX 2: ENVIRONMENTAL AUTHORISATION

To be included on approval (before construction begins).

APPENDIX 3: Maps & Drawings

APPENDIX 4: START-UP REPORT

To be included after start-up meeting.

APPENDIX 5: PENALTIES FOR NON-COMPLIANCE

PENALTIES FOR NON-COMPLIANCE

The contractors / sub-contractors must contact the ECO at any stage if unsure about any matter, or if a pollution incident occurs, or vegetation or animals are damaged.

ECO = Environmental Control Officer ESO= Environmental Site Officer

PHASE	Penalty for Non-compliance	
	Bottom range	Top Range*
PRE-CONSTRUCTION PHASE		
Construction area to be marked off before construction starts.		5000
The demarcated area must be maintained throughout the construction phase	500	1000
Site area for stock piling of building material must be demarcated	500	5000
Site area for storing of waste material must be demarcated	500	5000
Fencing off the construction site with mesh fencing of 1.8m, where necessary or other suitable material as agreed on by ECO	500	1000
Sitting of access road/s to be approved by ECO & demarcated with stakes before any construction starts (if applicable)		5000
Temporary route used for construction must be determined on site with ECO (if applicable)	1000	5000
Telecommunications & AC power routes must be determined with the ECO (if applicable)	1000	5000
Sensitive features that may be harmed must be clearly marked or demarcated.	500	2000
Vegetation that may not be removed must be clearly marked or demarcated.	500	5000
Contractor must make the Construction team and all sub-contractors aware of all environmental aspects that could lead to imposition of penalties	100	5000
Contractor to sign Declaration of understanding (DOU) before construction starts		5000
Contractor to assure that all subcontractors be informed and signed DOU	1000	5000
Method statements must be provided on request by the ECO. No work may commence until the Method Statement is accepted by the ECO and Engineer	1000	5000
CONSTRUCTION PHASE		
Information		
A copy of the EMP & Record of Decision with all the conditions of approval, and the relevant Method Statements must be at site at all times.	200	5000
Construction crew behaviour		

Construction crews may not overnight on site.	200	5000
No amplified music allowed on site	100	200
Construction crew must stay within the demarcated construction area. (Applicable in sensitive sites)	50	500
Eating of meals only allowed in demarcated area	50	500
No pets permitted on site		100
Driving, Parking & Storing of machinery and vehicles are only allowed inside demarcated areas and existing roads	1000	5000
Machinery may only be used on the road and may not disturb the vegetation on the sides of the road except if cleared by ECO. Machinery used must be carefully considered to limit environmental damage	500	5000
No vegetation other than that agreed on may be damaged - i.e. no access to areas outside construction area.	500	2000
No individual may cause unnecessary damage to flora and fauna on, around or near the site	20	2000
No littering allowed (incl. cigarette butts)	50	500
Excavations		
No topsoil may be removed or altered outside the demarcated area and/or which was not specified.		2000
Commercial sources of sand, rock and gravel to be cleared with ECO	200	5000
All surplus material to be taken off-site and be disposed of at approved site	500	5000
Toilets		
Sufficient ablution facilities must be provided		3000
Toilets to be secured to prevent them from falling or blowing over.	100	1000
They must be serviced regularly, (according to the manufacturer's instructions) and kept clean.	100	1000
Everybody on site must make use of ablution facilities	50	1000
Fire Prevention		
All mandatory firefighting equipment (s specified at start-up) must be on site at all times	500	4000
Firefighting equipment to be in good working order and serviced.	500	2000
No fires, including cooking fires, allowed on site	1000	5000
Cement		

Concrete may only be mixed within the boundaries of the demarcated area and/or where was agreed on by the ECO.	500	5000
All excess cement & concrete mixes to be contained on construction site prior to disposal off site	200	5000
Any cement / concrete spillage to be cleaned up immediately.	500	5000
Ready-mix delivery trucks must not carry out the wash down of their trucks on or around the site unless arranged with ECO.	1000	3000
Dust pollution control		
Ensure that loose building material is covered to prevent dust pollution	100	1000
Water run-off		
Contamination of water bodies, rivers, dams or wetlands must be prevented at all cost	500	5000
Rainwater from construction & building site/s must be channelled, contained & allowed to dry out, so as not to transport any pollutants into the surrounding area. Temporary trenches, straw stabilising, brush cutting can be used	500	5000
Waste control		
Sufficient refuse bins must be placed on site	500	2000
Refuse bins must be cleaned on a regular basis	100	1000
General litter / building refuse must be cleaned up on a regular basis from the site	500	3000
Cement-contaminated water; paint; oil; cement slurries etc must be stored in watertight containers or as agreed with ECO	500	5000
Store all refuse & waste material in wind & animal proof containers	100	1000
Waste must be disposed of at an official waste deposit site on a regular basis.	500	5000
The absence of or inadequate drip trays or bunding facilities	500	5000
Failure to address oil/fuel leaks from on-site machinery	200	5000
Herbicides		
No herbicides or pesticides whatsoever may be used.	200	2000
Construction road		
Road must be upgraded to prevent degradation and erosion of the road and surrounds.	500	5000
Power and Telecommunications supply		
Demarcate power supply route	500	5000

No vehicles to drive through vegetation unless authorised by ECO	500	5000
Storage of equipment may only take place at an area demarcated by the ECO.	500	5000
Working must be done in phases to prevent trampling of vegetation	N/A	
Use of generators and fuel powered equipment		
A watertight cover must be place under the power generator equipment to prevent accidental spillage of fuel & oil seeping into the soil.	500	5000
Drip tray must be able to take 120% of fuel on site	500	5000
All waste material generated from the use of this equipment must be contained and removed from the site	500	5000
Mobile fuel powered equipment must be well maintained and must not have any fuel or oil leaks.	200	5000
Soil Stabilisation		
Ensure that soil material for filling and stabilisation comes from a source that does not contain seeds alien to the area. The source must be cleared with the ECO.	100	2000
Rehabilitation		
Remove rocks and stones and stock pile in area recommended by ECO	500	5000
Remove all plants that can be used for rehabilitation and store on- or off-site in appropriate manner as agreed with ECO	200	5000
Removal of all old concrete and alien materials from site	500	5000
Site must be cleared of all waste and building material	500	5000

*(Large scale / repeated offence)

APPENDIX 6: INFO ON METHOD STATEMENTS

INFORMATION ON METHOD STATEMENT

Method Statements are to be completed by the person undertaking the work (i.e. the Contractor). The Method Statement will enable the potential negative environmental impacts associated with the proposed activity to be assessed.

The Method Statement can only be implemented once approved by the ECO

The Contractor (and, where relevant, any sub-contractors) must also sign the Method Statement, thereby indicating that the works will be carried out according to the methodology contained in the approved Method Statement.

The ECO will use the Method Statement to audit compliance by the Contractor with the requirements of the approved Method Statement.

Changes to the way the works are to be carried out must be reflected by amendments to the original approved Method Statement; amendments require the signature of the ECO denoting that the changed methodology or works are necessary for the successful completion of the works, and are environmentally acceptable. The Contractor will also be required to sign the amended Method Statement thereby committing him/herself to the amended Method Statement.

This Method Statement **MUST** contain sufficient information and detail to enable the ECO to apply their minds to the potential impacts of the works on the environment. The Contractor will also need to thoroughly understand what is required of him/her in order to undertake the works.

THE TIME TAKEN TO PROVIDE A THOROUGH, DETAILED METHOD STATEMENT IS TIME WELL SPENT. INSUFFICIENT DETAIL WILL RESULT IN DELAYS TO THE WORKS WHILE THE METHOD STATEMENT IS REWRITTEN TO THE ER'S AND ESO'S SATISFACTION.

The page overleaf provides a *pro forma* method statement sheet, which needs to be completed for each activity requiring a method statement in terms of the EMP.

APPENDIX 7: EXAMPLE OF METHOD STATEMENT

PRO-FORMA METHOD STATEMENT

CONTRACT:..... **DATE:**.....

PROPOSED ACTIVITY (give title of method statement and reference number):

WHAT WORK IS TO BE UNDERTAKEN (give a brief description of the works):

WHERE ARE THE WORKS TO BE UNDERTAKEN (where possible, provide an annotated plan and a full description of the extent of the works):

START AND END DATE OF THE WORKS FOR WHICH THE METHOD STATEMENT IS REQUIRED:

Start Date:

End Date:

HOW ARE THE WORKS TO BE UNDERTAKEN (provide as much detail as possible, including annotated maps and plans where possible):

Note: please attach extra pages if more space is required

DECLARATIONS

1) ENVIRONMENTAL CONSULTANT AND/OR ENVIRONMENTAL CONTROL OFFICER

The work described in this Method Statement, if carried out according to the methodology described, is satisfactorily mitigated to prevent avoidable environmental harm:

(Signed) (Print name)

(Signed) (Print name)

Dated: _____

2) PERSON UNDERTAKING THE WORKS

I understand the contents of this Method Statement and the scope of the works required of me. I further understand that this Method Statement may be amended on application to other signatories and that the ESO will audit my compliance with the contents of this Method Statement

(Signed) (Print name)

Dated: _____

3) THE APPLICANT

The works described in this Method Statement are approved.

(Signed) (Print name) (Designation)

Dated: _____

METHOD STATEMENT REGISTER		Principle Site Agent:			Project Name:		
		Main Contractor:			Project location:		
No.	METHOD STATEMENT ACTIVITY REFERENCE	DATE CREATED	DATE RECEIVED	CREATED BY	ACCEPTED / REJECTED	DATE approved	Approved By
1	Demarcation						
2	Clearing of vegetation and topsoil removal						
3	Stockpiling						
4	Temporary storage facilities						
5	Construction camp and site offices						
6	Fuel storage						
7	Labourer's facilities						
8	Entrance and haul roads						
9	Mandatory site equipment						
10	Waste management/control						
11	Cement mixing and batching areas						
12	Construction vehicle maintenance						
13	Dust control						
14	Erosion control						
15	Noise control						
16	Archaeological and heritage finds						
17	Rehabilitation						
18							
19	<u>Additional MS (Waste Licence requirements)</u>						
20							
21							
22							

APPENDIX 8: CONTACTOR ENVIRONMENTAL CHECKLIST

CONTACTOR/S REPRESENTATIVE: ENVIRONMENTAL WEEKLY CHECKLIST

SITE: _____

PHASE OF WORK AND % OF COMPLETION: _____

ENVIRONMENTAL ASPECT	YES/ NO (✓ or X)	COMMENTS
How many workers are on site		
All new personnel on site are aware of the contents of the EMP and have been through the environmental awareness course.		
Contractor's camp is neat and tidy and the labourers' facilities are of an acceptable standard.		
Sufficient and appropriate fire fighting equipment is visible and readily available.		
Waste control and removal system is being maintained.		
Refuse bins in place and maintained		
Toilets are in place and clean		
Demarcation and other fences are being maintained.		
What machinery are on site		
Drip trays are being utilised where there is a risk of incidental spillage		
Bunds/ drip trays are being emptied on a regular basis (especially after rain).		
No leakages (oil & fuel) are visible from construction vehicles		
No go areas, remaining natural features and trees have not been damaged.		
Dust control measures (if necessary) are in place and are effectively controlling dust.		
Noise Control measures (if necessary) is in place and is working effectively.		
Erosion control measures (if necessary) are in place and are effective in controlling erosion. (Access road, site areas etc.)		
Stockpiles are located within the boundary of the site, do not exceed 2 m in height and are protected from erosion.		

Completed by:..... Sign:..... Date:.....

To be submitted at the end of each week to the Environmental Site Officer (ESO)

Received by:

Environmental Site Officer: :..... Sign:

Date:.....

APPENDIX 9: BASIC RULES OF CONDUCT

BASIC RULES OF CONDUCT

The following list represents the basic Do's and Don'ts towards environmental awareness, which all participants in this project must consider whilst carrying out their tasks. These are not exhaustive and serve as a quick reference aid.

NOTE: ALL new site personnel must attend an environmental awareness presentation. Please inform your foreman or manager if you have not attended such a presentation or contact the ESO.

DO:

- Use the toilet facilities provided – report dirty or full facilities
- Clear your work areas of litter and building rubbish at the end of each day – use the waste bins provided and ensure that litter will not blow away.
- Report all fuel or oil spills immediately & stop the spill continuing.
- Dispose of cigarettes and matches carefully. (Littering is an offence.)
- Confine work and storage of equipment to within the immediate work area.
- Use all safety equipment and comply with all safety procedures.
- Prevent contamination or pollution of streams and water channels.
- Ensure a working fire extinguisher is immediately at hand if any “hot work” is undertaken e.g. welding, grinding, gas cutting etc.
- Report any injury of an animal.
- Drive on designated routes only.
- Prevent excessive dust and noise.

Do not:

- Remove or damage vegetation without direct instruction.
- Make any fires.
- Injure, trap, feed or harm any animals – this includes birds, frogs, snakes, lizards etc.
- Enter any fenced off or marked area.
- Allow cement or cement bags to blow around.
- Speed or drive recklessly
- Allow waste, litter, oils or foreign materials into the stream
- Swim in the dam.
- Litter or leave food laying around

Notes:

If any animals such as tortoises, chameleons or snakes be encountered then do not harm them. The ECO or Site Supervisor must be contacted to remove these safely. The harming of any animal will result in disciplinary action.

Construction and heavy machine operators must be particularly sensitive to staying within access routes and prevention of unnecessary damage. Dust and noise is also of particular concern. Ensure that vehicles and machinery do not leak fuel or oils. Refuelling or maintenance must be done within the maintenance camp area only.

Alien plant clearing and control work teams must be closely supervised.

BASIESE GEDRAGSKODES

Die volgende lys vertenwoordig die moets en moenies vir omgewingsbewustheid wat alle deelnemers aan hierdie projek in ag moet neem tydens die uitvoer van hul take. Hierdie lys is nie volledig nie en dien slegs as 'n vinnige verwysing.

Nota: alle nuwe terreinpersoneel moet 'n aanbieding ten opsigte van omgewingsbewustheid bywoon. Indien u nog nie so 'n aanbieding bygewoon het nie, lig asseblief u voorman of bestuurder in of kontak die omgewings terreinbeampte.

Moets:

- Gebruik die beskikbare toilet-geriewe – rapporteer vuil of vol geriewe.
- Maak u werkplek skoon van rommel of bourommel aan die einde van elke dag – gebruik beskikbare vullisdromme en verseker dat rommel nie rondwaai nie.
- Rapporteer alle brandstof- en olie stortings onmiddellik – stop verdere storting.
- Wees versigtig met die wegdoen van sigarette en vuurhoutjies. (rommelstrooi is 'n oortreding.)
- Beperk werkaktiwiteite en die stoor van toerusting tot die onmiddellike werkarea.
- Gebruik veiligheidstoerusting en voldoen aan alle veiligheids-maatreëls.
- Voorkom besoedeling van strome en waterbane
- Verseker dat 'n brandblusser in werkende toestand byderhand is wanneer “warm” werk verrig word bv. Sweis, wegslyp, gasny, ens.
- Rapporteer beseerde diere.
- Ry slegs op aangewese roetes.
- Voorkom oormatige stof en geraas.

Moenie:

- Plantegroei verwyder of beskadig sonder direkte instruksie nie.
- Enige vure maak nie.
- Enige diere dood, beseer, vang of voer nie, insluitende voëls, paddas, slange, akkedisse, ens.
- Enige omheinde of afgesperde areas binnetree nie.
- Sement of sementsakke laat rondwaai nie.
- Vinnig of roekeloos bestuur nie.
- Enige rommel, afval, olie or enige vreemde materiaal in strome laat beland nie.
- In die dam swem nie.
- Rommelstrooi of kos laat rondlê nie.

Notas:

Indien enige diere soos skilpaaie, verkleurmannetjies of slange teëgekomp word, moet hulle nie beseer of dood nie. Kontak die otb of ri om hulle veilig te verwyder. Die besering van diere sal lei tot dissiplinêre optrede.

Operateurs van konstruksie- en swaar masjiene moet veral versigtig wees om binne toegangsroetes te bly en om enige onnodige skade te voorkom. Verseker dat voertuie en masjiene nie olie of brandstof lek nie. Brandstofaanvulling en voertuigonderhoud mag slegs binne die onderhoudsarea gedoen word.

Streng toesig moet gehou word oor indringerplantbeheerspanne.

EZIPPHAMBILI EKUNYANZELEKILEYO UKUBA ZENZIWE

Zonke ezi zinto zilandelayo zizinto ekufuneka zenziwe nekufuneka zingenziwanga.

Wonke umntu ofikayo kufuneka afundiswe ngemigaqo kupala. Needa yazisa iforman yakho ikuba awukhange uye kufundiswa.

Izinto emazenziwe

- Sebenzisa izindlu zangasese, yazisa xa kukho umonakalo.
- Zama ukucoca apho ubusebenza khona.
- Sebenzisa imigqomo yenkukuma ungayeki iphaphtieke.
- Yazisa xa ubona ioil echithskalayo okanye ipetrol.
- Cima lozoli cigarette xa ugqibibile ukutshaya
- Zonke izixhobo usebenza zibuyisele apho zihlaka khona xa ucgibile apho zihlala khona xa ugqibile ukuzisebenzisa.
- Zisebenzise izikhuselixa uzinkiwe.
- Sukugalela izinto emlanjeni.
- Masibekho isicima mlilo xa usebenza ngomlilo.
- Yazisa msinyane xa ubone isilwanyana ezonzakeleyo.
- Xauqhuba isithuthi hamba endleleni qha ungafathulinje.
- Naphina zamaungenzi thuli okanye ingxolo xa usebenza.

Emazingenziwa

- Sukususa nesiphina isityalo ungakhange uxelelwe
- Sukwenza mlilo nokuba sekubanda
- Amagqara ukubulala izilwanyana nokuzifida akuvumelekanga
- Sukungena xa kuvaliwe ngaphandle kwe mvume
- Ingxowa zesamente mazincedwe zingahlwa nje
- Sukuqhuba ngesantya esiphakamileyo
- Sukugalele nayiphi into phaya emlanjeni
- Sukuqubha edameni q oqosha yonk inkukuma

APPENDIX 10: ECO/ESO REPORT/CHECKLIST

ECO / ESO SITE VISIT CHECKLIST / REPORT:

PROJECT NAME: DATE

PROJECT & PHASE: LOCATION

ENVIRONMENTAL ASPECT		POINTS
<p>Note: 1 = Poor, 2 = Average, 3 = Good NA = Not Applicable</p>		
<p>DEMARCATIION METHOD STATEMENT Boundaries of “no go” areas, construction sites, offices, temporary storage areas as well as labourer’s facilities must be demarcated (EMP and ECO requirements) and maintained for the length of the construction period.</p>		
<p>NO-GO AREAS/PROTECTION OF FAUNA & FLORA Identified “No-Go Areas“, remaining natural veld and indigenous- or significant trees are protected features and must be demarcated for protection from construction damage (including secondary impact). All areas outside of the demarcated construction sites and access roads to be regarded as NO-GO areas unless otherwise agreed upon with the client and ECO. All flora identified to be rescued must be removed and placed in an area specifically allocated and taken care off until re-used in pre-approved way. Identified areas with significant vegetation must be protected as NO-GO areas.</p>		
<p>CLEARING OF VEGETATION & TOPSOIL REMOVAL METHOD STATEMENT Before any construction or earthworks, topsoil must be stripped (>150mm) and stockpiled for rehabilitation/ landscaping. Stockpiles: must be protected (may not blow or wash away or gets compacted) and stored separately. may not be moved further than 50m or mixed with any other soil. must be convex and should not exceed 2m in height. In addition: Cleared areas must be stabilized. Burning or burying of cleared vegetation is prohibited, but may be used for mulch or slope stabilisation on site.</p>		
<p>STOCKPILING METHOD STATEMENT Top- and subsoil’s from trenches must be located within site boundaries, stabilised and may not exceed 2m in height.</p>		
<p>TEMPORARY STORAGE FACILITIES METHOD STATEMENT Must be demarcated, organised, neat and tidy and of acceptable standards.</p>		
<p>CONSTRUCTION CAMP & SITE OFFICES METHOD STATEMENT Must be demarcated, organised and free of day-to-day litter (maintaining good housekeeping standards).</p>		

ENVIRONMENTAL ASPECT		POINTS
<p>Note: 1 = Poor, 2 = Average, 3 = Good NA = Not Applicable</p>		
<p>FUEL STORAGE METHOD STATEMENT Fuel storage areas must be situated within the demarcated construction camp site (or an area approved by the ECO). Bunds must be built (EMP and ECO requirements) around larger fuel storage areas (accidental spillages). Drip trays must be used (in accordance with EMP) at all fuel and oil storage and refilling sites and must be cleaned regularly, especially after rain.</p>		
<p>LABOURER'S FACILITIES METHOD STATEMENT Facilities must be of acceptable standards suitably demarcated, well maintained, neat and tidy and with adequate ablution facilities.</p>		
<p>ENTRANCE AND HAUL ROADS METHOD STATEMENT Only approved entrance and haul roads may be used (existing roads and infrastructure). No new roads or parking areas may be developed without written approval from the ECO.</p>		
<p>MANDATORY SITE EQUIPMENT METHOD STATEMENT Mandatory site equipment must be in place, well maintained and in accordance with EMP and ECO requirements. Sufficient refuse bins must be on site (well placed and conspicuous) and must be cleaned regularly. Fire extinguishers must be readily available, maintained and functional. Drip trays must be used (in accordance with EMP) at all fuel and oil storage and refilling sites and must be cleaned regularly, especially after rain. Toilets and sanitation facilities must be kept clean neat and hygienic (toilet paper must be available).</p>		
<p>WASTE CONTROL METHOD STATEMENT The contractor is expected to control all construction related waste material and general litter on actual construction sites and its immediate surroundings. Waste management must be in accordance with the EMP, of acceptable standards, with regular removal of general waste, hazardous waste as well as construction waste (e.g. concrete waste and spoil).</p>		
<p>CEMENT MIXING & BATCHING AREAS METHOD STATEMENT Mixing areas must be approved by the ECO, suitably demarcated and may not result in pollution. Polluted cement water may only be released into sedimentation ponds. Sedimentation ponds must be maintained and cleaned regularly (and reinstated after use).</p>		

ENVIRONMENTAL ASPECT	RISKS	
Note: 1 = Poor, 2 = Average, 3 = Good NA = Not Applicable		
CONSTRUCTION VEHICLE MAINTENANCE METHOD STATEMENT Construction vehicles must be in good working order and well maintained to prevent oil and fuel leakages and to reduce noise levels. Maintenance areas must be approved by ECO. Refuelling must be done in accordance with the EMP, using drip trays.		
HEAVY EARTHMOVING EQUIPMENT Construction vehicles and equipment may only operate <u>within</u> the demarcated site boundaries (and approved access roads), especially heavy earthmoving vehicles.		
DUST CONTROL METHOD STATEMENT Adequate control measures must be in place to prevent dust pollution as a result of construction activities (especially with regard to entrance-, haul roads and exposed surfaces). Areas of concern must be watered regularly during construction AND periods of strong winds, BUT must take water saving into account.		
EROSION CONTROL METHOD STATEMENT Erosion resulting from works must be controlled. Temporary and permanent drainage works must be maintained. Erosion damage and damage in drainage courses must be reinstated.		
NOISE CONTROL METHOD STATEMENT Effective noise control measures must be in place and acceptable working hours must be kept (deviations must be approval by the ECO).		
ENVIRONMENTAL CONDUCT Environmental conduct of construction personnel must be acceptable (e.g. no burning or burying of refuse; no littering and no cement bags or other construction waste material lying around).		
ARCHAEOLOGICAL & HERITAGE FINDS METHOD STATEMENT Should any archaeological or heritage remains be exposed during excavations or any activity on site, these must immediately reported to The site agent/engineer, the ECO or SAHRA.		
REHABILITATION METHOD STATEMENT On completion of the project or phase, all areas impacted by the construction activities must be reinstated and/or rehabilitated to the satisfaction of the ECO with emphasis on the following: Site offices must be removed and the areas rehabilitated or reinstated to the satisfaction of the ECO. Labourer's facilities must be removed and the areas rehabilitated or reinstated to the satisfaction of the ECO.		

ENVIRONMENTAL ASPECT		POINTS
Note: 1 = Poor, 2 = Average, 3 = Good NA = Not Applicable		
<p>All construction site areas must be rehabilitated or reinstated to the satisfaction of the ECO.</p> <p>All temporary fencing and demarcation must be removed and the areas reinstated to the satisfaction of the ECO.</p> <p>Temporary storage areas must be rehabilitated or reinstated to the satisfaction of the ECO.</p> <p>All remaining construction material must be removed and the areas rehabilitated or reinstated to the satisfaction of the ECO.</p> <p>Any additional disturbed areas must be rehabilitated or reinstated to the satisfaction of the ECO.</p>		
<p>ADDITIONAL METHOD STATEMENTS</p> <p>Method statements must be submitted and approved before commencement of the works and must be available at the site offices.</p>		
<p>ENVIRONMENTAL CHECKLIST</p> <p>The contractor must ensure that the weekly environmental checklist is completed at the end of each week and it must be available at the site offices.</p>		
<p>SPOT FINES & PENALTIES</p> <p>Spot fines and penalties must be recorded and documented by the ECO (in accordance with the EMP).</p>		
<p>FIXED POINT PHOTOS</p> <p>Photographs must be taken by the ECO, Site Engineer and or Site Manager, prior to, during and immediately after construction as visual reference. These photographs must be stored with other records relating to the EMP.</p>		

ECO:

APPENDIX 11: METHOD STATEMENT REGISTER

APPENDIX 12: ENVIROMENTAL INCIDENT REPORT FORM

METHOD STATEMENT REGISTER		Principle Site Agent:				Project Name:	
		Main Contractor:				Project location:	
No.	METHOD STATEMENT ACTIVITY REFERENCE	DATE CREATED	DATE RECEIVED	CREATED BY	ACCEPTED / REJECTED	DATE approved	Approved By
1	Demarcation						
2	Clearing of vegetation and topsoil removal						
3	Stockpiling						
4	Temporary storage facilities						
5	Construction camp and site offices						
6	Fuel storage						
7	Labourer's facilities						
8	Entrance and haul roads						
9	Mandatory site equipment						
10	Waste management/control						
11	Cement mixing and batching areas						
12	Construction vehicle maintenance						
13	Dust control						
14	Erosion control						
15	Noise control						
16	Archaeological and heritage finds						
17	Rehabilitation						
18							
19	<u>Additional MS (Waste Licence requirements)</u>						
20							
21							
22							

APPENDIX 12: ENVIROMENTAL INCIDENT REPORT FORM

ENVIRONMENTAL INCIDENT REPORT

PROJECT NAME:	_____
PROJECT LOCATION:	_____
SITE AGENT:	_____
DATE OF INCIDENT:	_____ TIME: _____

BRIEF DESCRIPTION AND CAUSE OF INCIDENT:

WHAT IMMEDIATE ACTIONS/CONTROL MEASURES WERE TAKEN:

WHAT CORRECTIVE ACTIONS WERE TAKEN TO ENSURE NO REPEATS OF THE INCIDENT:

ECO/ESO RESPONSE TO INCIDENT AND RECOMMENDATIONS:

IS THIS INCIDENT A: **FIRST OFFENCE** **SECOND OFFENCE** **THIRD OFFENCE**

SIGNATURE OF SITE AGENT: _____	DATE: _____
SIGNATURE OF ECO/ESO: _____	DATE: _____

REMEMBER: TO BE FACTUAL WHEN DESCRIBING THE INCIDENT.

APPENDIX 13: COMPLAINTS REGISTER FORM

